




***State of the Projects that belong to the Agenda Agreed Upon Consensus (Agenda de Implementación Consensuada – AIC - in Spanish)
and the IIRSA Project Portfolio Estado de Avance***

Carlos Tamayo
*Projec Economist VPC/BID
CCT-IIRSA*



- X Meeting of IIRSA National Coordinators
- Montevideo. July 2007

Strategic Objectives 2006-2010



Implementation

- The implementation of the projects that belong to the Agenda Agreed Upon Consensus (Agenda de Implementación Consensuada – AIC - in Spanish) and the IIRSA Portfolio is one of the four cornerstones of the IIRSA Strategic Objectives 2006-2010
- During 2006, the implementation process has received a very important technical and financial support thanks to the new instruments implemented in the Initiative:
 - Information System for Strategic Management (SIGE, in Spanish)
 - New financing mechanisms for studies related to the IIRSA Portfolio
 - IDB (or BID, in Spanish) Integration Fund
 - ADC (or CAF, in Spanish) Infrastructure Fund
 - Funds from FONPLATA

State of the Projects that belong to the Agenda Agreed Upon Consensus (Agenda de Implementación Consensuada – AIC - in Spanish) and the IIRSA Project Portfolio

Information Source:

1. SIGE
2. Financial Organizations that make up the CCT : BID – CAF and FONPLATA
3. GTEs: Central Inter-oceanic, Peru- Brazil –Bolivia and Amazon*

*** Ecuador N/A**

AIC - PROJECT UNDER SATISFACTORY PROGRESS

State: Under Execution. All sections of the works in Road 14 that correspond to the provinces of Corrientes and Entre Ríos are signed and about to be started.

Amount: US\$ 370 M (BID US\$ 200 M)

Completion planned: 2º semester 2010

MERCOSUR-CHILE HUB

AIC 1 -
Road 14

Legend

- Road
- Railway
- Waterway
- Gas Pipeline
- Energy
- Bridge Border
- ◆ Center
- ⚓ Port

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

AIC – PROJECT UNDER SATISFACTORY PROGRESS

State: Under Execution. The works of the project are in different stages: (i) started; (ii) under tender process and; (iii) under the phase related to the completion of the studies. Taking the year 2003 as the starting year, the following progress is observed: approx. 50 % completed and about to be finished by the end of 2007, the remaining 50 % of the work is under execution and tender processes.

Amount: US\$ 176.8 M (BID US\$ 77 M)

Completion planned: 2° semester 2009

MERCOSUR-CHILE HUB

**AIC 2 –
Corridor: Río
Branco-Colonia –
Nueva Palmira**

Road 14

Legend

- Road
- Railway
- Waterway
- Gas Pipeline
- Energy
- Bridge Border
- ◆ Center
- ⚓ Port

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

AIC – PROJECT UNDER SATISFACTORY PROGRESS

State: Under execution : Both countries give priority to the development of the project. Political-institutional measures were agreed upon consensus. Two new agreements have been set on February 26th, 2007, one regarding the construction of the second bridge (public work) and the other regarding the refitting of the existing bridge "Barão de Mauá".

Amount: US\$ 12 M

Completion planned: 2º semester 2009

MERCOSUR-CHILE HUB

Corridor: Río Branco-Colonia -
Nueva Palmira

Road 14

**AIC 3 -
Bridge:
Yaguarón - Río
Branco**

Legend

- Road
- Railway
- Waterway
- Gas Pipeline
- Energy
- Bridge Border
- ◆ Center
- ⚓ Port

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

AIC – PROJECT UNDER SATISFACTORY PROGRESS

State: Under execution. The critical stages are being overcome according to what was planned. Project with requested financing.

Amount: US\$ 1,200 M (BID US\$ 100 M)

Completion planned: March 2010

MERCOSUR-CHILE HUB

**AIC 4 -
Rodovia
Palhoça -
Osório**

Branco

**Corridor: Río Branco-Colonia -
Nueva Palmira**

Legend

- Road
- Railway
- Waterway
- Gas Pipeline
- Energy
- Bridge Border
- ◆ Center
- ⚓ Port

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

AIC – PROJECT WITH SOME RESTRICTIONS

State: Bidding/Concession. Agreement between both countries (Argentina and Chile) to extend the opening of the technical proposals until August 23rd, 2007, and the opening of the economic proposals until October 9th, 2007. Private-sector financing.

Amount : US\$ 251 M

Completion planned: April 2010

MERCOSUR-CHILE HUB

**AIC 5 – Railway:
Los Andes -
Mendoza**

**Corridor: Río Branco-Colonia -
Nueva Palmira**

Rodovia Palhoça - Osório

Road14

**Bridge: Yaguarón - Río
Branco**

Legend

- Road
- Railway
- Waterway
- Gas Pipeline
- Energy
- Bridge Border
- ◆ Center
- ⚓ Port

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

AIC – PROJECT UNDER SATISFACTORY PROGRESS

State: Under execution. Works have been started.
Private-sector financing.

Amount: US\$ 286 M

Completion planned: June 2008

MERCOSUR-CHILE HUB

AIC 6 - Road 60

Railway: Los Andes - Mendoza

Corridor: Río Branco-Colonia -
Nueva Palmira

Rodovia Palhoça - Osório

Road 14

Bridge: Yaguarón - Río
Branco

Legend

- Road
- Railway
- Waterway
- Gas Pipeline
- Energy
- Bridge Border
- ◆ Center
- ⚓ Port

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

AIC – PROJECT UNDER MODERATE PROGRESS

State: Under development. Public financing (25%)
Private financing (75%)

Amount: US\$ 1,000 M

Completion planned: 2º semester 2008

MERCOSUR-CHILE HUB

AIC 7 – Nortease Gas Pipeline

Railway: Los Andes - Mendoza

Corridor: Río Branco-Colonia -
Nueva Palmira

Rodovia Palhoça - Osório

Road 14

Bridge: Yaguarón - Río
Branco

Legend

- Road
- Railway
- Waterway
- Gas Pipeline
- Energy
- Bridge Border
- ◆ Center
- ⚓ Port

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Other Projects in the Portfolio

State: Execution

Amount: US\$ 10 M (CAF US\$ 10M)

MERCOSUR-CHILE HUB

Northeast Gas Pipeline

Road 60

Railway: Los Andes - Mendoza

Corridor: Río Branco-Colonia -
Nueva Palmira

Load Center:
Paso de los
Libres

Road14

Bridge: Yaguarón - Río
Branco

Legend

- Road
- Railway
- Waterway
- Gas Pipeline
- Energy
- Bridge Border
- ◆ Center
- ⚓ Port

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Other Projects in the Portfolio

State: Development

Amount : US\$ 30 M (FONPLATA US\$ 10 M)

MERCOSUR-CHILE HUB

New Bridges over Uruguay River in the AR-BR Border

Rodovia Palhoça - Osório

Road14

Bridge: Yaguarón - Río Branco

Northeast Gas Pipeline

Road 60

Railway: Los Andes - Mendoza

Corridor: Río Branco-Colonia - Nueva Palmira

Legend

- Road
- Railway
- Waterway
- Gas Pipeline
- Energy
- Bridge Border
- ◆ Center
- ⚓ Port

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Other Projects in the Portfolio

State: Execution

Amount : US\$ 188 M (CAF US\$ 106.7 M)

MERCOSUR-CHILE HUB

Northeast Gas Pipeline

Road 60

Paving Road 145

Railway: Los Andes - Mendoza

Corridor: Río Branco-Colonia -
Nueva Palmira

New Bridges over Uruguay
River in the AR-BR
Border

Load Center: Paso de los
Libres

Rodovia Palhoça - Osório

Road 14

Bridge: Yaguarón - Río
Branco

Legend

- Road
- Railway
- Waterway
- Gas Pipeline
- Energy
- Bridge Border
- ◆ Center
- ⚓ Port

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Other Projects in the Portfolio

State: Execution

Amount: US\$ 16 M (CAF US\$ 11.6 M)

MERCOSUR-CHILE HUB

Northeast Gas Pipeline

Road 60

Paving Road 145

Railway: Los Andes - Mendoza

Corridor: Río Branco-Colonia -
Nueva Palmira

Paving National
Road N°40
South

New Bridges over Uruguay
River in the AR-BR
Border

Load Center: Paso de los
Libres

Rodovia Palhoça-Osório

Road 14

Bridge: Yaguarón-Río
Branco

Legend

- Road
- Railway
- Waterway
- Gas Pipeline
- Energy
- Bridge Border
- Center
- Port

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Other Projects in the Portfolio

State: Execution

Amount: US\$ 50 M (CAF US\$ 35 M)

MERCOSUR-CHILE HUB

Northeast Gas Pipeline

Road 60

Paving Road 145

Railway: Los Andes - Mendoza

Corridor: Río Branco-Colonia -
Nueva Palmira

Paving National Road N°40
South

New Bridges over Uruguay
River in the AR-BR
Border

Load Center: Paso de los
Libres

Rodovia Palhoça - Osório

Road 14

Bridge: Yaguarón - Río
Branco

National Road
N°7: railway
detour La
Picas a lagoon

Legend

- Road
- Railway
- Waterway
- Gas Pipeline
- Energy
- Bridge
- Border
- Center
- Port

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Other Projects in the Portfolio

State: Execution

Amount : US\$ 10 M (CAF US\$ 10 M)

MERCOSUR-CHILE HUB

Northeast Gas Pipeline

Road 60

Paving Road 145

Railway: Los Andes - Mendoza

Corridor: Río Branco-Colonia -
Nueva Palmira

Paving National Road N°40
South

New Bridges over Uruguay
River in the AR-BR
Border

Load Center: Paso de los
Libres

Rodovia Palhoça - Osório

Road 14

Bridge: Yaguarón - Río
Branco

National Road N°7:
railway detour La Picas a
lagoon

National Road
N°7: road
detour: La
Picas a lagoon

Legend

- Road
- Railway
- Waterway
- Gas Pipeline
- Energy
- Bridge
- Border
- Center
- Port

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Other Projects in the Portfolio

State: Development. The BID has a CT with the resources from the Integration Fund.

Amount: US\$ 85 M (BID US\$ 48 M)

MERCOSUR-CHILE HUB

Modernization
of Montevideo
Port

Load Center: Paso de los
Libres

Rodovia Palhoça - Osório

Road 14

Bridge: Yaguarón - Río
Branco

National Road N°7:
railway detour: La Picaza
lagan

National Road N°7: Road
detour: La Picaza lagan

Northeast Gas Pipeline

Road 60

Paving Road 145

Railway: Los Andes - Mendoza

Corridor: Río Branco-Colonia -
Nueva Palmira

Paving National Road N°40
South


Legend

- Road
- Railway
- Waterway
- Gas Pipeline
- Energy
- Bridge Border
- Center
- Port

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Total of Projects: 14

- AIC - 7
- Rest of the IIRSA Portfolio - 7

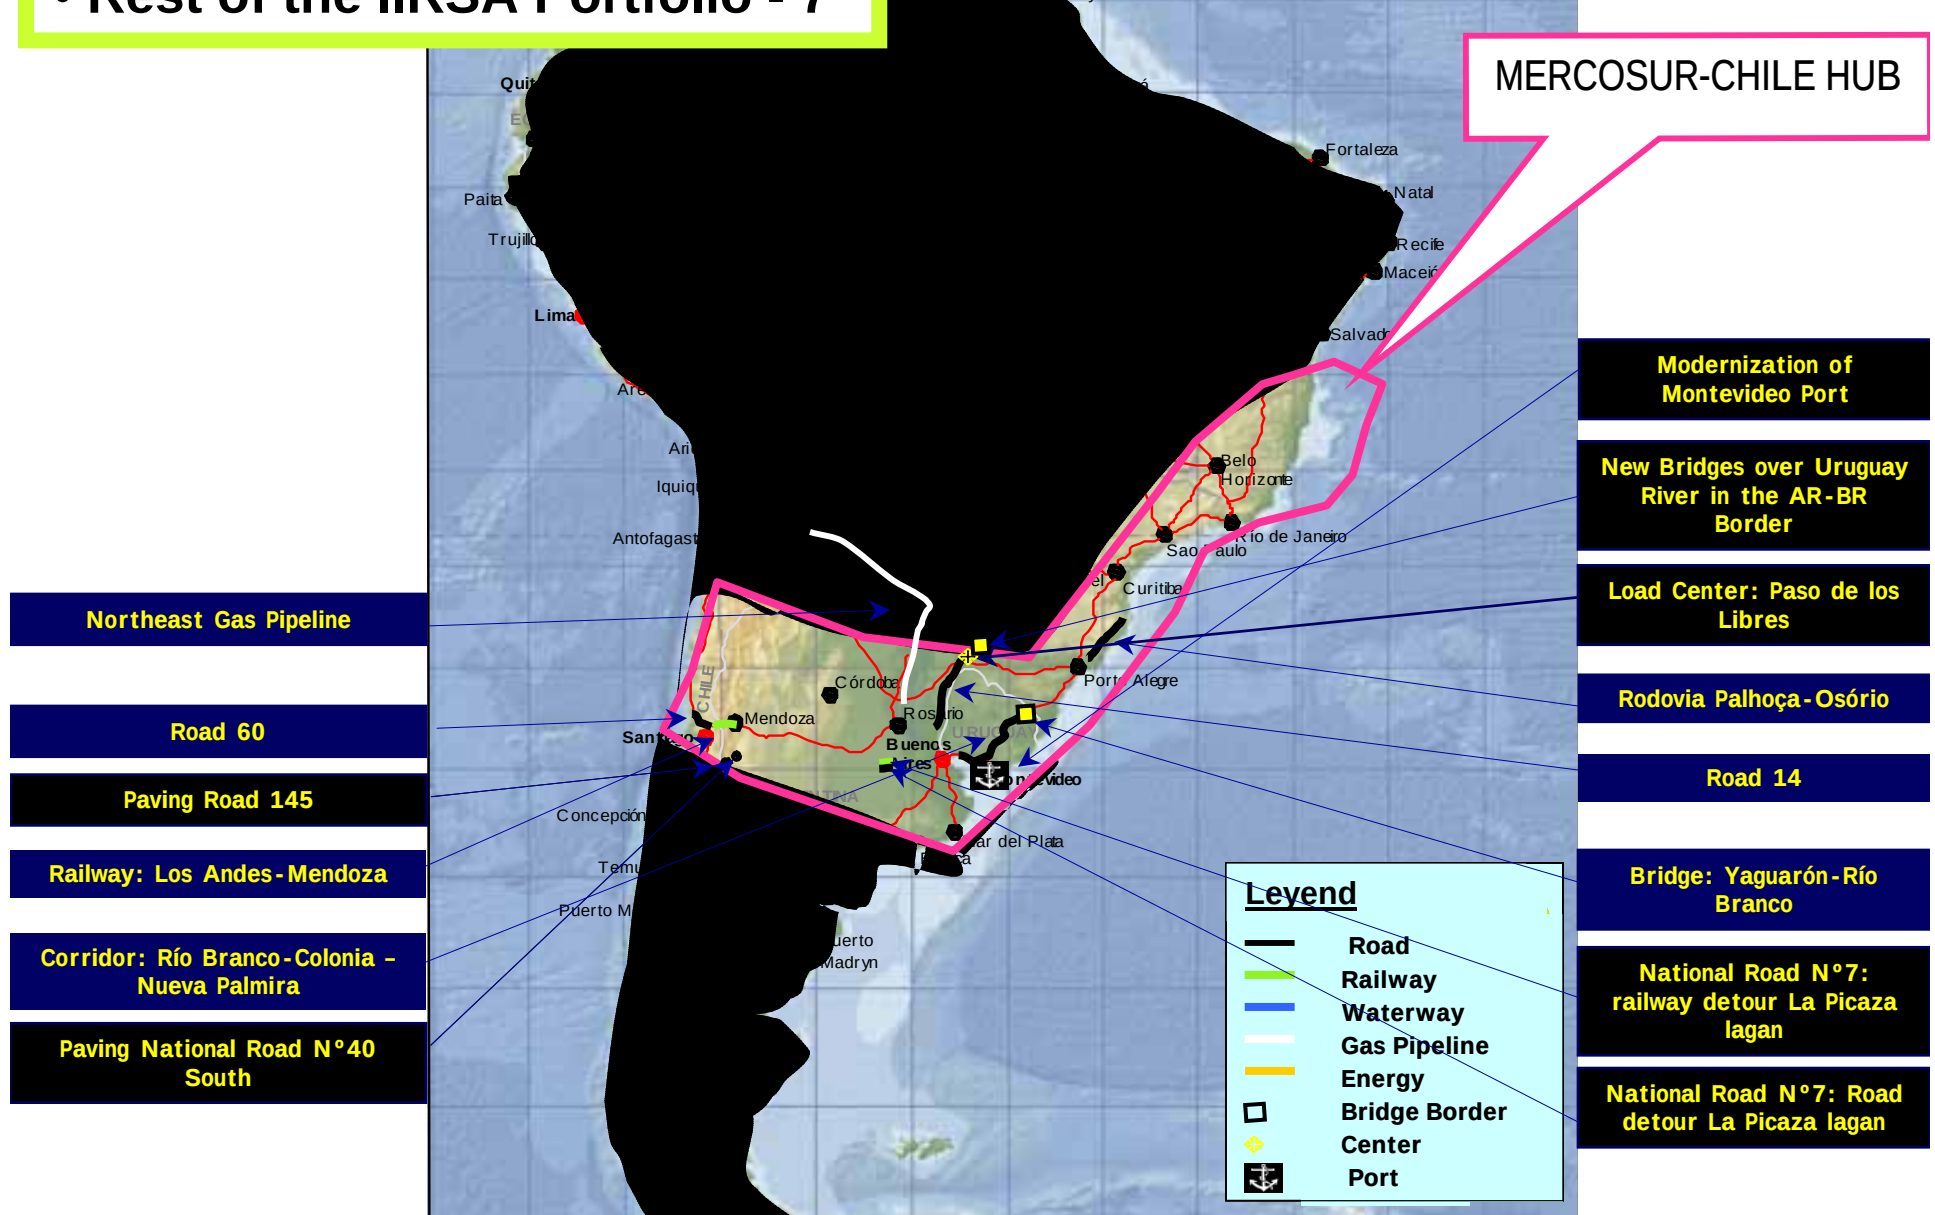

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

AIC – PROJECT UNDER MODERATE PROGRESS


State: Feasibility study completed. May 2007, agreement is pending regarding: 1) A possible improvement work schedule in the existing bridge and; 2) A possible schedule regarding tasks for the execution of the works of the new bridge to be built, access works and integrated control center.

Amount: US\$ 10 M (FONPLATA)

Completion planned: December 2008

CAPRICORN HUB

**AIC 8 – Bridge:
Salvador Mazza-
Yacuiba and
Border Center**

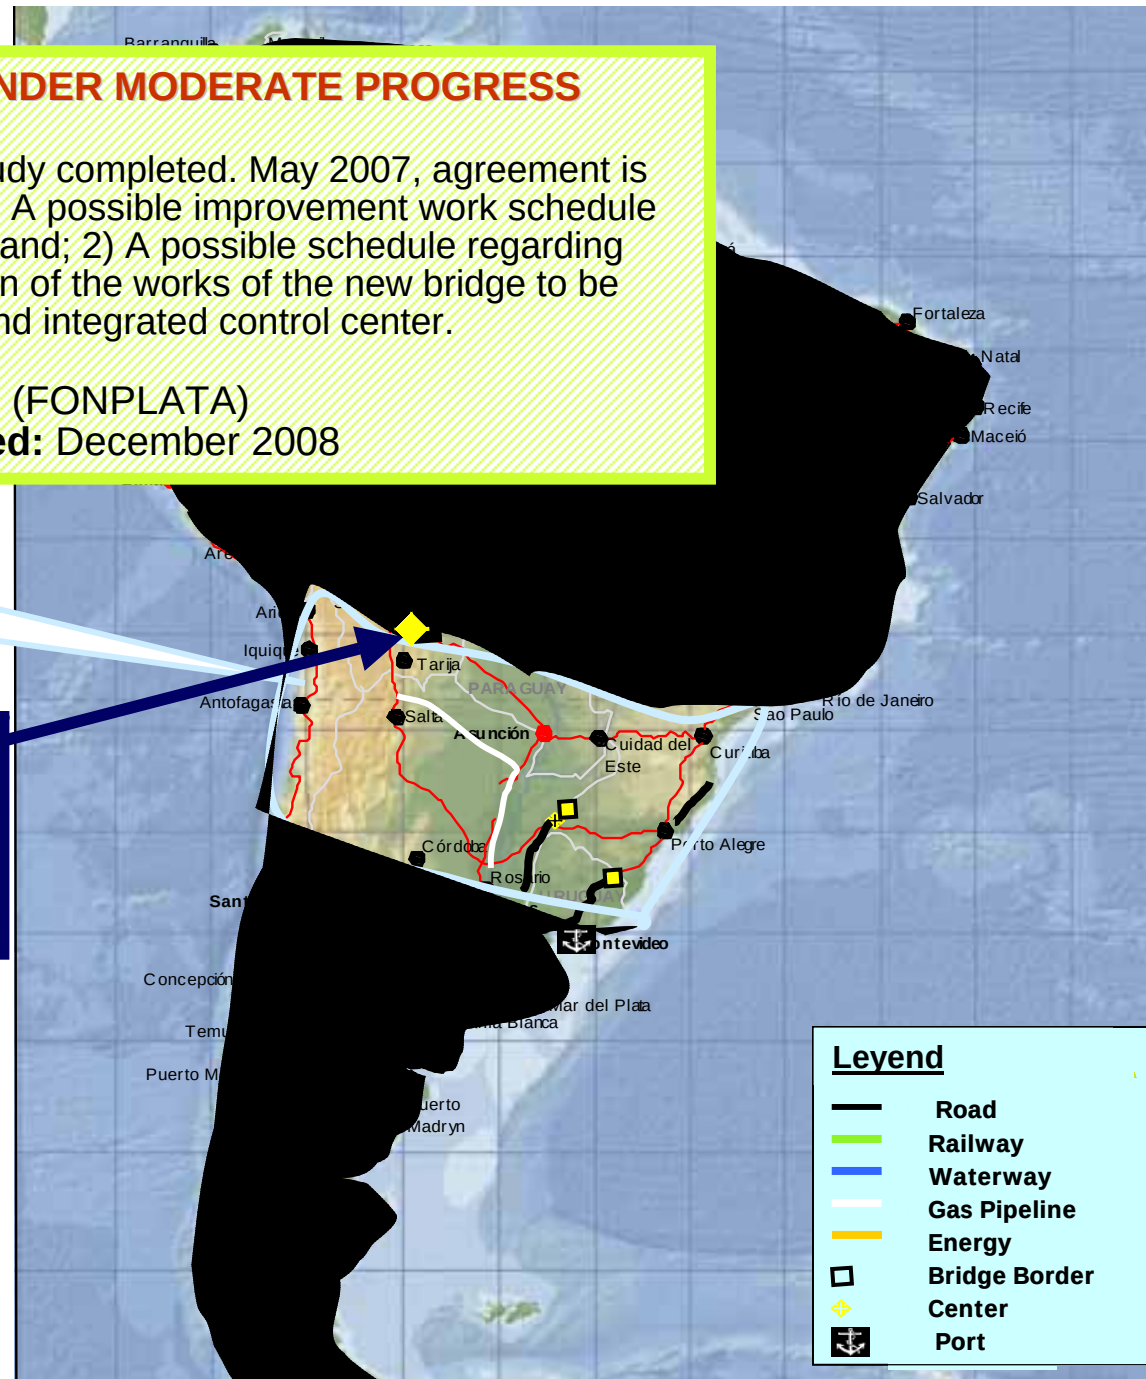

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

AIC – PROJECT UNDER MODERATE PROGRESS

State: Pre-feasibility completed. The Brazilian Government is about to follow tendering procedures regarding the Design and Construction of the Works. The BID is negotiating a CT for the designs of the accesses in the Paraguayan side.


Amount: US\$ 55 M (FONPLATA US\$ 30 M)

Completion planned: 2º four-month period 2010

CAPRICORN HUB

Bridge: Salvador Mazza-
Yacuiba and Border Center

AIC 9 –
Bridge: Pres.
Franco-
Porto Meira
and Border
Center

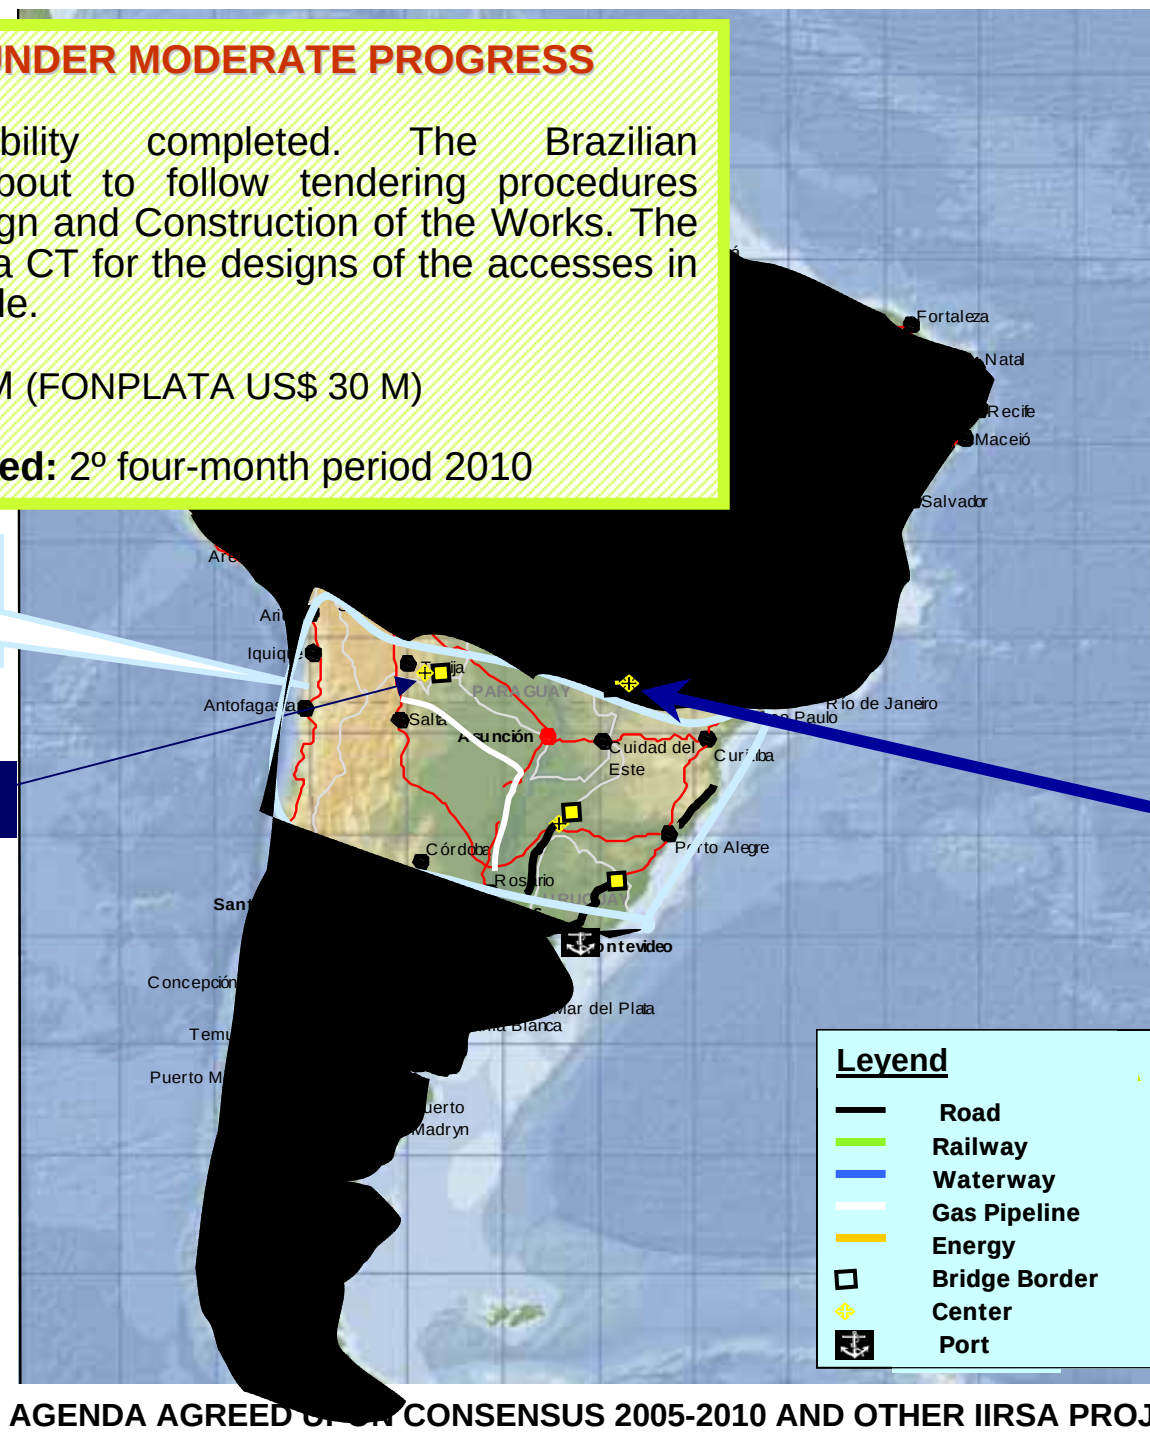

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Other Projects in the Portfolio

State: Execution

Amount: US\$ 54 M (CAF US\$ 54 M)

Accesses to Paso de Jama

CAPRICORN HUB

Bridge: Salvador Mazza-Yacuiba and Border Center

Bridge: Pres. Franco-Porto Meira and Border Center

Legend

- Road
- Railway
- Waterway
- Gas Pipeline
- Energy
- Bridge Border
- ◆ Center
- ⚓ Port

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Other Projects in the Portfolio

State: Execution is starting. Approved financing.

Amount: US\$ 752 M (BID US\$ 580 M)


Accesses to Paso de Jama

CAPRICORN HUB

Bridge: Salvador Mazza-
Yacuiba and Border Center

Electric
Interconnection:
NOA - NEA

Bridge: Pres. Franco-
Porto Meira and Border
Center

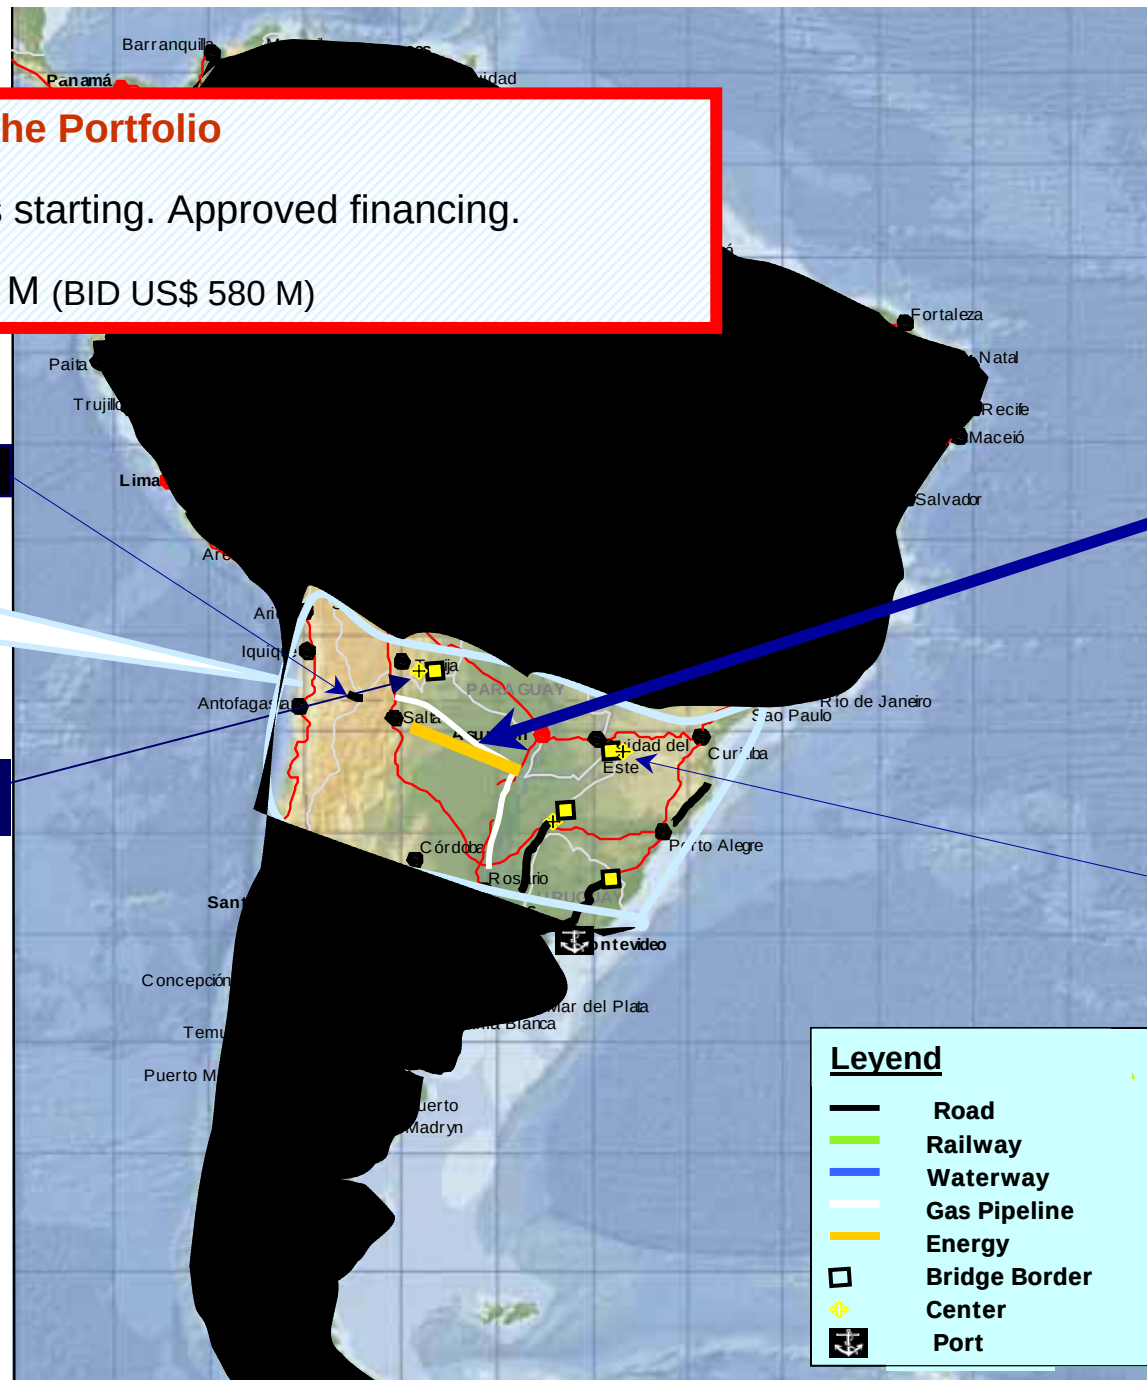

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Other Projects in the Portfolio

State: Execution.

Amount : US\$ 126.2 M (CAF US\$ 90.2 M)


Accesses to Paso de Jama

CAPRICORN HUB

Bridge: Salvador Mazza-
Yacuiba and Border Center

RN N° 81.
Paving: Las
Lomitas

Bridge: Pres. Franco-
Porto Meira and Border
Center

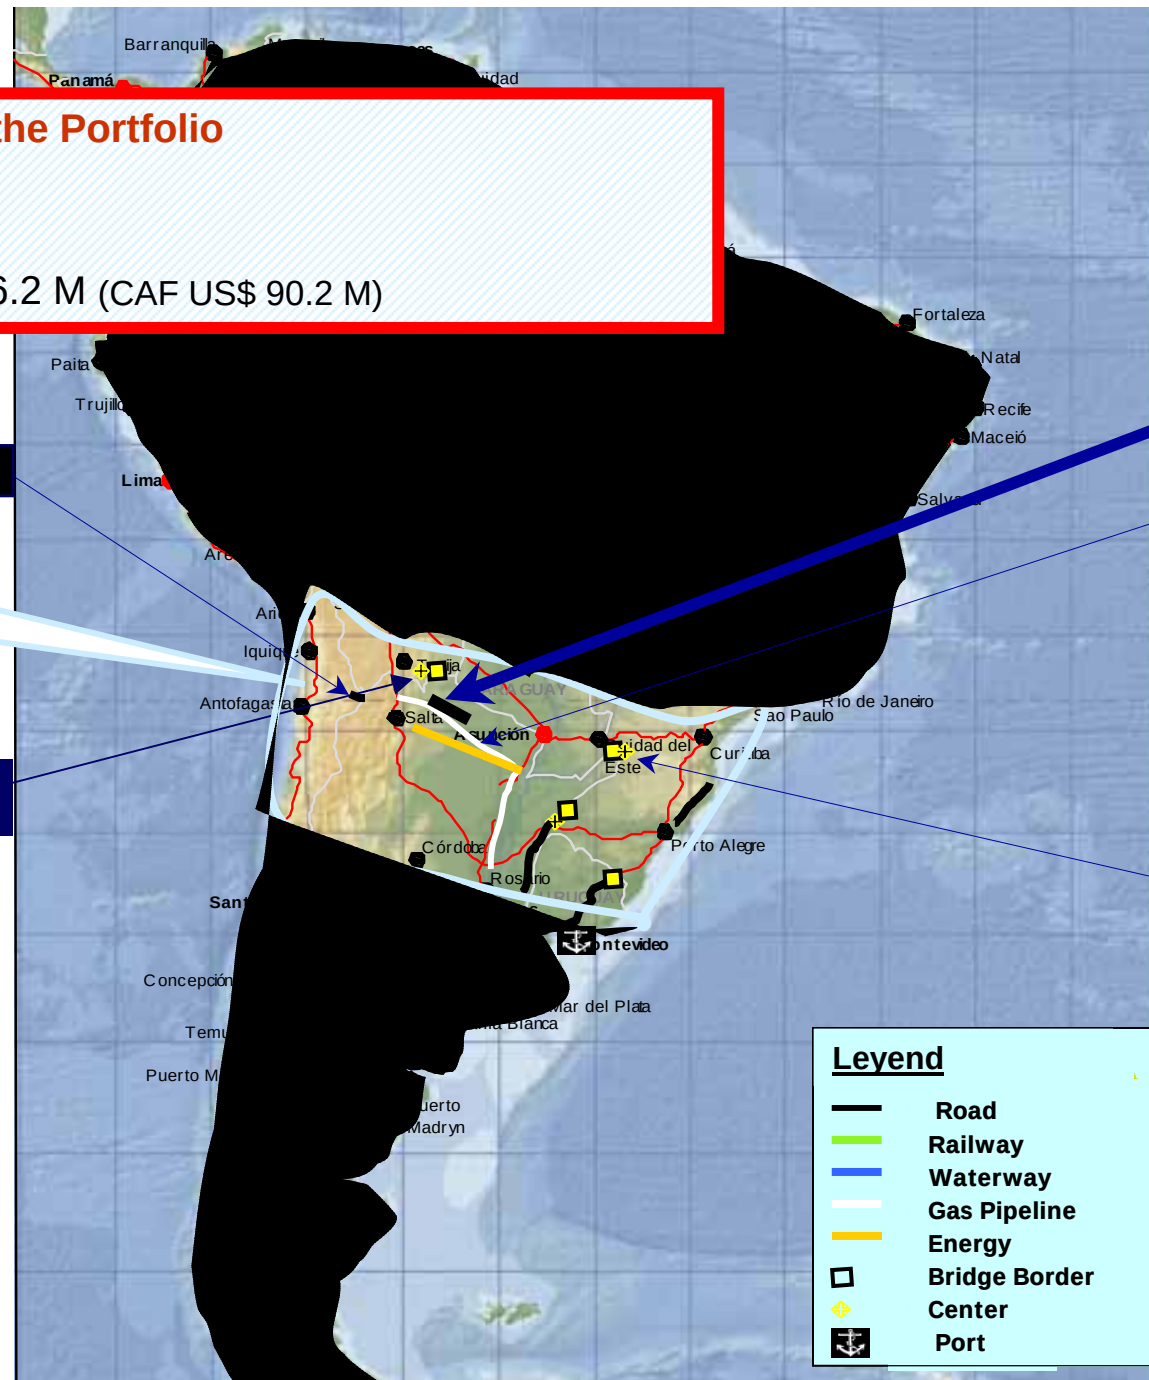

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Other Projects in the Portfolio

State: Development.

Amount : US\$ 15 M (FONPLATA US\$ 10 M)

Accesses to Paso de Jama

CAPRICORN HUB


Bridge: Salvador Mazza -
Yacuiba and Border Center

RN N° 81. Paving: Las
Lomitas

Electric Interconnection:
NOA - NEA

Optimization
of the Node:
Clorinda -
Asunción

Bridge: Pres. Franco -
Porto Meira and Border
Center

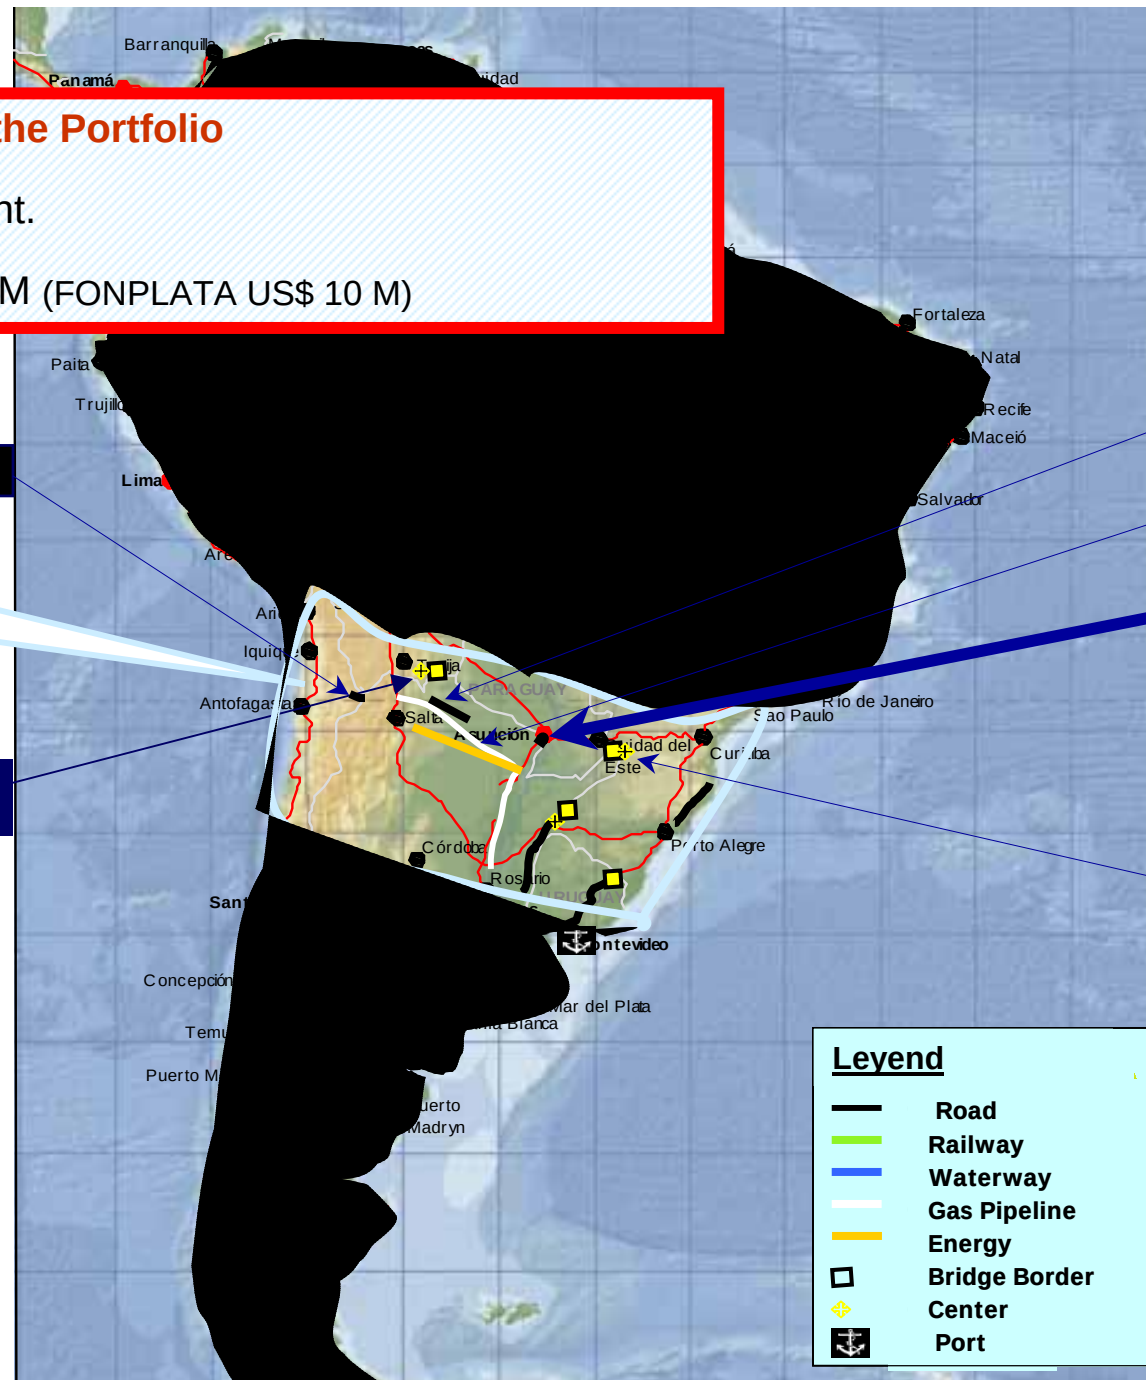

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Other Projects in the Portfolio

State: Execution.

Amount : US\$ 190 M (FONPLATA US\$ 18 M, BID US\$ 100 M)

Accesses to Paso de Jama


CAPRICORN HUB

Bridge: Salvador Mazza -
Yacuiba and Border Center

Paving:
Tartagal -
Misión, La Paz
- Pozo Hondo
- Mariscal
Estigarribia

Optimization of the Node:
Clorinda - Asunción

Bridge: Pres. Franco -
Porto Meira and Border
Center

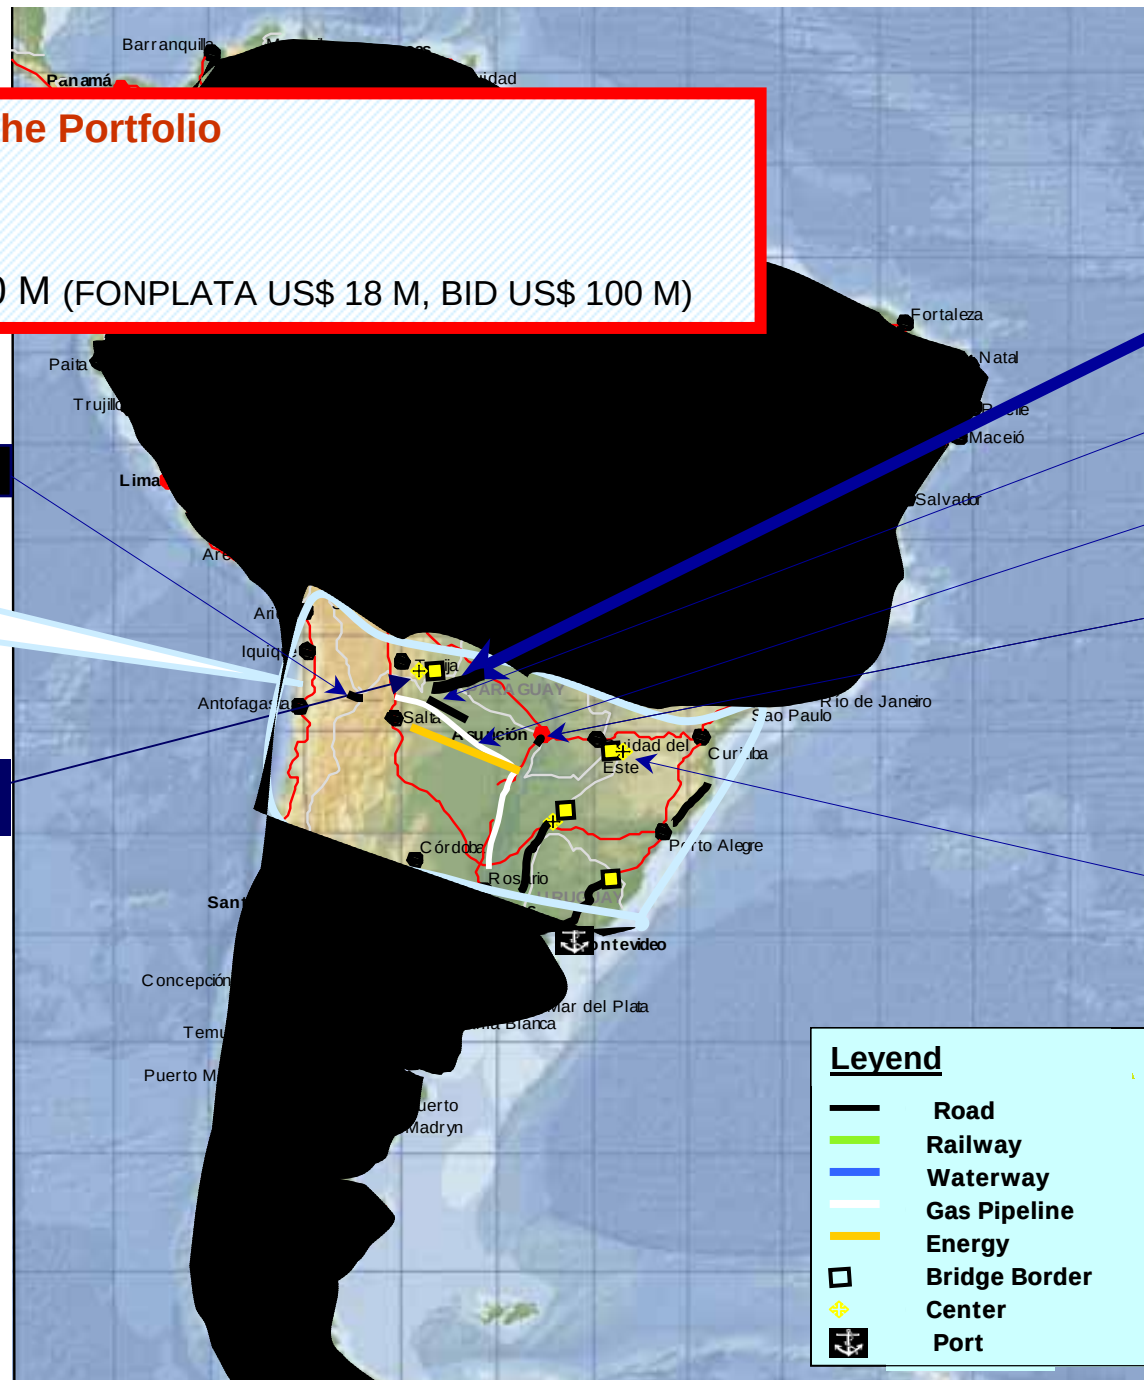

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Other Projects in the Portfolio

State: Execution.

Amount : US\$ 104.5 M (FONPLATA US\$ 17M)

Road: Abapó -
Camiri

CAPRICORN HUB

Bridge: Salvador Mazza-
Yacuiba and Border Center


Paving: Tartagal - Misión,
La Paz - Pozo Hondo -
Mariscal Estigarribia

RN N° 81. Paving: Las
Lomitas

Electric Interconnection:
NOA - NEA

Optimization of the Node:
Clorinda - Asunción

Bridge: Pres. Franco-
Porto Meira and Border
Center

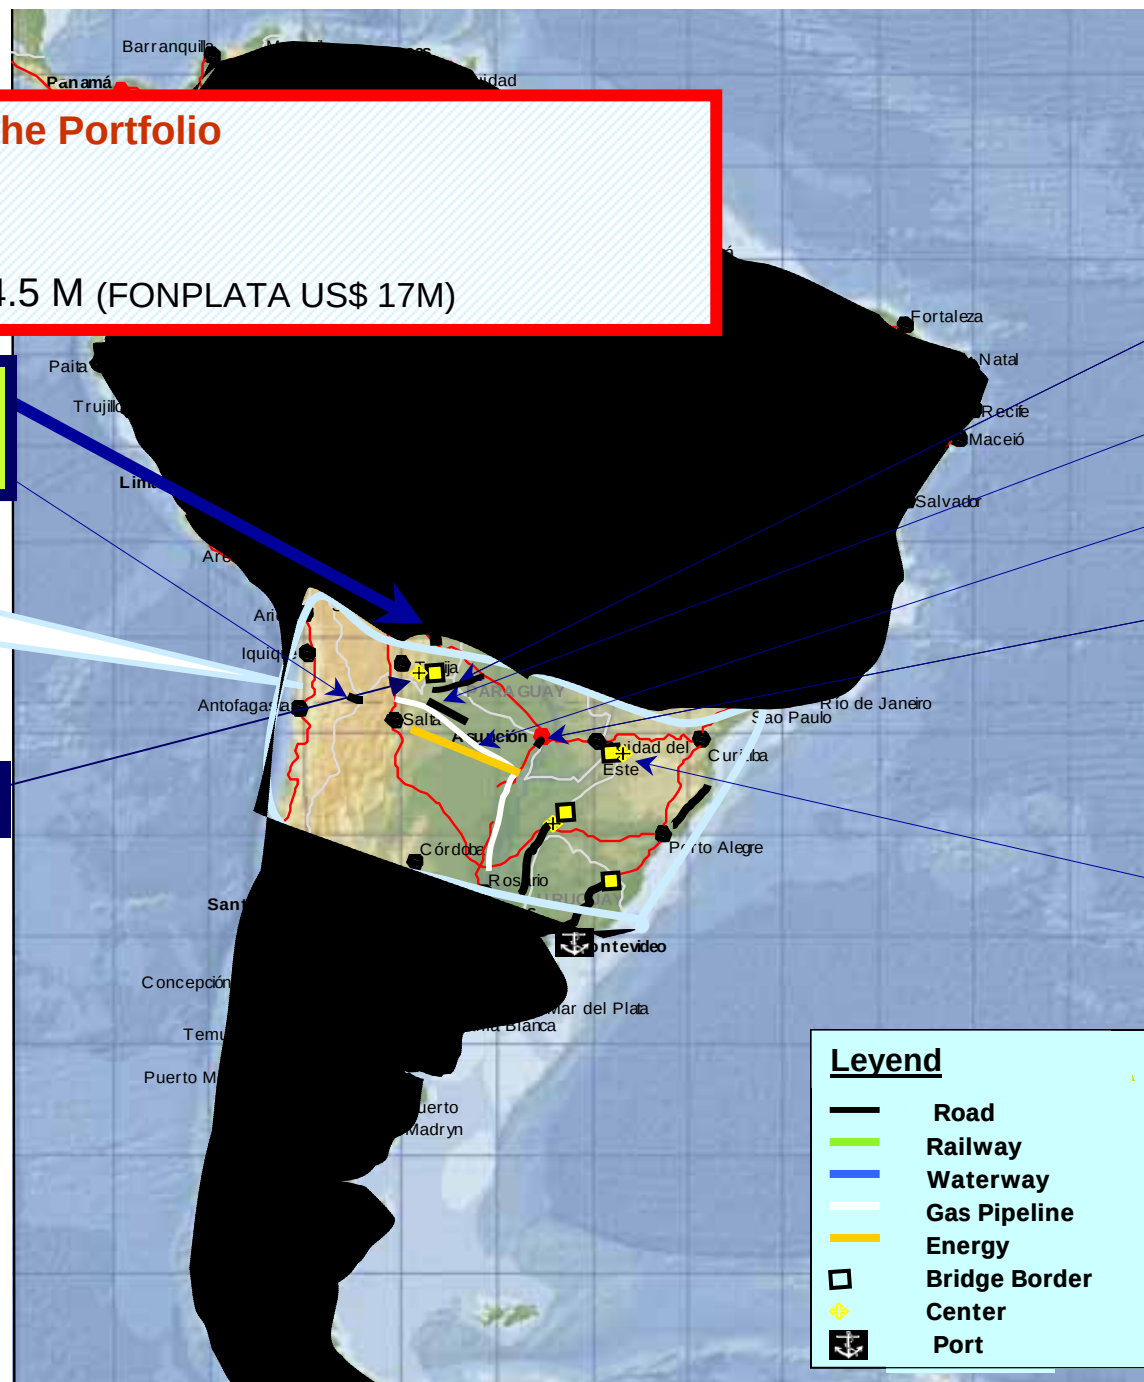

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Other Projects in the Portfolio

State: Development.

Amount : US\$ 15 M (FONPLATA US\$ 10 M)

Road: Abapó - Camiri

Accesses to Paso de Jama

CAPRICORN HUB

Bridge: Salvador Mazza -
Yacuiba and Border Center

Paving: Tartagal - Misión,
La Paz - Pozo Hondo -
Mariscal Estigarribia


RN N° 81. Paving: Las
Lomitas

Electric Interconnection:
NOA - NEA

Optimization of the Node:
Clorinda - Asunción

Improvement of
the Bridge:
Posadas -
Encarnación

Bridge: Pres. Franco -
Porto Meira and Border
Center

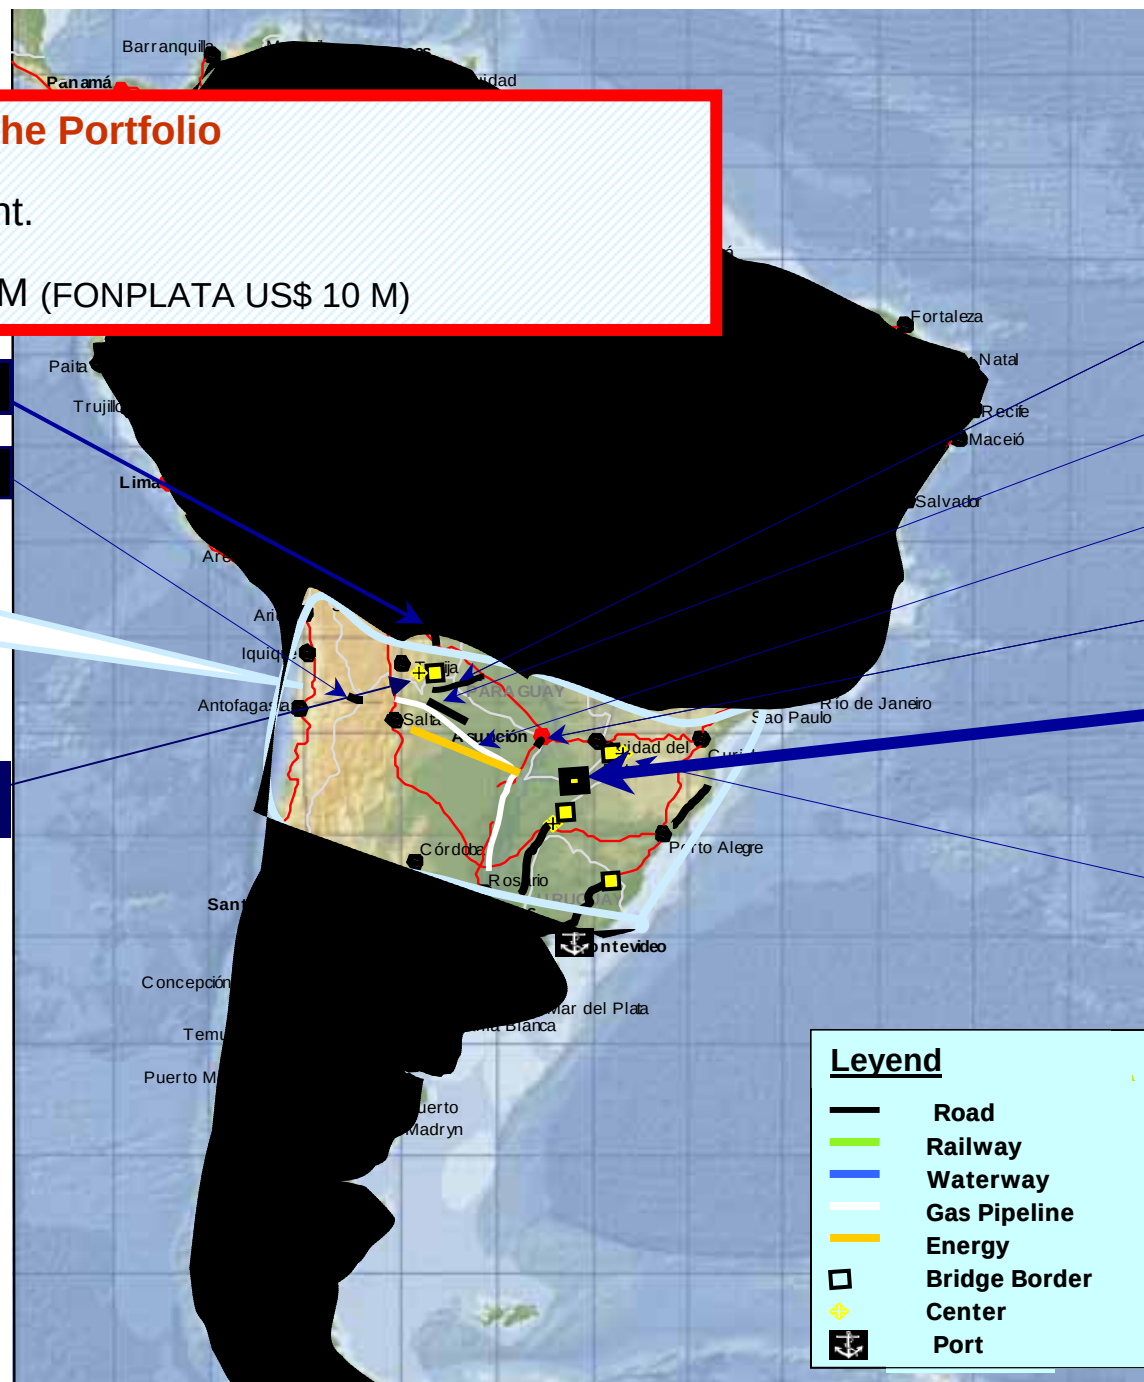

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Other Projects in the Portfolio

State: Development.

Amount : US\$ 90 M (BID US\$ 80 M)

Road: Abapó - Camiri

Accesses to Paso de Jama

CAPRICORN HUB

Bridge: Salvador Mazza -
Yacuiba and Border Center

Paving: Tartagal - Misión,
La Paz - Pozo Hondo -
Mariscal Estigarribia


RN N° 81. Paving: Las
Lomitas

Electric Interconnection:
NOA - NEA

Optimization of the Node:
Clorinda - Asunción

Improvement Posadas -
Encarnación Bridge

Construction:
Road 8
Caazapa -
Coronel
Bogado

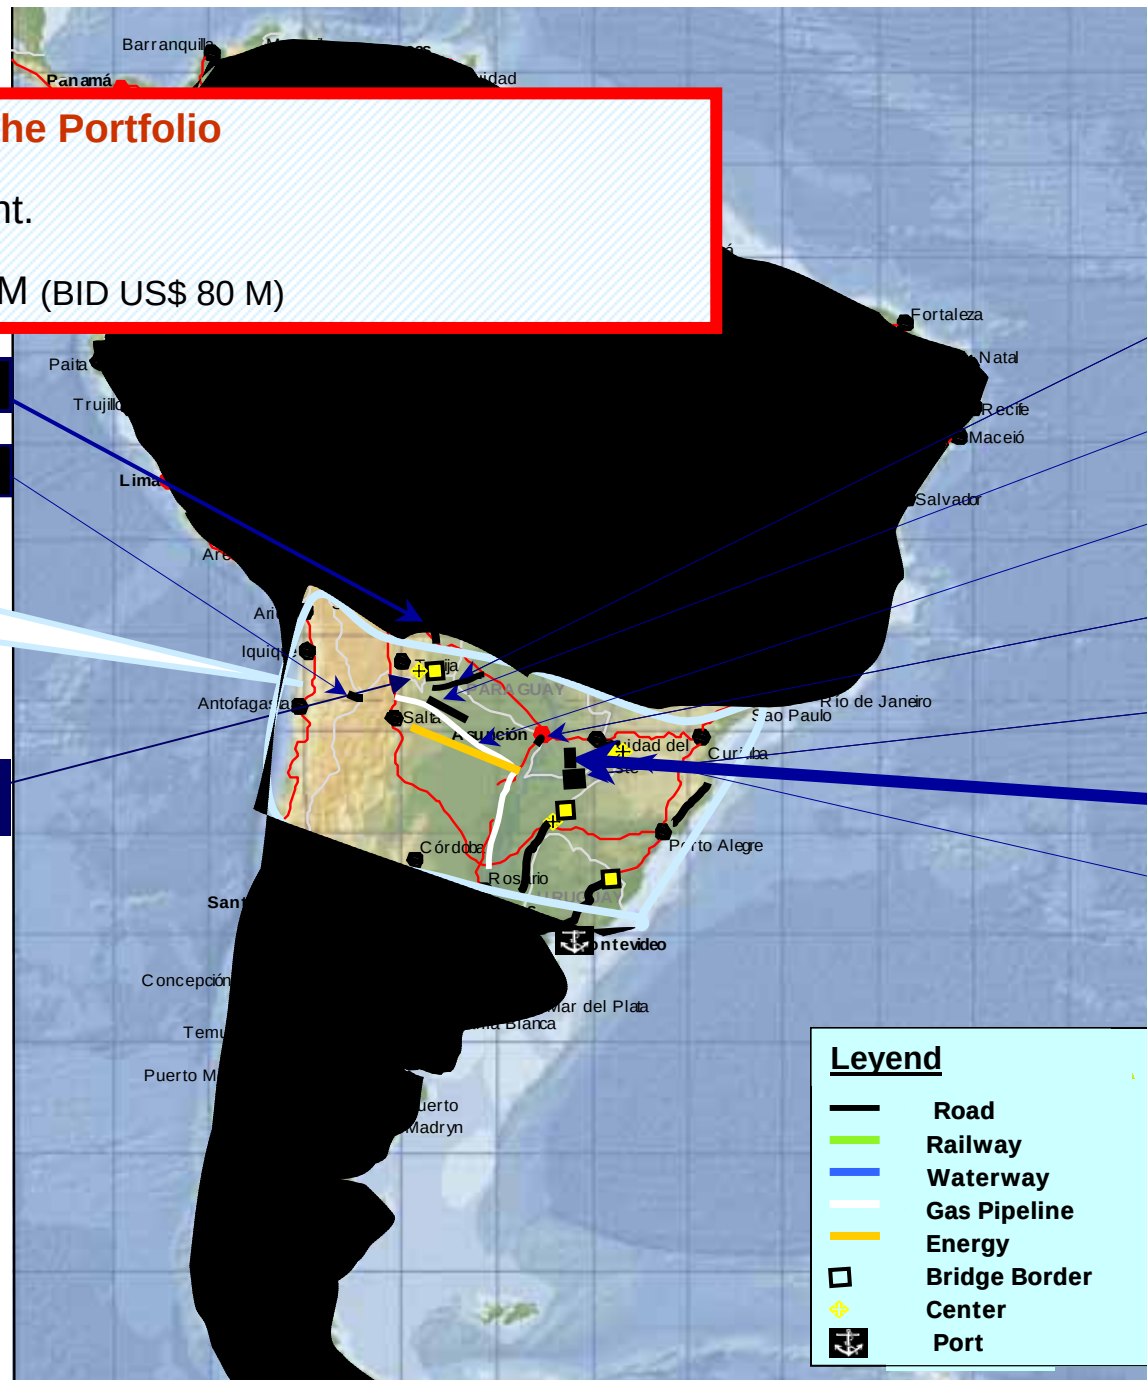

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Other Projects in the Portfolio

State: Development.

Amount : US\$ 56 M (BID US\$ 56 M)

Road: Abapó - Camiri

Accesses to Paso de Jama

CAPRICORN HUB

Bridge: Salvador Mazza -
Yacuiba and Border Center

Accesses to
Cisco Border
Crossing

Paving: Tartagal - Misión,
La Paz - Pozo Hondo -
Mariscal Estigarribia

RN N° 81. Paving: Las
Lomitas


Electric Interconnection:
NOA - NEA

Optimization of the Node:
Clorinda - Asunción

Improvement Posadas -
Encarnación Bridge

Construction Road 8
Caazapa - Coronel Bogado

Bridge: Pres. Franco -
Porto Meira and Border
Center

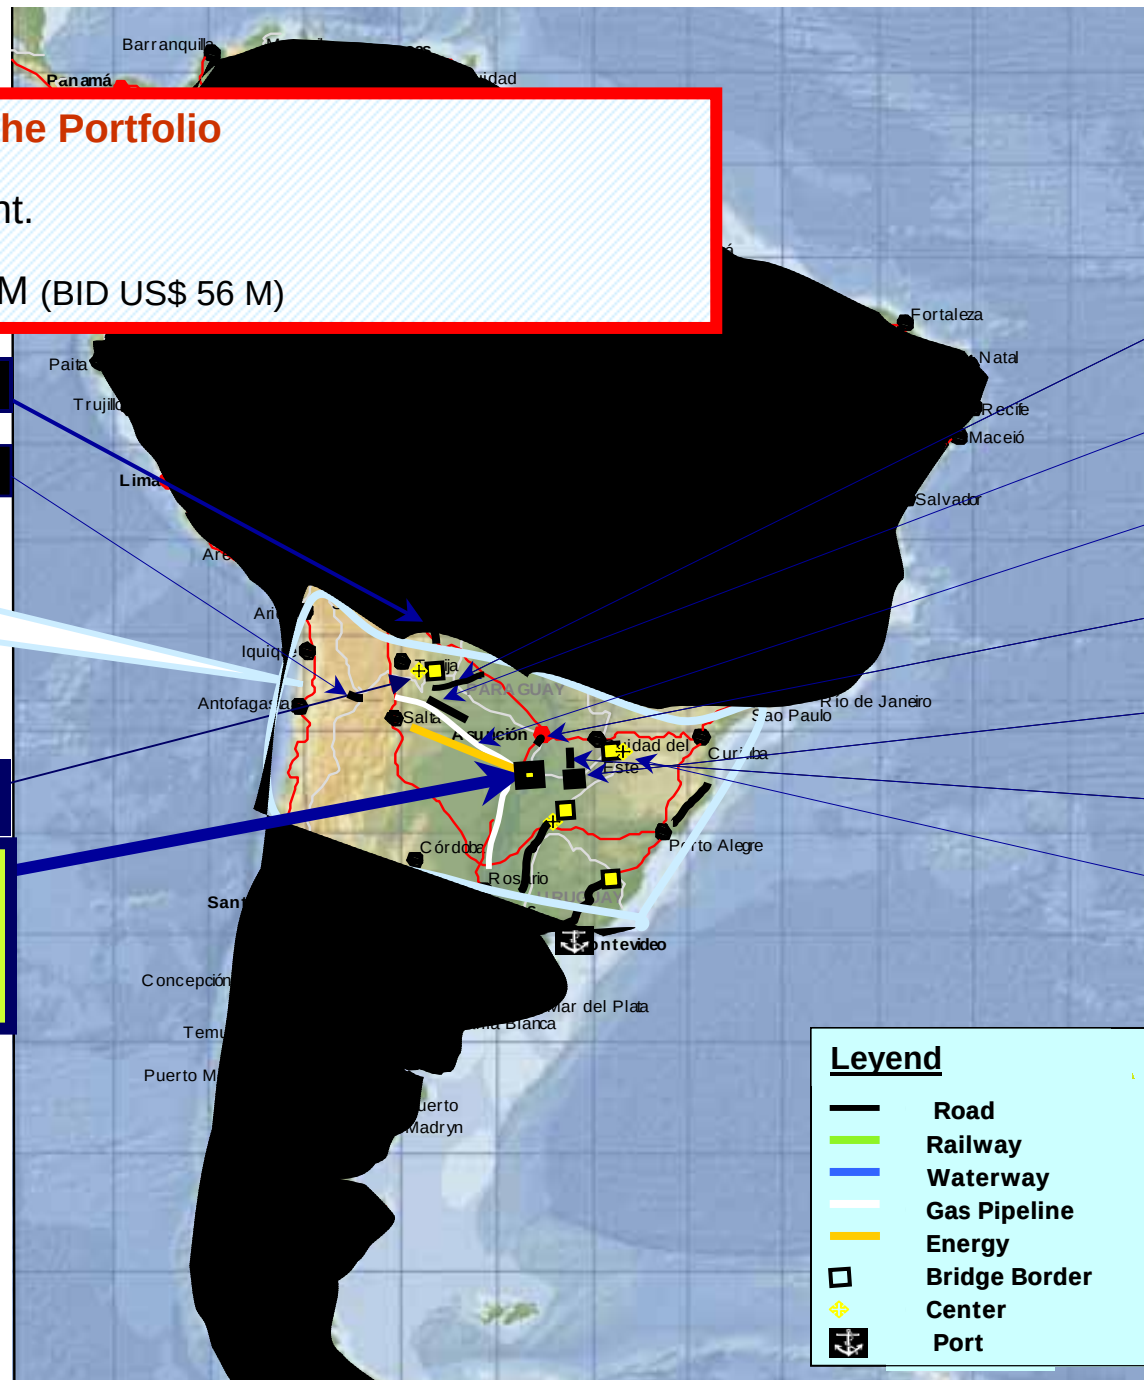

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Other Projects in the Portfolio

State: Development.

Amount : US\$ 50 M (FONPLATA US\$ 40 M)

Road: Abapó - Camiri

Accesses to Paso de Jama

CAPRICORN HUB

Construction
Ñeembucú -
Chaco Bridge

Construction Bimodal
Resistencia - Corrientes Bridge

Paving: Tartagal - Misión,
La Paz - Pozo Hondo -
Mariscal Estigarribia

RN N° 81. Paving: Las
Lomitas


Electric Interconnection:
NOA - NEA

Optimization of the Node:
Clorinda - Asunción

Improvement Posadas -
Encarnación Bridge

Construction Road 8
Caazapa-Coronel Bogado

Bridge: Pres. Franco-
Porto Meira and Border
Center

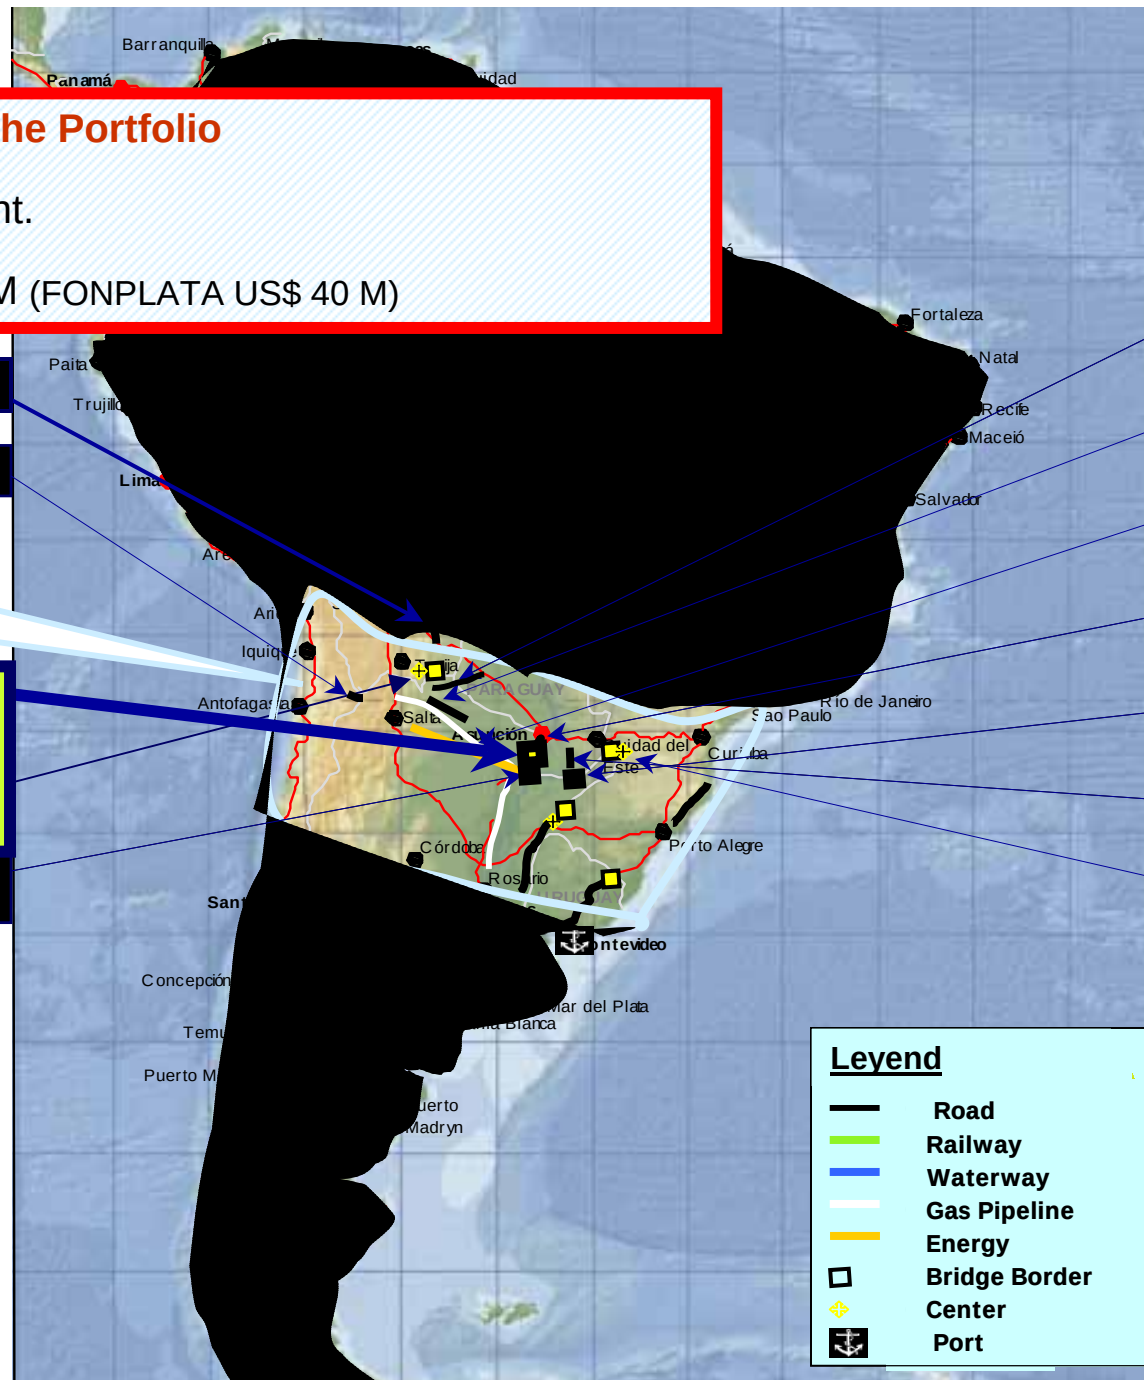

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Total of Projects: 12

- AIC - 2
- Rest of the IIRSA Portfolio - 10

Road: Abapó - Camiri

Accesses to Paso de Jama

CAPRICORN HUB

Construction Bridge: Ñeembucú - Chaco

Bridge: Salvador Mazza - Yacuiba and Border Center

Construction Bridge: Bimodal Resistencia - Corrientes

Paving: Tartagal - Misión,
La Paz - Pozo Hondo -
Mariscal Estigarribia

RN N° 81. Paving: Las
Lomitas


Electric Interconnection:
NOA - NEA

Optimization of the Node:
Clorinda - Asunción

Improvement Posadas -
Encarnación Bridge

Construction Road 8
Caazapa - Coronel Bogado

Bridge: Pres. Franco -
Porto Meira and Border
Center

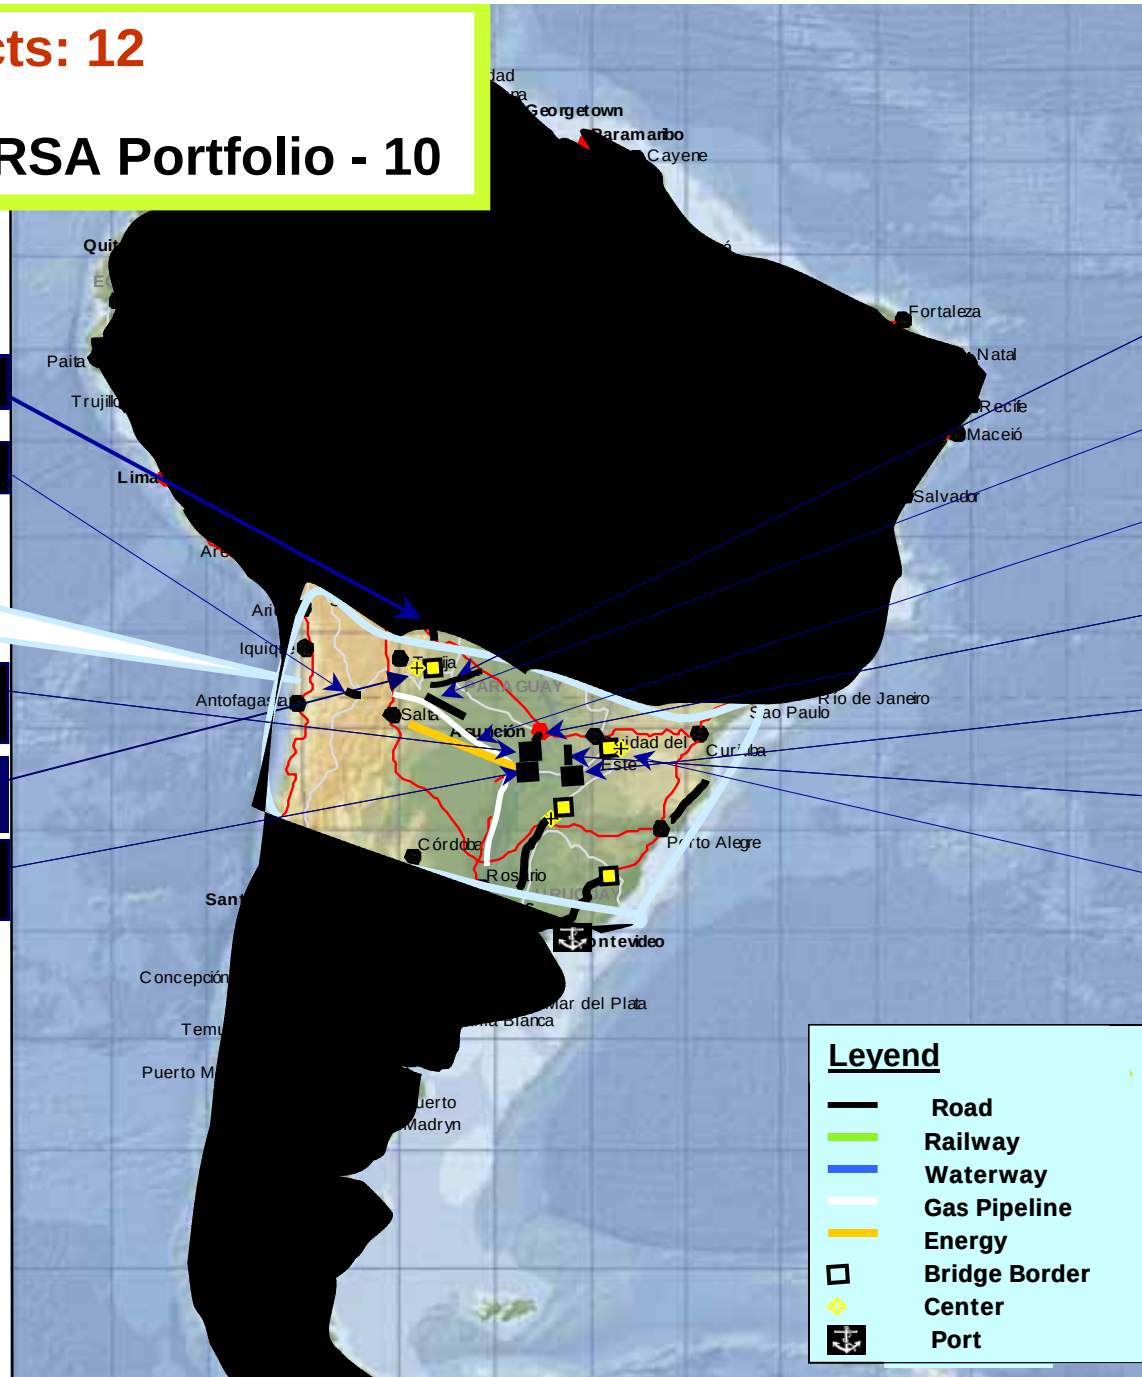

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

AIC – PROJECT UNDER SATISFACTORY PROGRESS


State: Execution.

Amount : US\$ 444,8 (CAF US\$ 280 M – BID US\$ 75 M, and others)

Completion planned: January 2009

**AIC 10 –
Road: Pailón –
Puerto Suárez**

**CENTRAL INTER-
OCEANIC HUB**

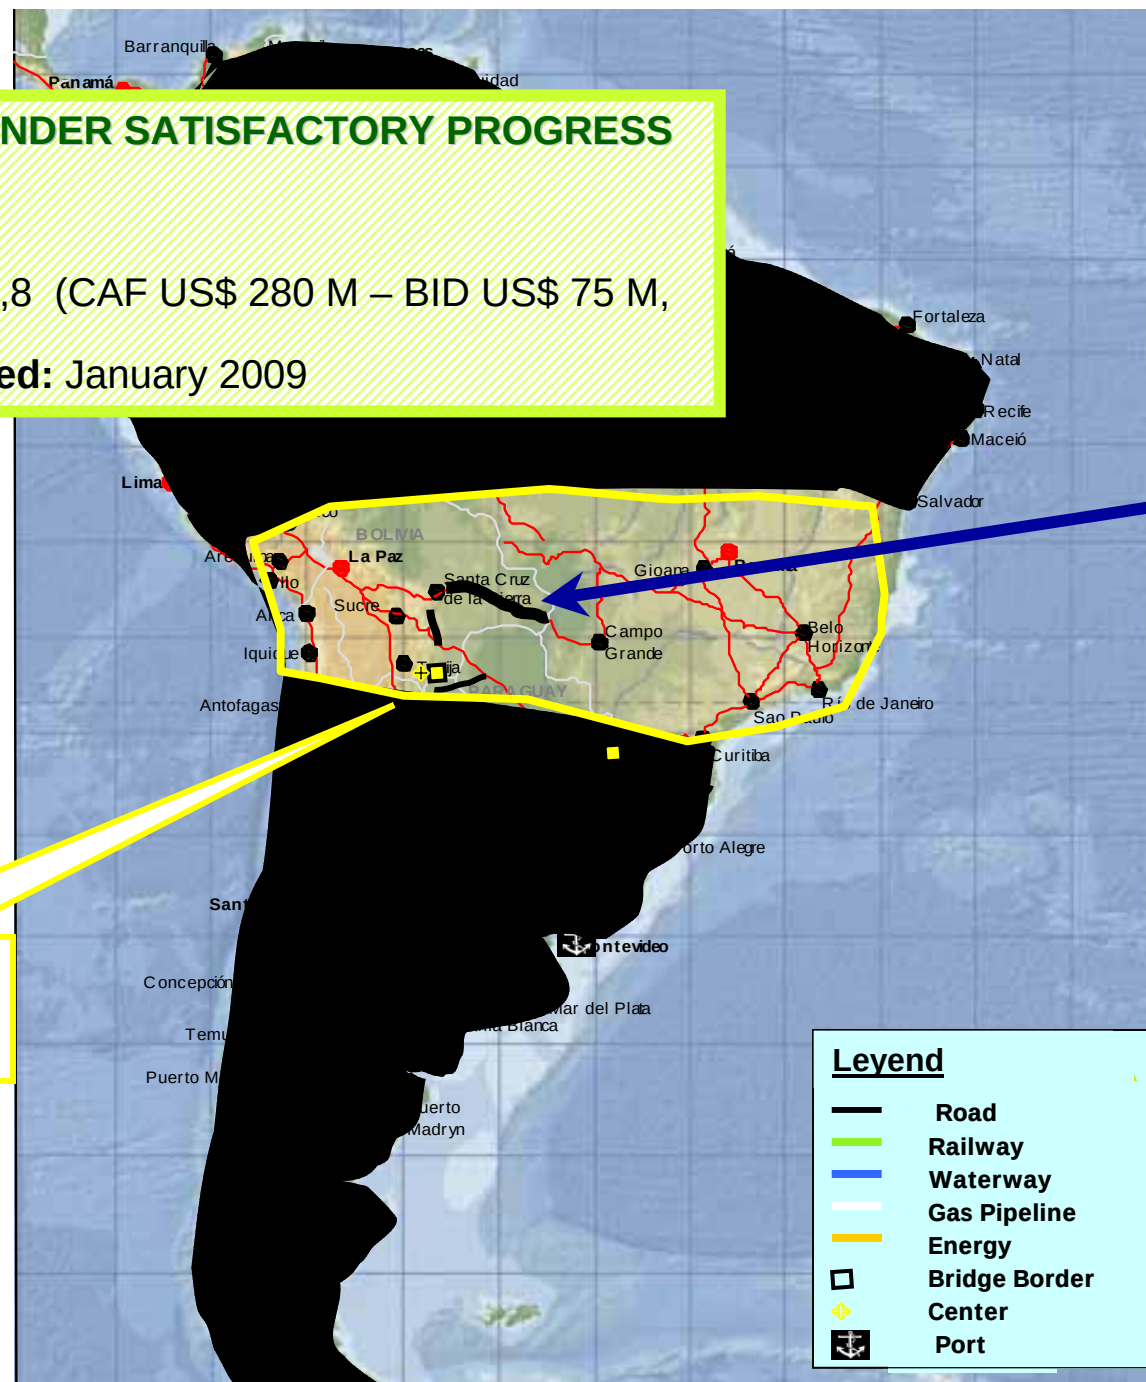

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

AIC – PROJECT WITH SOME RESTRICTIONS

State: The government is re-evaluating the studies carried out by the concessionaire MRS Logistica. Financing to be defined, possible concession to the private sector.

Amount : US\$ 400 M

Completion planned: To be defined.

CENTRAL INTER-OCEANIC HUB

Road: Pailón - Puerto Suárez

AIC 11 - São Paulo Railway Ring

Legend

- Road
- Railway
- Waterway
- Gas Pipeline
- Energy
- Bridge Border
- ⬠ Center
- ⚓ Port

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

AIC – PROJECT UNDER SATISFACTORY PROGRESS

State: Under development. Part of a big program that is performed with the support of: CAF, BID and FONPLATA.

Amount : US\$ 1.2 M (BID US\$ 1.0)

Completion planned: 1º semester 2008

CENTRAL INTER-
OCEANIC HUB

Road: Pailón - Puerto
Suárez

São Paulo Railway Ring

**AIC 12 -
Border
Center:
Cañada Oruro
-Infante
Rivarola**

Legend

- Road
- Railway
- Waterway
- Gas Pipeline
- Energy
- Bridge Border
- ◆ Center
- ⚓ Port

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

AIC – PROJECT UNDER SATISFACTORY PROGRESS

State: Execution.

Amount : US\$ 60 M I Stage (CAF US\$ 60 M)

Completion planned: 2010

CENTRAL INTER-
OCEANIC HUB

Road: Pailón - Puerto
Suárez

AIC 13 -
Road: Cañada
Oruro -
Villamontes

Oruro -Infante Rivarola

Legend

- Road
- Railway
- Waterway
- Gas Pipeline
- Energy
- Bridge Border
- ⬢ Center
- ⚓ Port

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

AIC – PROJECT UNDER SATISFACTORY PROGRESS

State: Execution.

Amount : US\$ 93 M (CAF US\$ 63.9 M)

Completion planned: 2009

**AIC 14 – Road:
Toledo- Pisiga**

CENTRAL INTER-
OCEANIC HUB

Road: Pailón – Puerto
Suárez

Road: Cañada Oruro –
Villamontes

São Paulo Railway Ring

Border Center: Cañada
Oruro –Infante Rivarola

Legend

- Road
- Railway
- Waterway
- Gas Pipeline
- Energy
- Bridge Border
- ⬢ Center
- ⚓ Port

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

AIC – PROJECT UNDER SATISFACTORY PROGRESS

State: Execution.

Amount : US\$ 37 M

Completion planned: December 2010

Road: Toledo - Pisiga

**AIC 15 -
Refitting:
Iquique - Colchane**


CENTRAL INTER-
OCEANIC HUB

Road: Pailón - Puerto
Suárez

Road: Cañada Oruro -
Villamontes

São Paulo Railway Ring

Border Center: Cañada
Oruro -Infante Rivarola

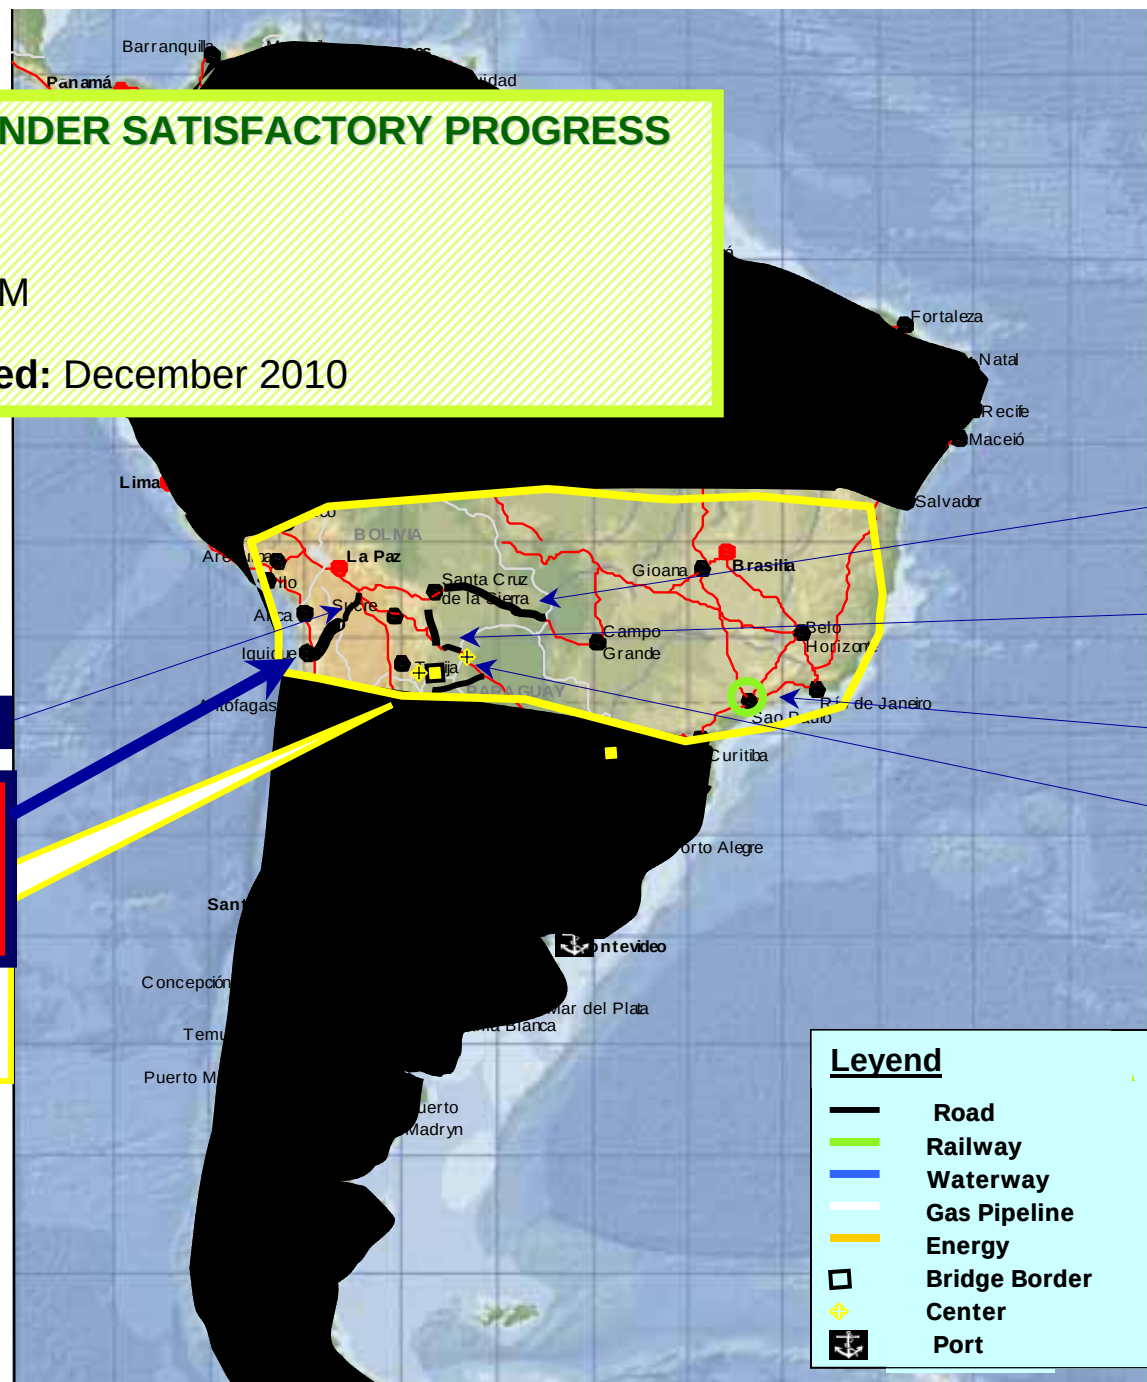

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

AIC – PROJECT UNDER MODERATE PROGRESS

State: The Solution to the geological instability of the Section is being studied.

Amount: US\$ 2.5 M (Study)

Completion planned: 3° quarter 2009

AIC 16 – Refitting Section: El Sillar

Road: Cañada Oruro –
Villamontes

São Paulo Railway Ring

Border Center: Cañada
Oruro –Infante Rivarola

Road: Toledo- Pisiga

Refitting: Iquique-Colchane

CENTRAL INTER-
OCEANIC HUB

Legend

- Road
- Railway
- Waterway
- Gas Pipeline
- Energy
- Bridge Border
- ⬢ Center
- ⚓ Port

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Other Projects in the Portfolio

State: First section is completed, second section is under execution and third section is being studied.

Amount : US\$ 642 M Sections: II and III (CAF US\$ 90.2 M)

**Paving: Potosí-
Tupiza - Villazón**

Road: Toledo - Pisiga

Refitting: Iquique - Colchane

**CENTRAL INTER-
OCEANIC HUB**


**Refitting Section: El
Sillar**

**Road: Pailón - Puerto
Suárez**

**Road: Cañada Oruro -
Villamontes**

São Paulo Railway Ring

**Border Center: Cañada
Oruro -Infante Rivarola**

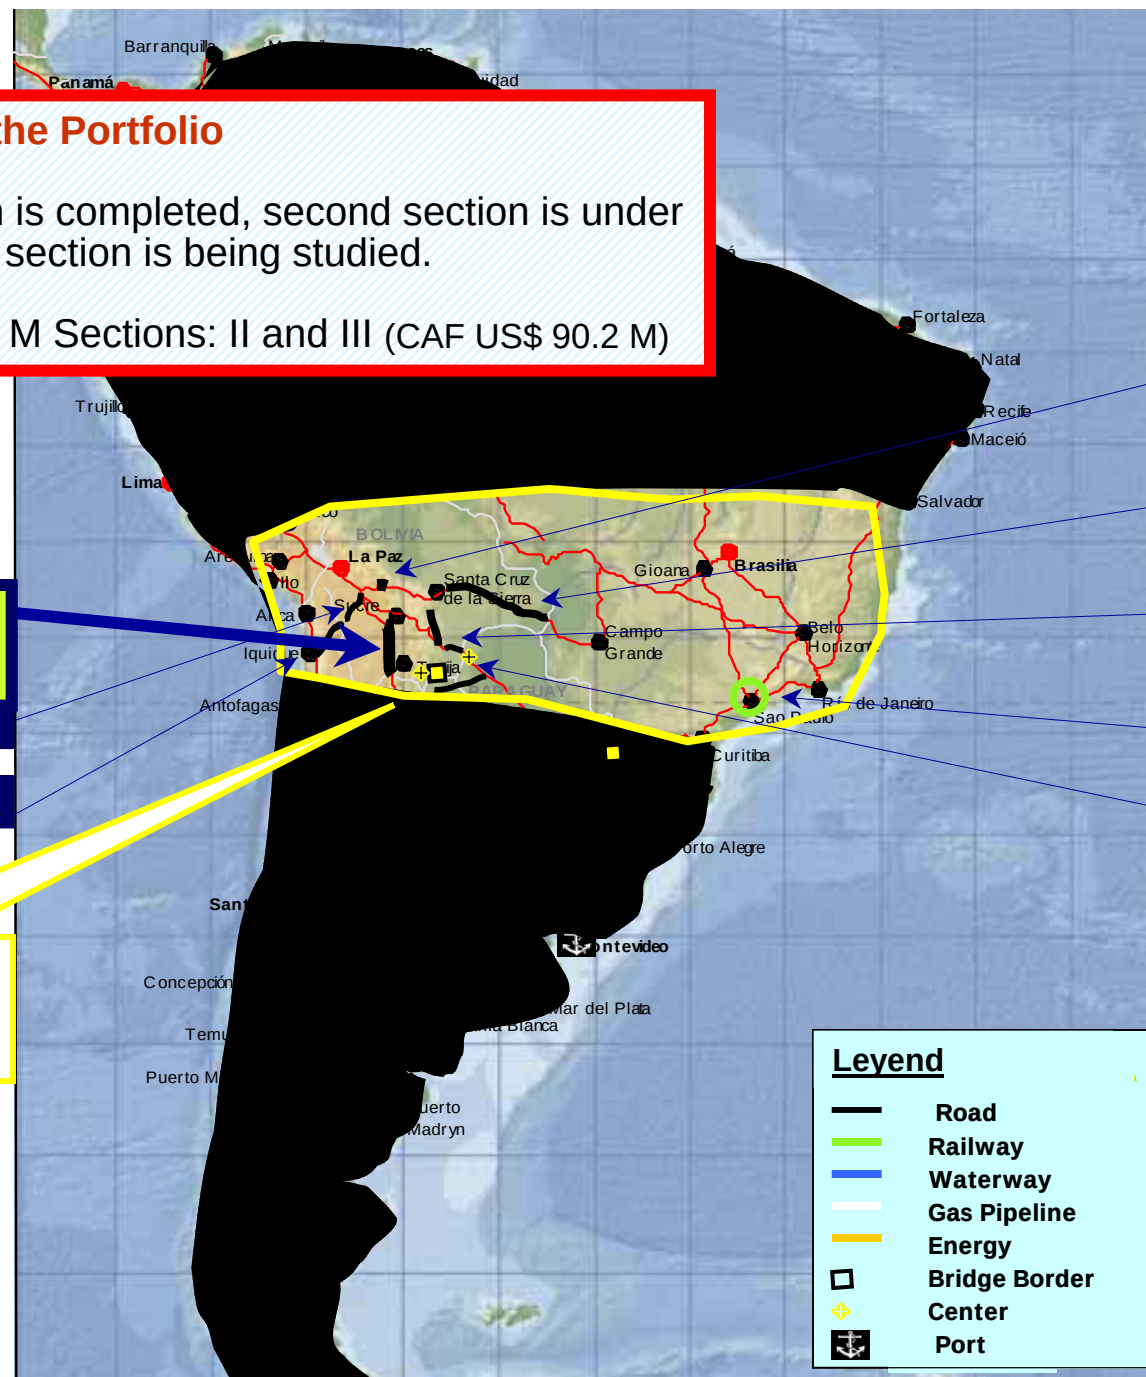

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Other Projects in the Portfolio

State: Completed.

Amount : US\$ 21 M

Railway Ring: Campo Grande

Road: Toledo - Pisiga

Refitting: Iquique - Colchane

Paving: Potosí - Tupiza -
Villazón

CENTRAL INTER-
OCEANIC HUB


Refitting Section: El
Sillar

Road: Pailón - Puerto
Suárez

Road: Cañada Oruro -
Villamontes

São Paulo Railway Ring

Border Center: Cañada
Oruro - Infante Rivarola

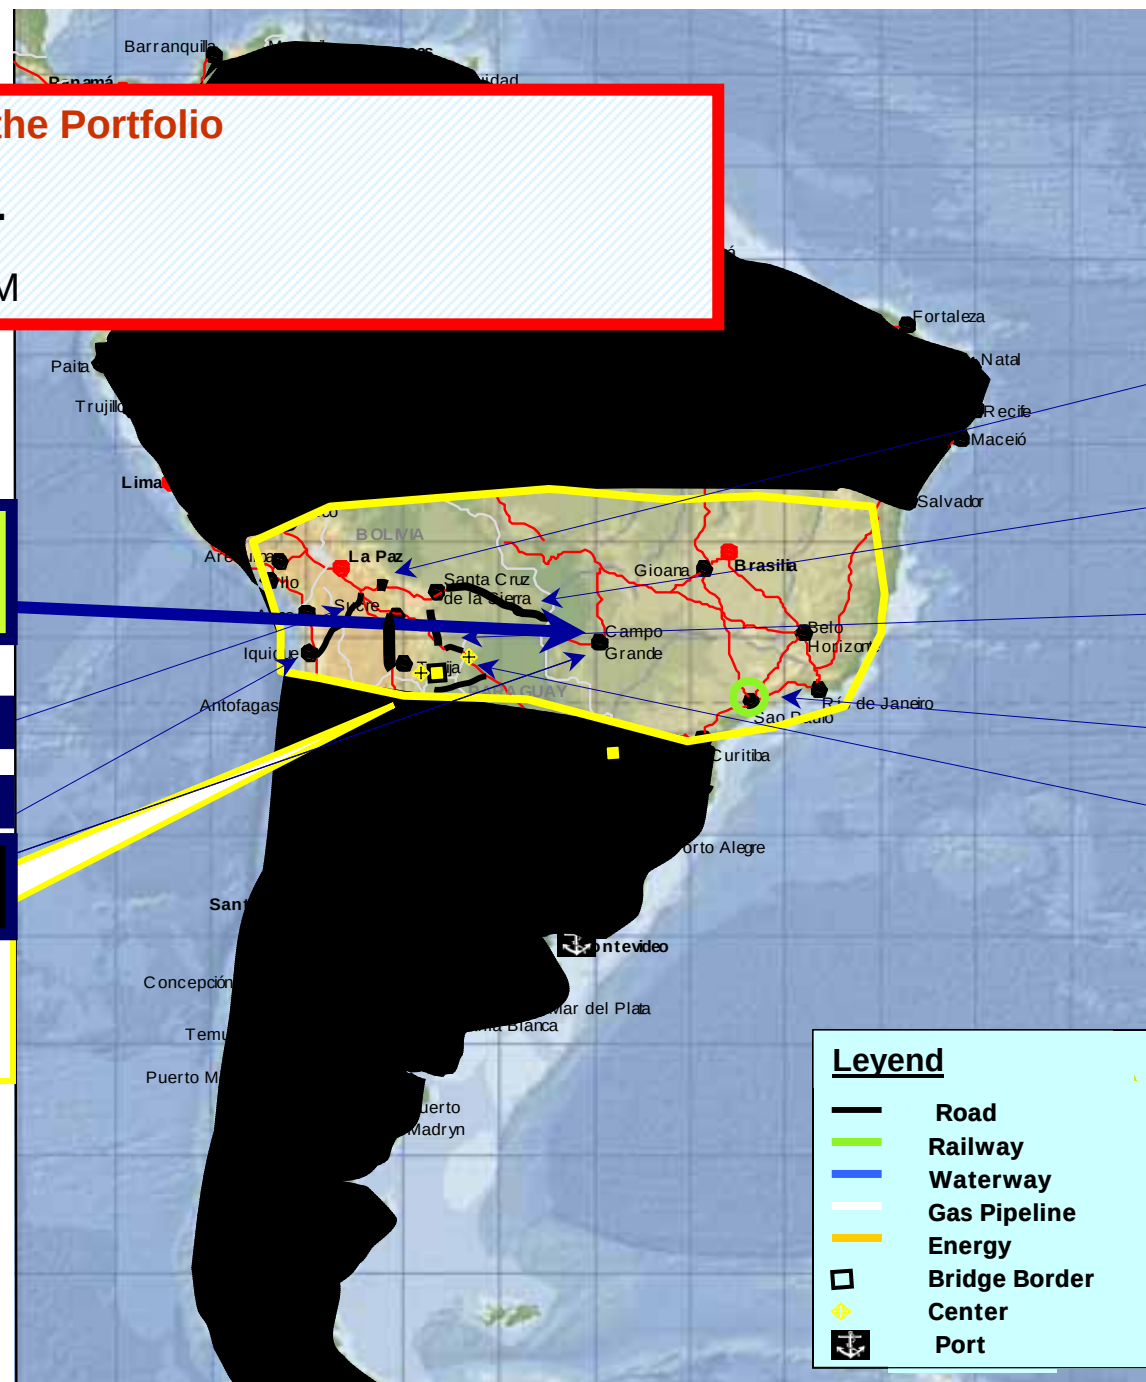

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Other Projects in the Portfolio

State: Execution. Own resources.

Amount : US\$ 2.4 M

**Road Loop:
Coruba**

Road Loop: Campo Grande

Railway Ring: Campo Grande

Road: Toledo - Pisiga

Refitting: Iquique - Colchane

**Paving: Potosí - Tupiza -
Villazón**

**CENTRAL INTER-
OCEANIC HUB**


**Refitting Section: El
Sillar**

**Road: Pailón - Puerto
Suárez**

**Road: Cañada Oruro -
Villamontes**

São Paulo Railway Ring

**Border Center: Cañada
Oruro -Infante Rivarola**

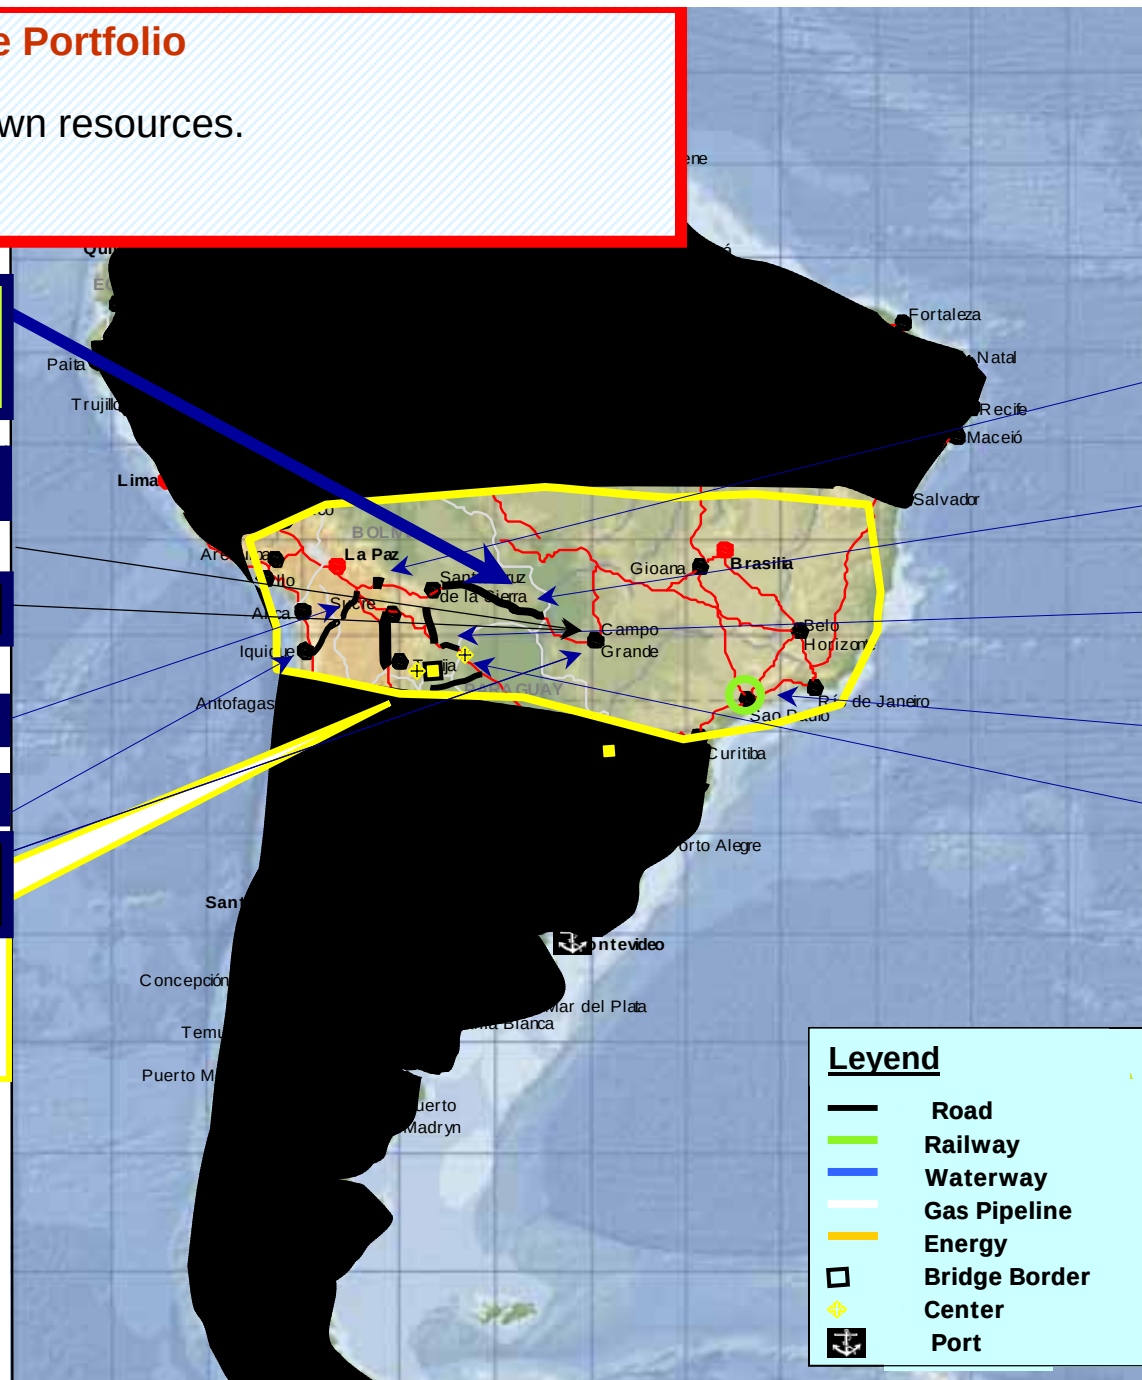

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Other Projects in the Portfolio

State: Execution. Own resources.

Amount : US\$ 41.4 M

Road Loop: Coruba

Road Loop: Campo Grande

Railway Ring: Campo Grande

Road: Toledo- Pisiga

Refitting: Iquique-Colchane

Paving: Potosí- Tupiza -
Villazón

CENTRAL INTER-
OCEANIC HUB

Railway: Campo
Grande -Bauru -
Santos


Refitting Section: El
Sillar

Road: Pailón - Puerto
Suárez

Road: Cañada Oruro -
Villamontes

São Paulo Railway Ring

Border Center: Cañada
Oruro -Infante Rivarola

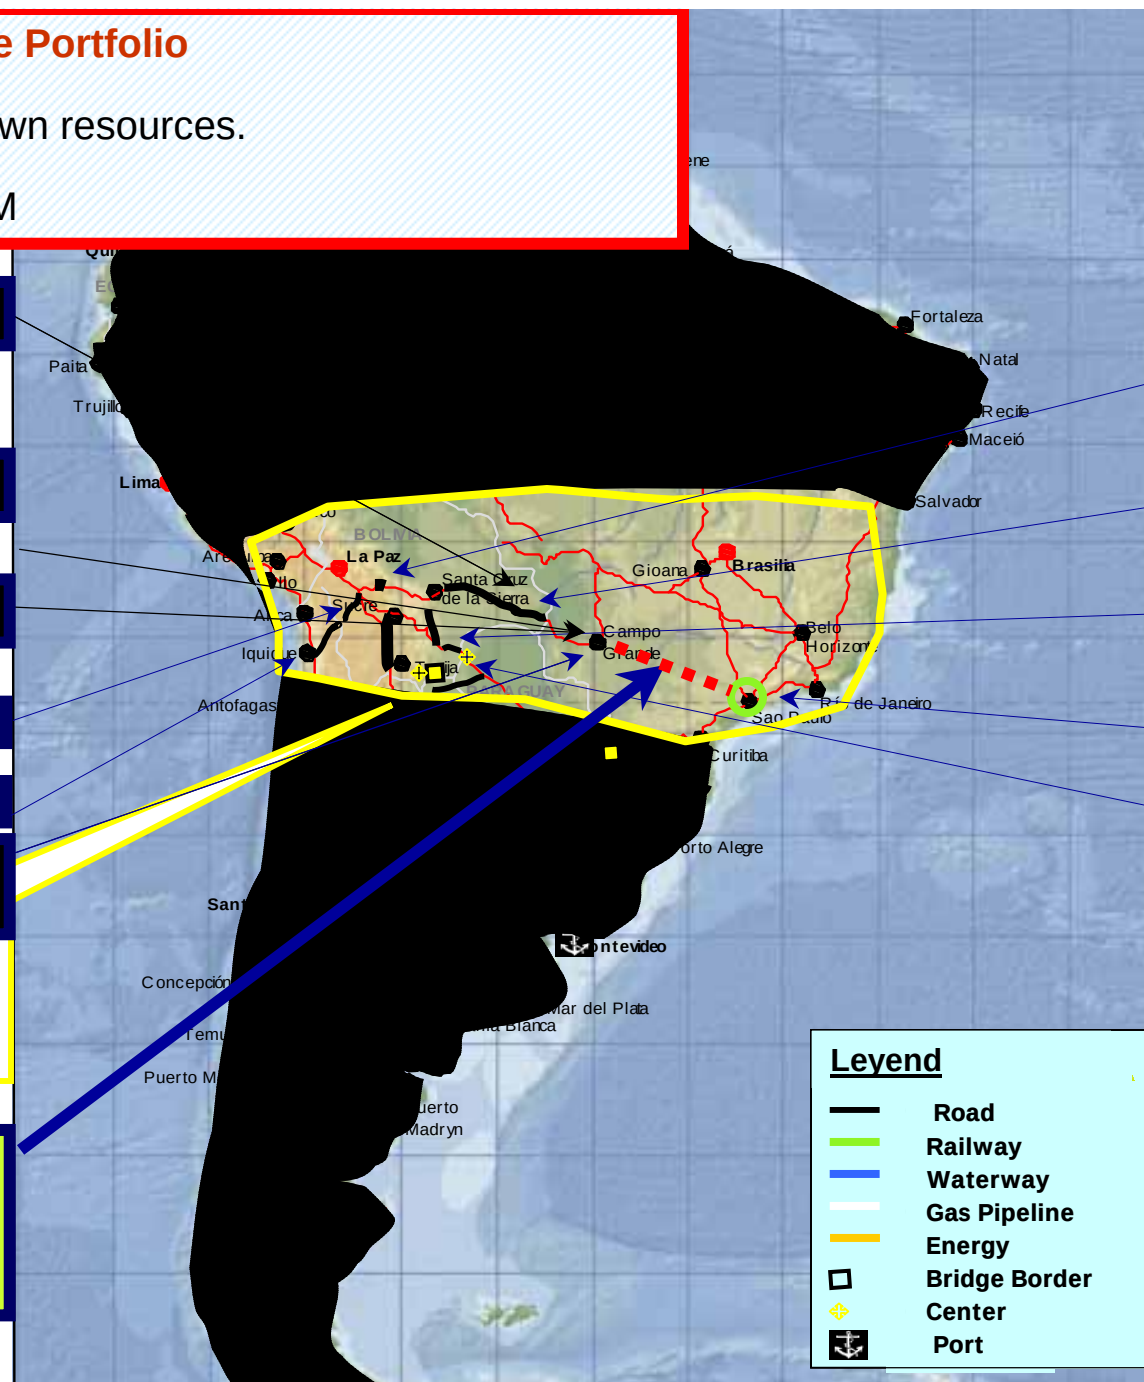

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Other Projects in the Portfolio

State: Execution. Own resources.

Amount : US\$ 63.9 M

Road Loop: Coruba

Road Loop: Campo Grande

Railway Ring: Campo Grande

Road: Toledo- Pisiga

Refitting: Iquique-Colchane

Paving: Potosí - Tupiza - Villazón

CENTRAL INTER-OCEANIC HUB

Railway: Campo Grande - Bauru - Santos

Railway: Curumba - Campo Grande


Refitting Section: El Sillar

Road: Pailón - Puerto Suárez

Road: Cañada Oruro - Villamontes

São Paulo Railway Ring

Border Center: Cañada Oruro - Infante Rivarola

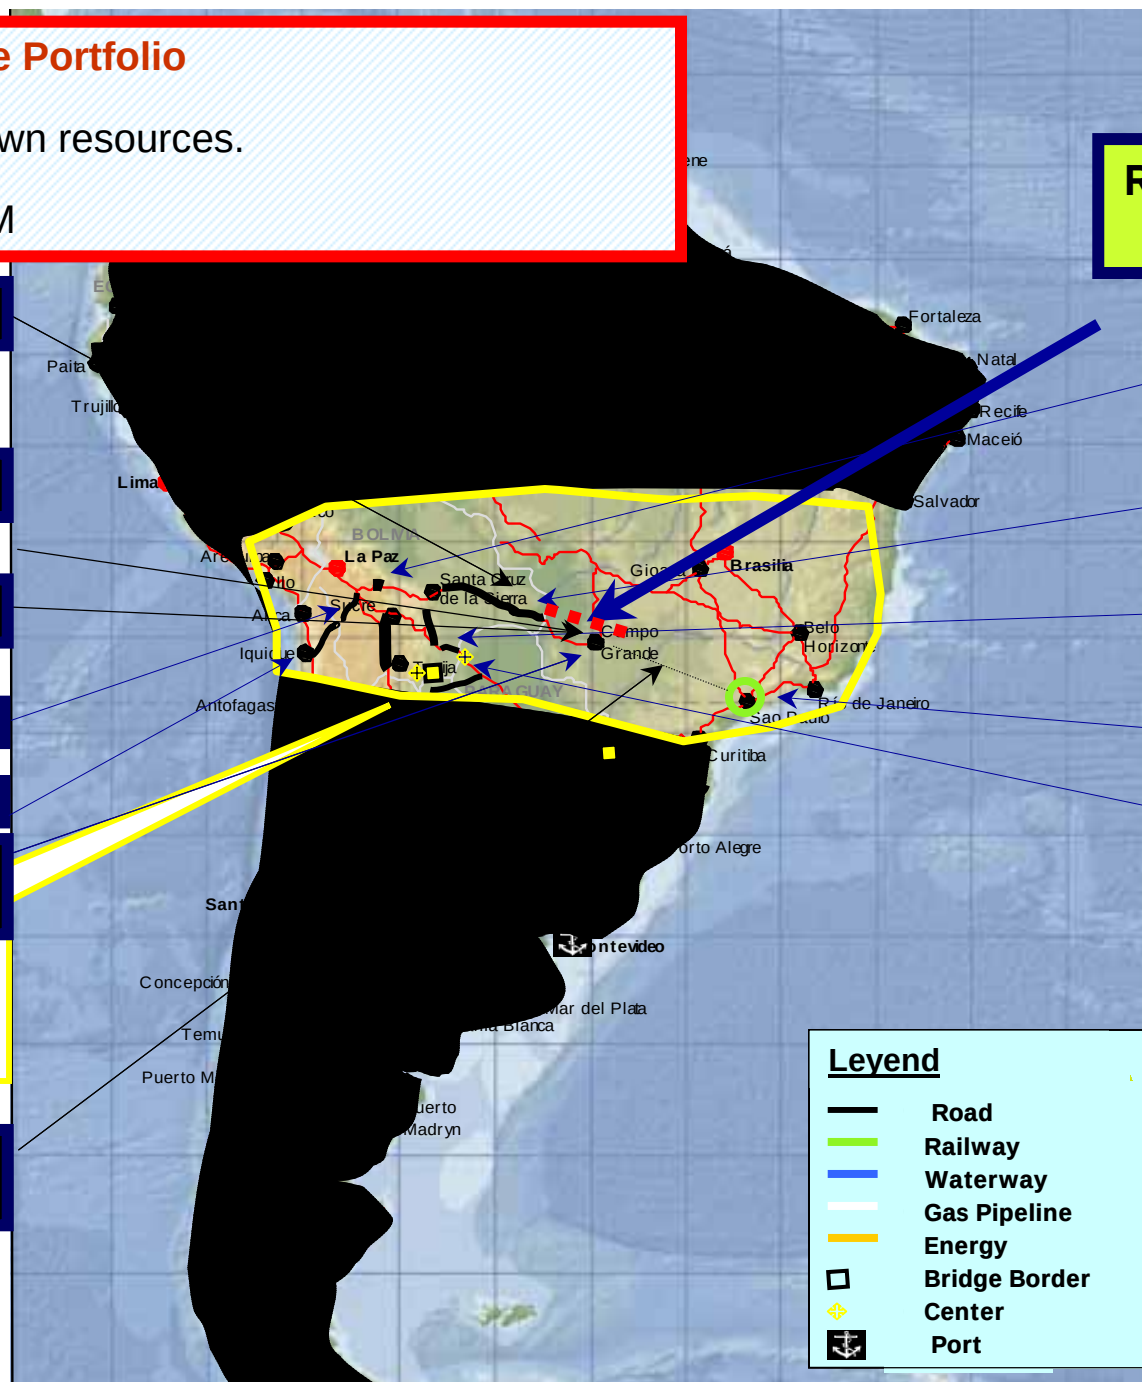

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Other Projects in the Portfolio

State: Execution.

Amount : US\$ 256 M

Road Loop: Coruba

Road Loop: Campo Grande

Railway Ring: Campo Grande

Road: Toledo- Pisiga

Refitting: Iquique-Colchane

Paving: Potosí- Tupiza -
Villazón

CENTRAL INTER-
OCEANIC HUB

Railway: Campo Grande -
Bauru-Santos

Road: Concepción
San Matias

Railway: Curumba - Campo
Grande


Refitting Section: El
Sillar

Road: Pailón - Puerto
Suárez

Road: Cañada Oruro -
Villamontes

São Paulo Railway Ring

Border Center: Cañada
Oruro -Infante Rivarola

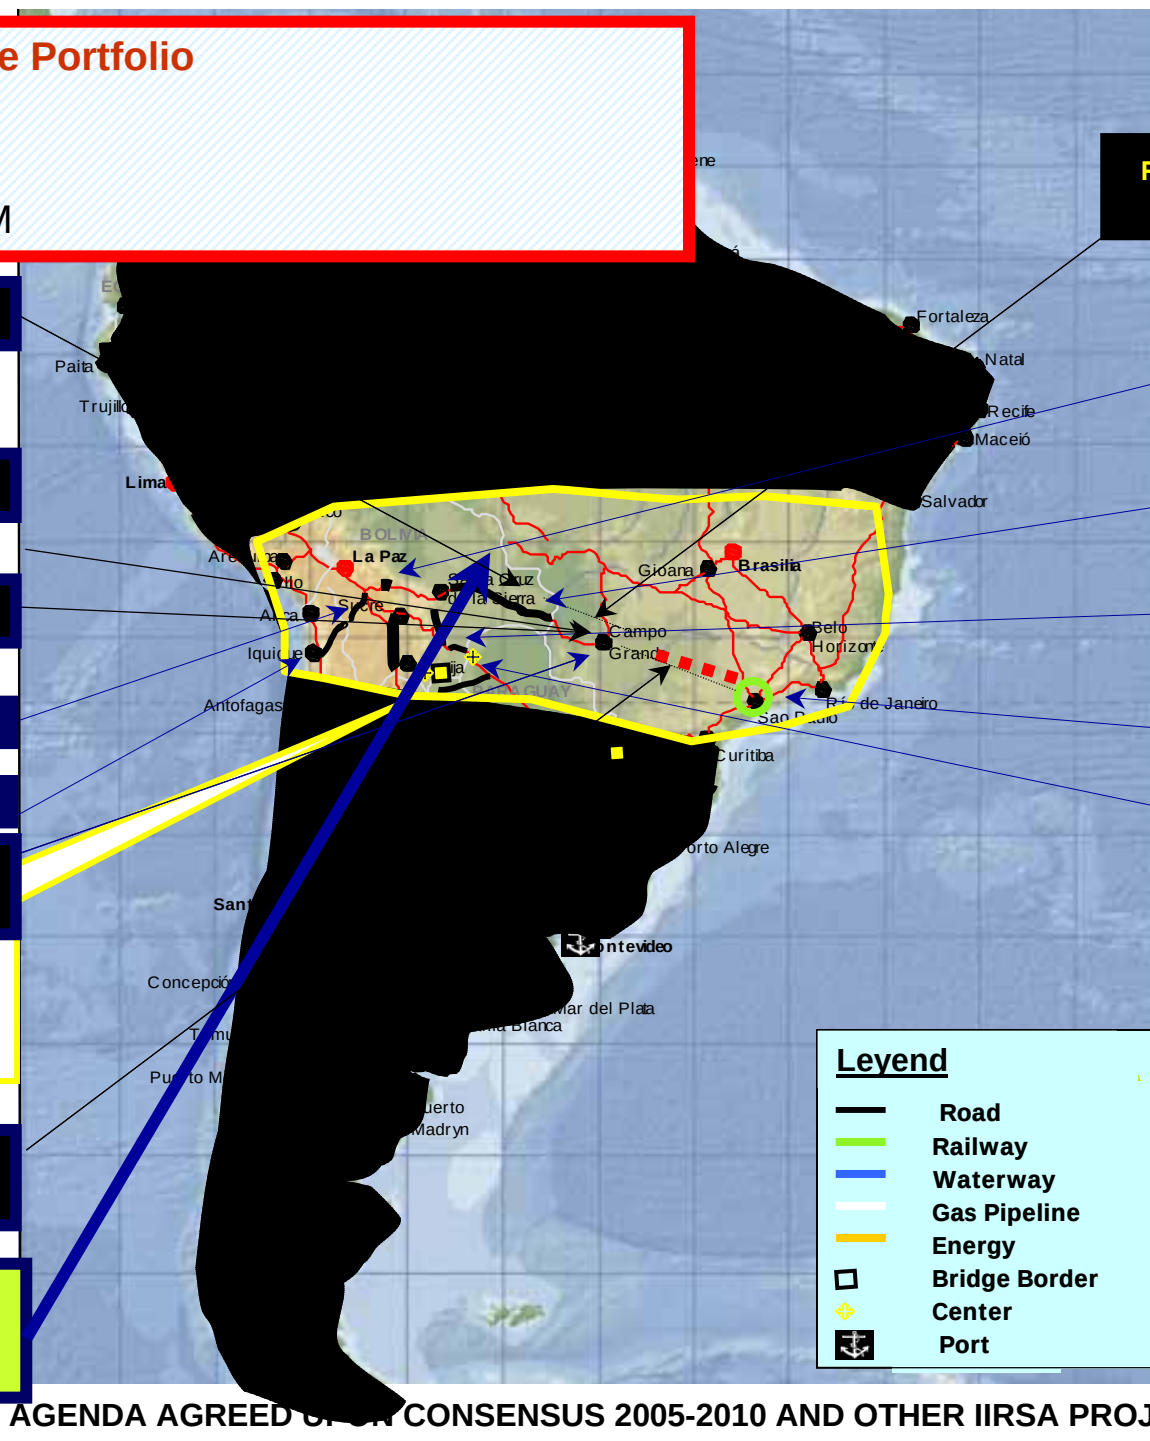

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Other Projects in the Portfolio

State: Execution.

Amount : US\$ 2 M

Road Loop: Coruba

Road Loop: Campo Grande

Railway Ring: Campo Grande

Road: Toledo- Pisiga

Refitting: Iquique-Colchane

Paving: Potosí- Tupiza -
Villazón

CENTRAL INTER-
OCEANIC HUB

Railway: Campo Grande -
Bauru-Santos

Road: Concepción San Matias

Railway. Curumba - Campo
Grande

Border Crossing:
Pisiga - Colchane


Refitting Section: El
Sillar

Road: Pailón - Puerto
Suárez

Road: Cañada Oruro -
Villamontes

São Paulo Railway Ring

Border Center: Cañada
Oruro -Infante Rivarola

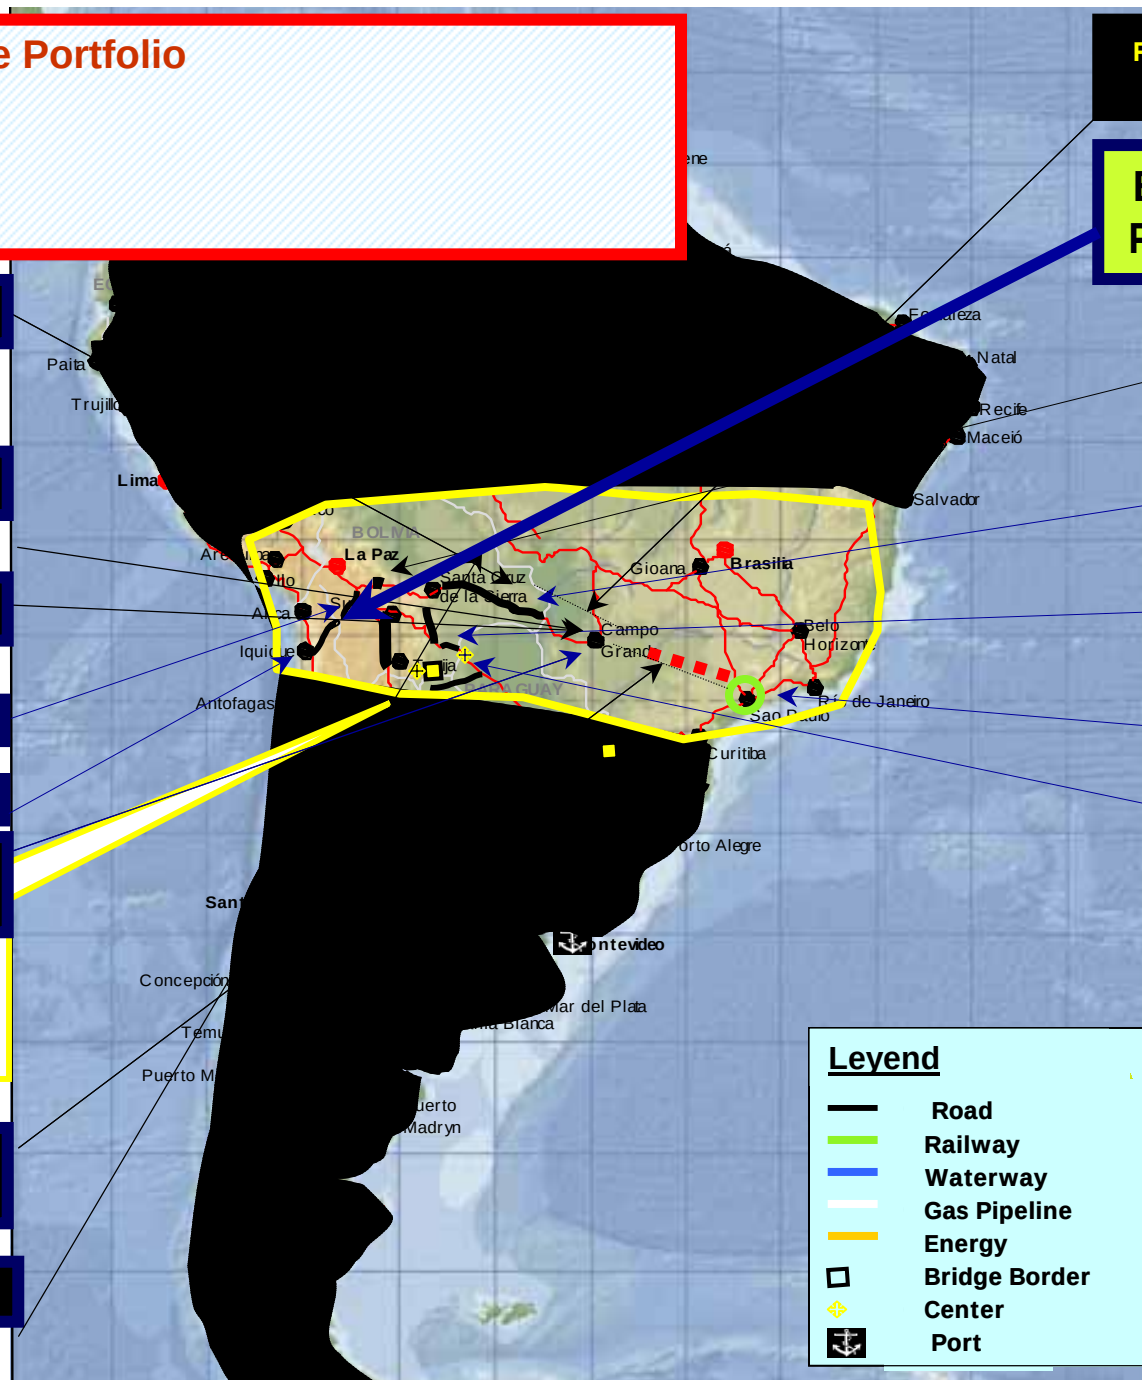

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Other Projects in the Portfolio

State: Completed (2 Improvement and Concession Proj.)

Amount : US\$ 60 M Private Financing.

Road Loop: Coruba

Road Loop: Campo Grande

Railway Ring: Campo Grande

Road: Toledo- Pisiga

Refitting: Iquique-Colchane

Paving: Potosí- Tupiza-
Villazón

CENTRAL INTER-
OCEANIC HUB

Railway: Campo Grande -
Bauru-Santos

Road: Concepción San Matias

Railway: Curumba - Campo
Grande

Border Crossing: Pisiga -
Colchane


Improvement and
Concession of
Arica Port

Road: Pailón - Puerto
Suárez

Road: Cañada Oruro -
Villamontes

São Paulo Railway Ring

Border Center: Cañada
Oruro -Infante Rivarola

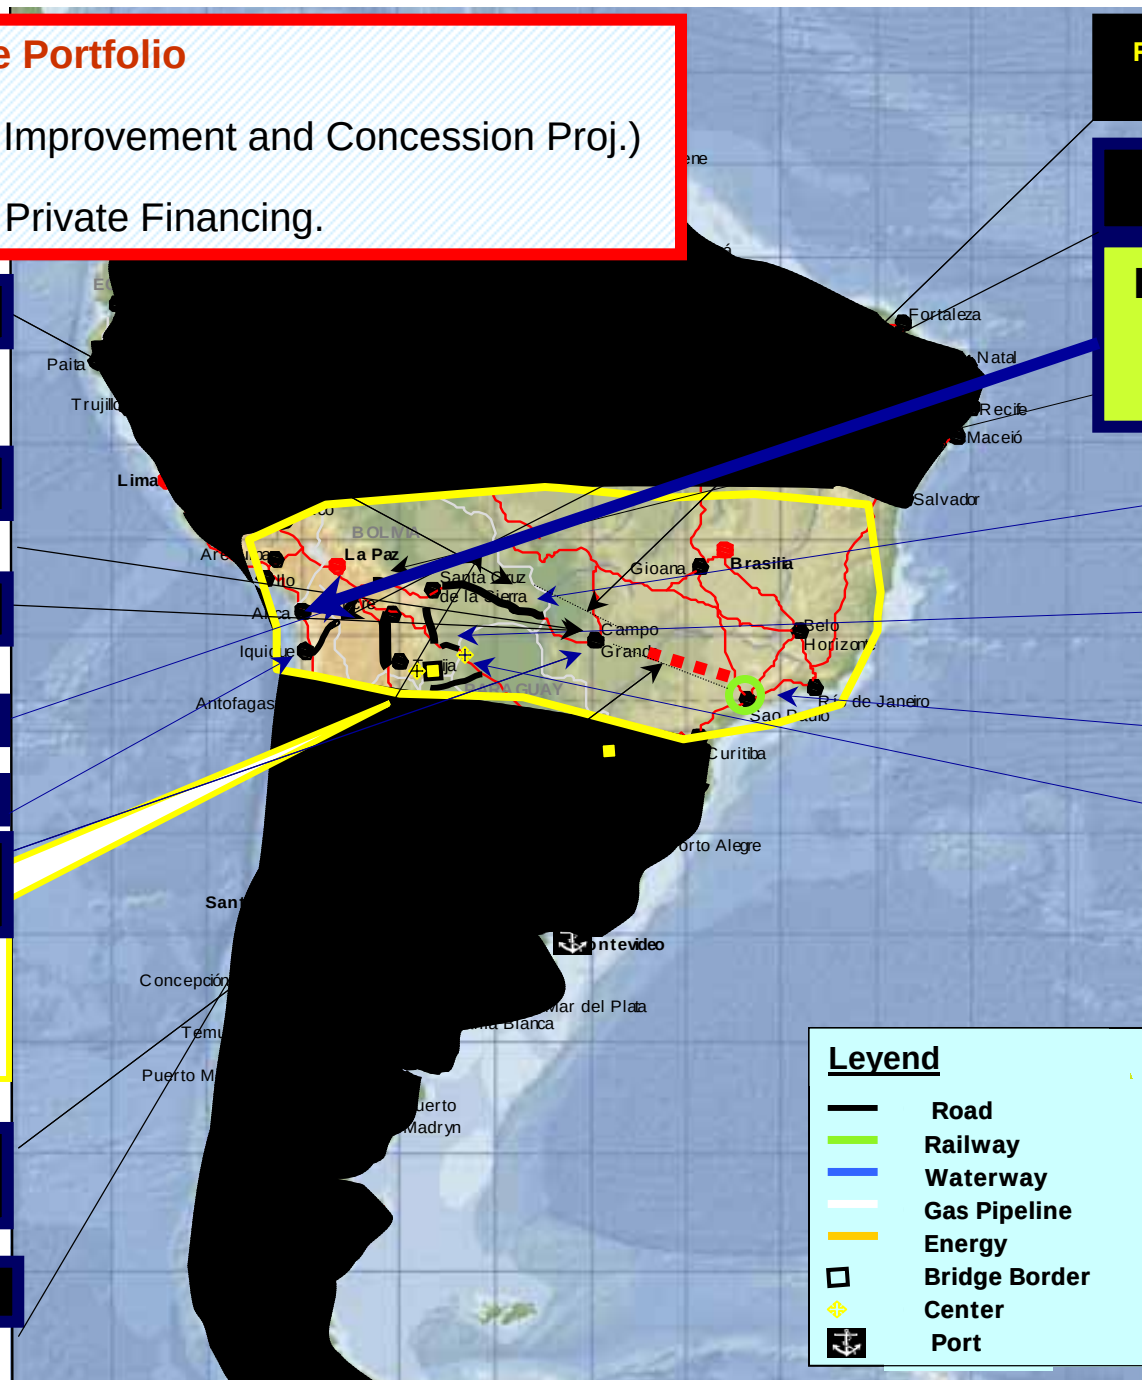

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Other Projects in the Portfolio

State: Execution.

Amount : US\$ 37 M Public Investment.

Road Loop: Coruba

Road Loop: Campo Grande

Railway Ring: Campo Grande

Road: Toledo- Pisiga

Refitting: Iquique-Colchane

**Paving: Potosí- Tupiza-
Villazón**

**CENTRAL INTER-
OCEANIC HUB**

**Railway: Campo Grande -
Bauru-Santos**

Road: Concepción San Matias

**Railway: Curumba - Campo
Grande**

**Border Crossing: Pisiga -
Colchane**

**Improvement and
Concession of Arica Port**

**Refitting Section: El
Sillar**


**Road: Pailón - Puerto
Suárez**

**Road: Cañada Oruro -
Villamontes**

São Paulo Railway Ring

**Border Center: Cañada
Oruro -Infante Rivarola**

**Refitting Road:
Pisiga - Colchane**

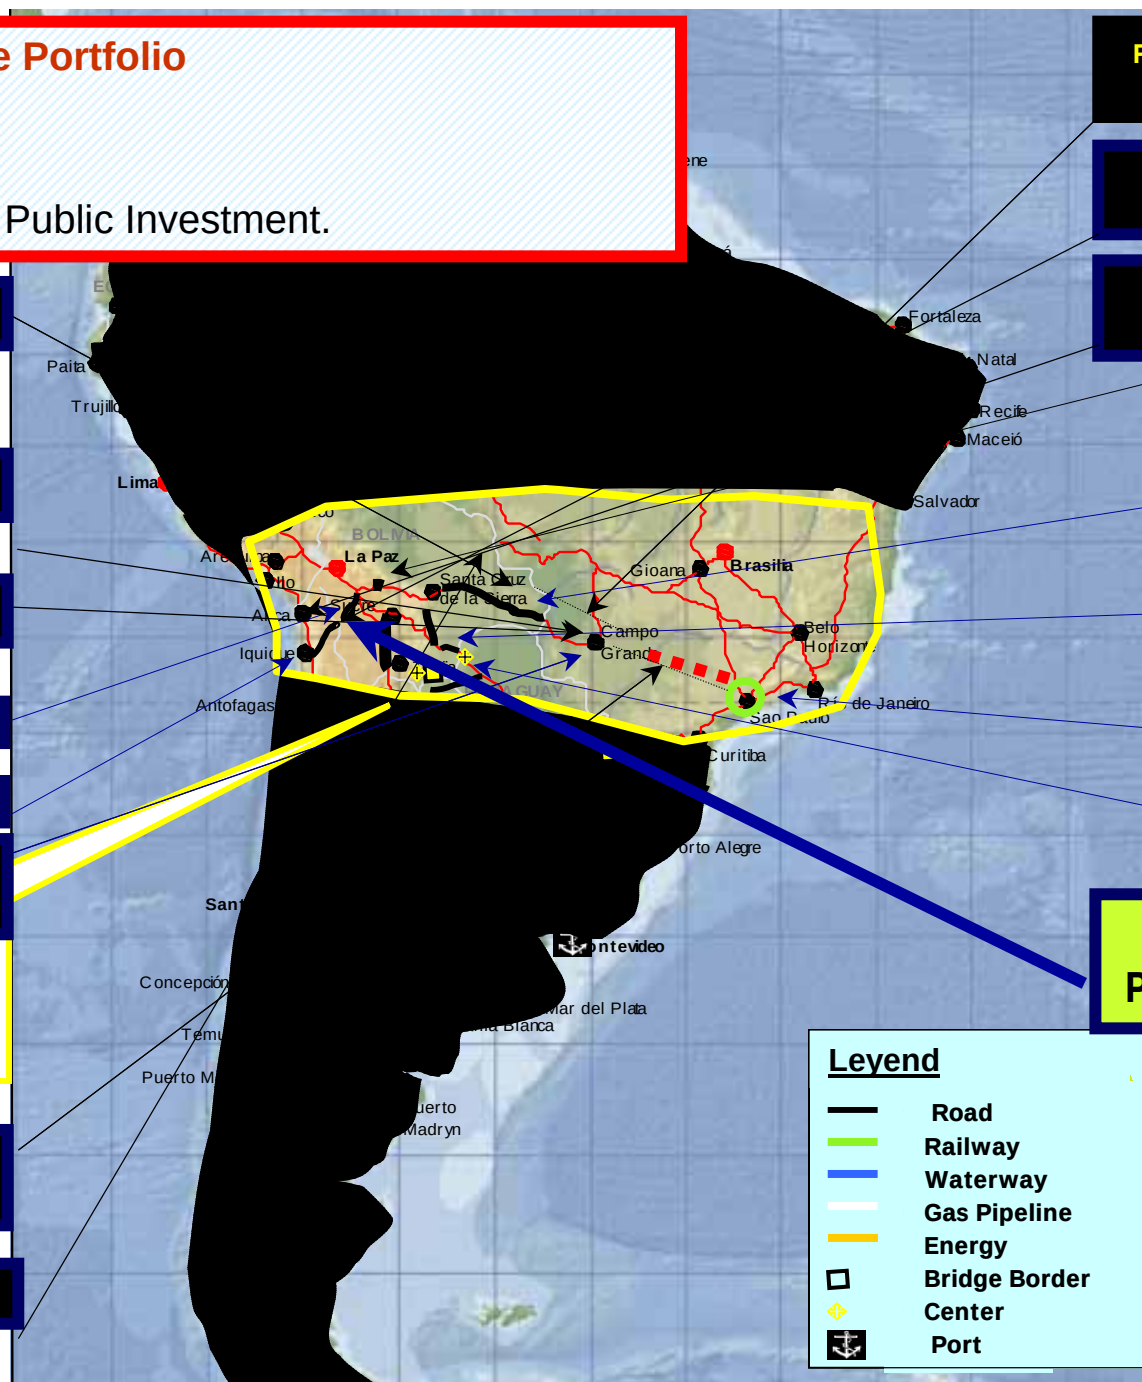

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Other Projects in the Portfolio

State: Execution, completion planned: 2008

Amount : US\$ 36.6 M (CAF and BM).

Road Loop: Coruba

Road Loop: Campo Grande

Railway Ring: Campo Grande

Road: Toledo- Pisiga

Refitting: Iquique-Colchane

Paving: Potosí- Tupiza- Villazón

CENTRAL INTER-OCEANIC HUB

Road: Campo Grande - Bauru-Santos

Road: Concepción San Matias

Railway: Curumba - Campo Grande

Border Crossing: Pisiga - Colchane

Improvement and Concession of Arica Port

Refitting Section: El Sillar

Road: Pailón - Puerto Suárez


Road: Cañada Oruro - Villamontes

São Paulo Railway Ring

Border Center: Cañada Oruro -Infante Rivarola

Refitting Road: Pisiga - Colchane

Paving Road: Antigua Santa Cruz - Cochabamba

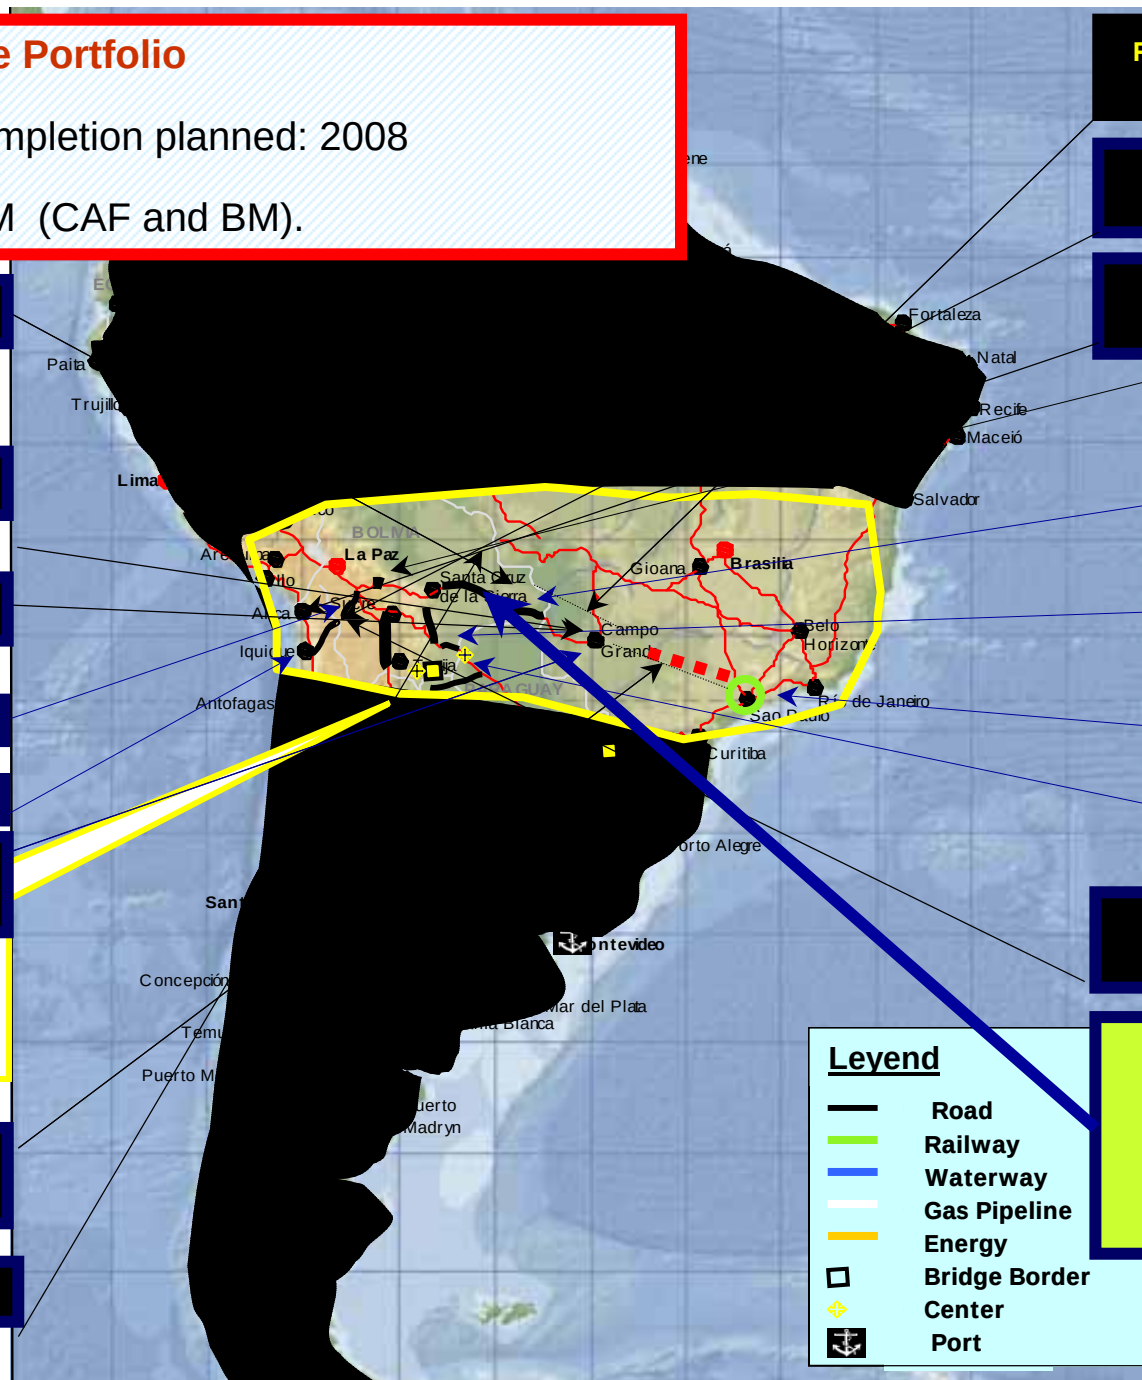

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Other Projects in the Portfolio

State: Completed.

Amount : US\$ 3.1 M (Proj. New Bridge) Fin. by Japan.

Road Loop: Coruba

Road Loop: Campo Grande

Railway Ring: Campo Grande

Road: Toledo- Pisiga

Refitting: Iquique-Colchane

Paving: Potosí-Tupiza-Villazón

CENTRAL INTER-OCEANIC HUB

Railway: Campo Grande - Bauru-Santos

Road: Concepción San Matías

Railway: Curumba - Campo Grande

Border Crossing: Pisiga - Colchane

Improvement and Concession of Arica Port

Refitting Section: El Sillar

Road: Pailón - Puerto Suárez

Road: Cañada Oruro - Villamontes


São Paulo Railway Ring

Border Center: Cañada Oruro -Infante Rivarola

Refitting Road: Pisiga - Colchane

Paving Road: Antigua Santa Cruz - Cochabamba

Refitting: Puente de la Amistad

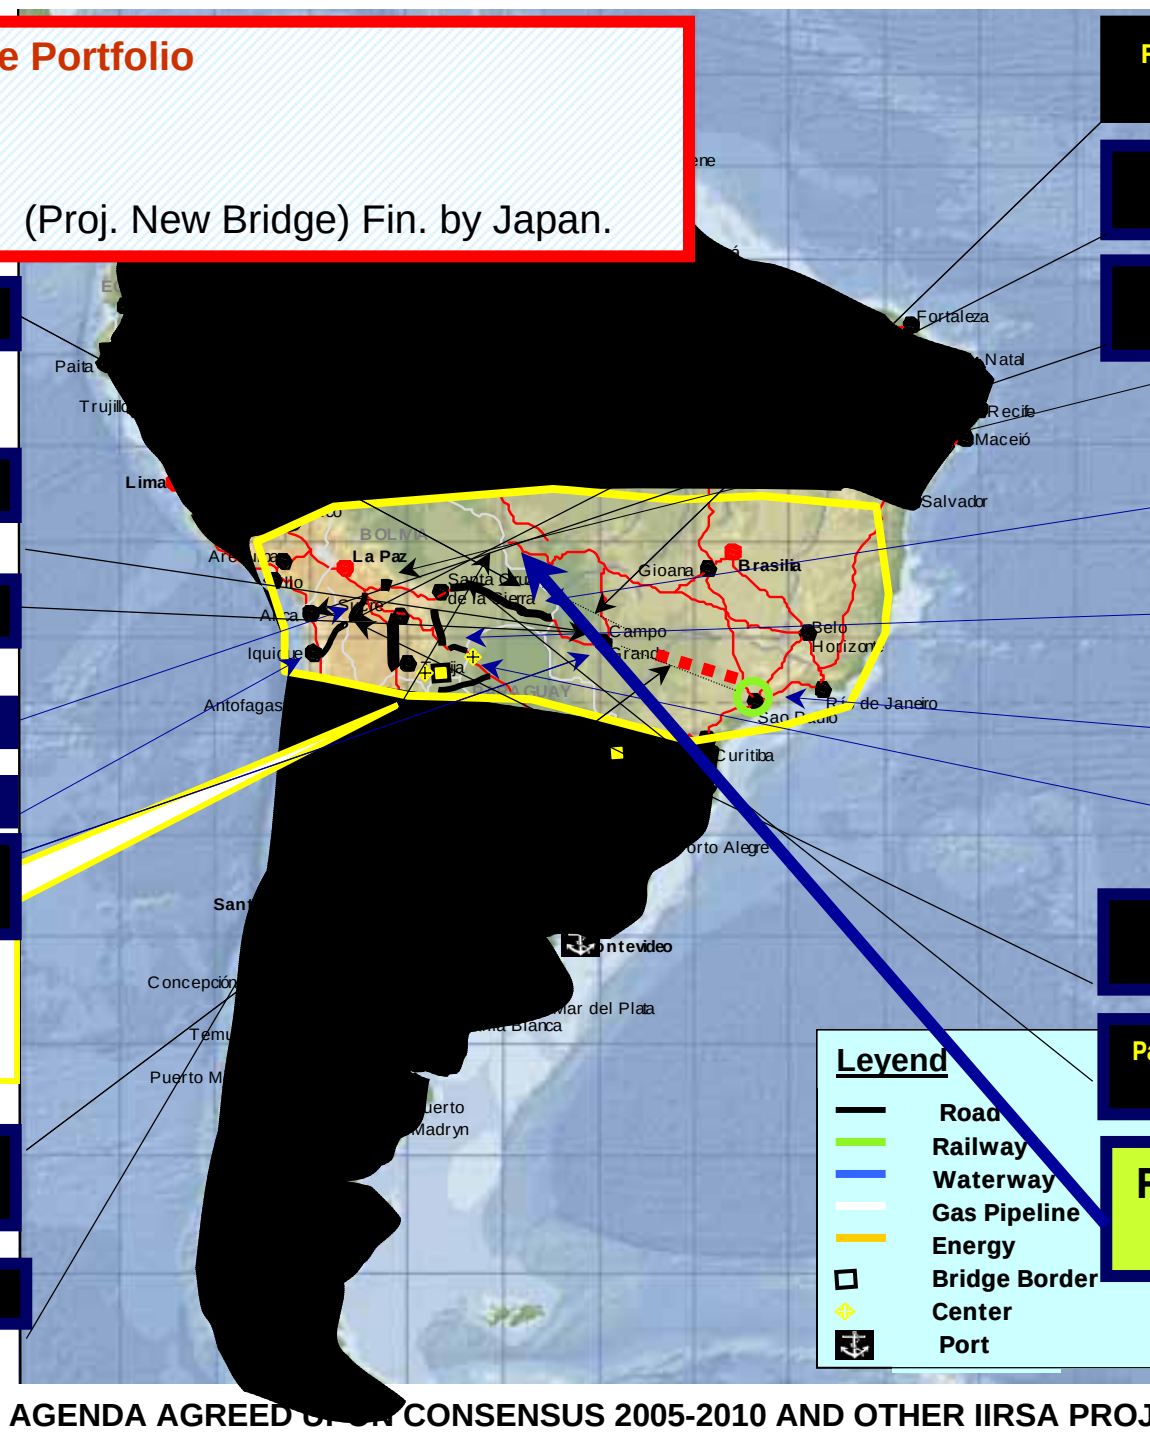

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Other Projects in the Portfolio

State: Tender Process.

Amount : US\$ 104.3 M. Private Financing.

Road Loop: Coruba

Road Loop: Campo Grande

Railway Ring: Campo Grande

Road: Toledo- Pisiga

Refitting: Iquique-Colchane

Paving: Potosí-Tupiza-Villazón

CENTRAL INTER-OCEANIC HUB

Railway: Campo Grande - Bauru-Santos

Road: Concepción San Matias

Railway: Curumba - Campo Grande

Border Crossing: Pisiga - Colchane

Improvement and Concession of Arica Port

Refitting Section: El Sillar

Road: Pailón - Puerto Suárez

Road: Cañada Oruro - Villamontes

São Paulo Railway Ring

Border Center: Cañada Oruro -Infante Rivarola

Refitting Road: Pisiga - Colchane

Paving Road: Antigua Santa Cruz - Cochabamba

Refitting: Puente de la Amistad

Modernization of Ilo Port and Improvement of Matarani Port

Legend

- Road
- Railway
- Waterway
- Gas Pipeline
- Energy
- Bridge Border
- + Center
- ⚓ Port

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Total of Projects: 22

- AIC - 7
- Rest of the IIRSA Portfolio - 15

Road Loop: Coruba

Road Loop: Campo Grande

Railway Ring: Campo Grande

Road: Toledo - Pisiga

Refitting: Iquique - Colchane

Paving: Potosí - Tupiza - Villazón

CENTRAL INTER-OCEANIC HUB

Railway: Campo Grande - Bauru - Santos

Road: Concepción San Matias

Railway: Curumba - Campo Grande

Border Crossing: Pisiga - Colchane

Improvement and Concession of Arica Port

Refitting Section: El Sillar

Road: Pailón - Puerto Suárez

Road: Cañada Oruro - Villamontes

São Paulo Railway Ring


Border Center: Cañada Oruro - Infante Rivarola

Refitting Road: Pisiga - Colchane


Paving Road: Antigua Santa Cruz - Cochabamba

Refitting: Puente de la Amistad

Modernization of Ilo port and Improvement of Matarani port

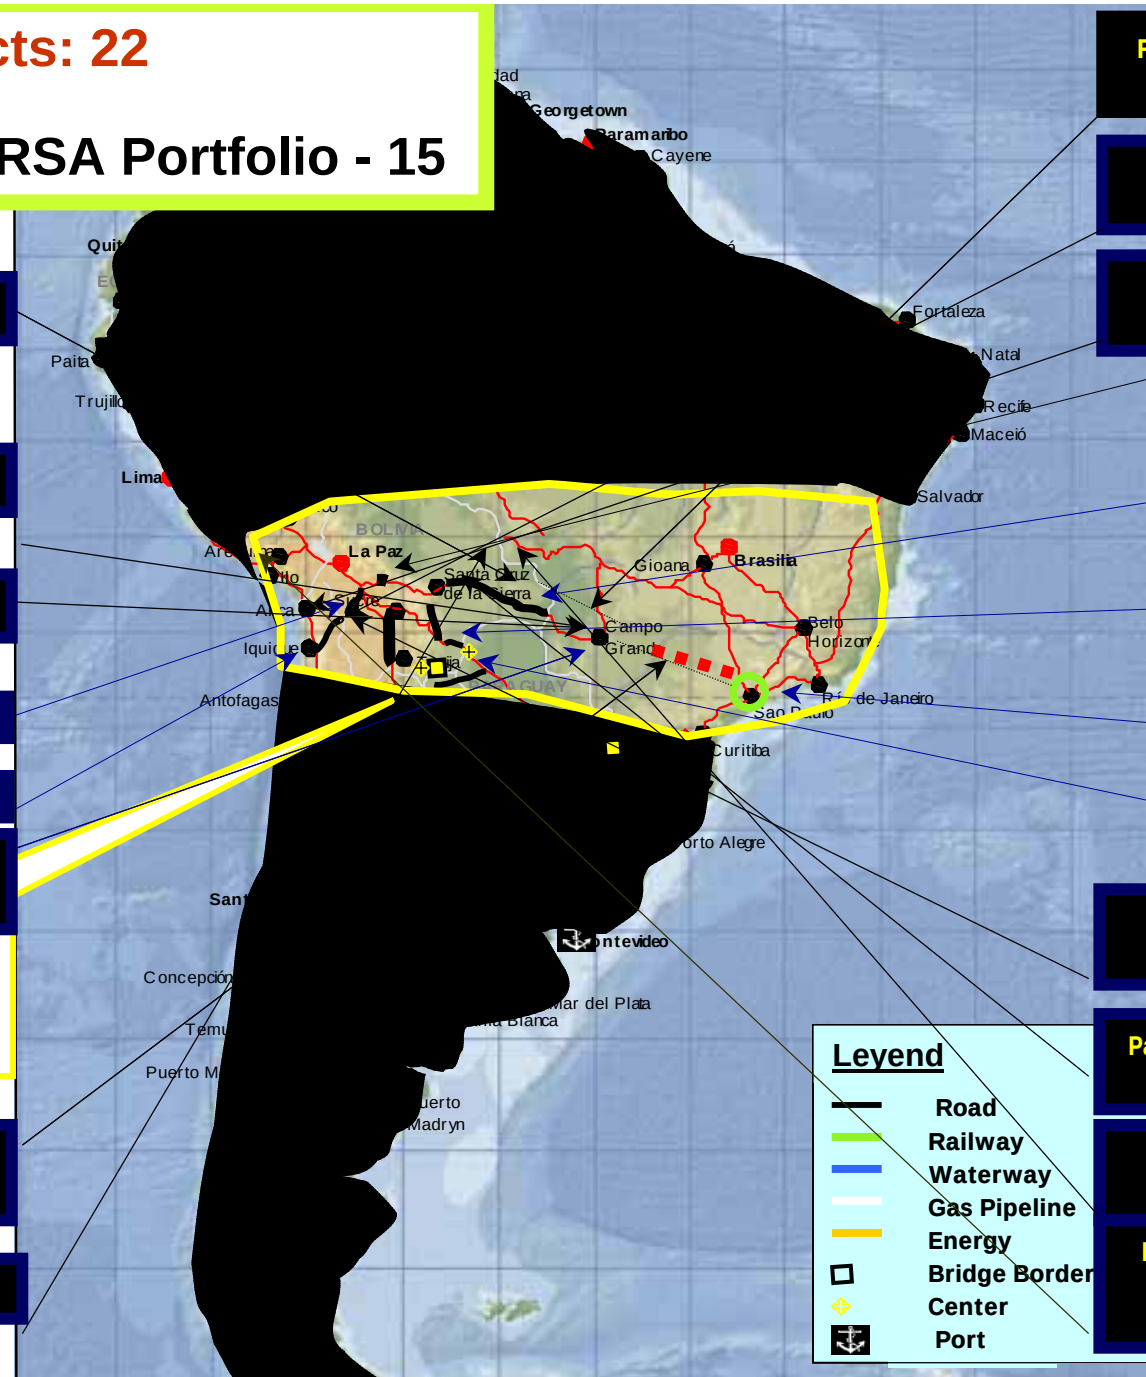

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

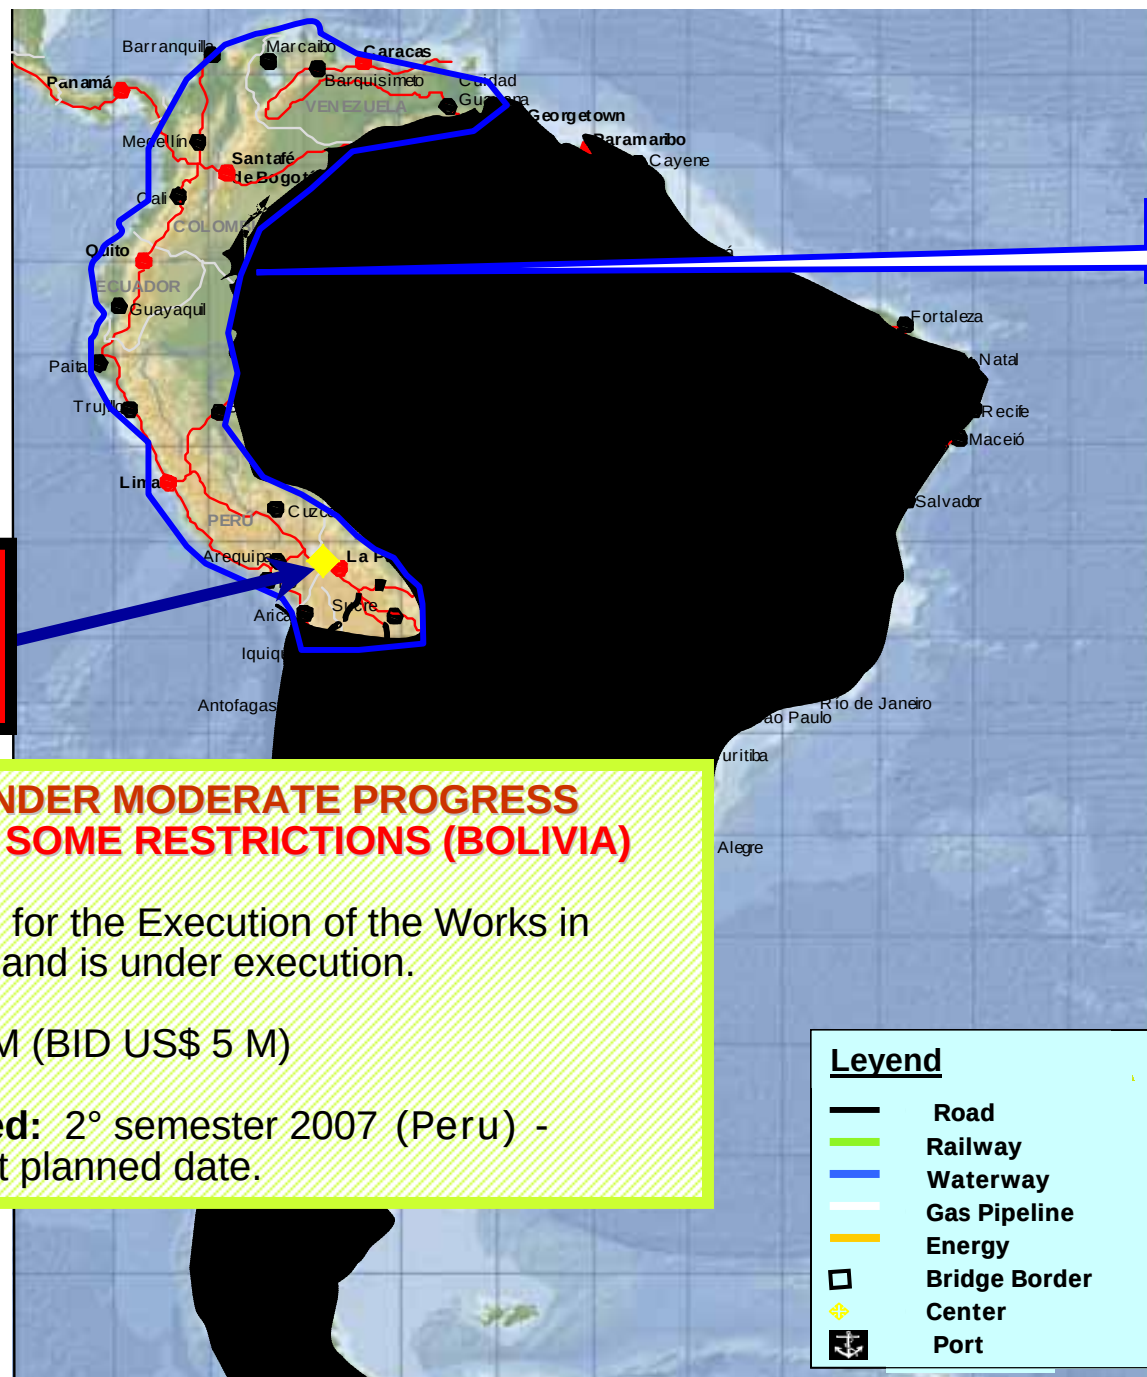

ANDEAN HUB


**AIC 17 - Border
Center:
Desaguadero**

**AIC – PROJECT UNDER MODERATE PROGRESS
(PERU) AND WITH SOME RESTRICTIONS (BOLIVIA)**

State: The BID loan for the Execution of the Works in Peru was approved and is under execution.

Amount : US\$ 7.5 M (BID US\$ 5 M)

Completion planned: 2° semester 2007 (Peru) - Bolivian side without planned date.

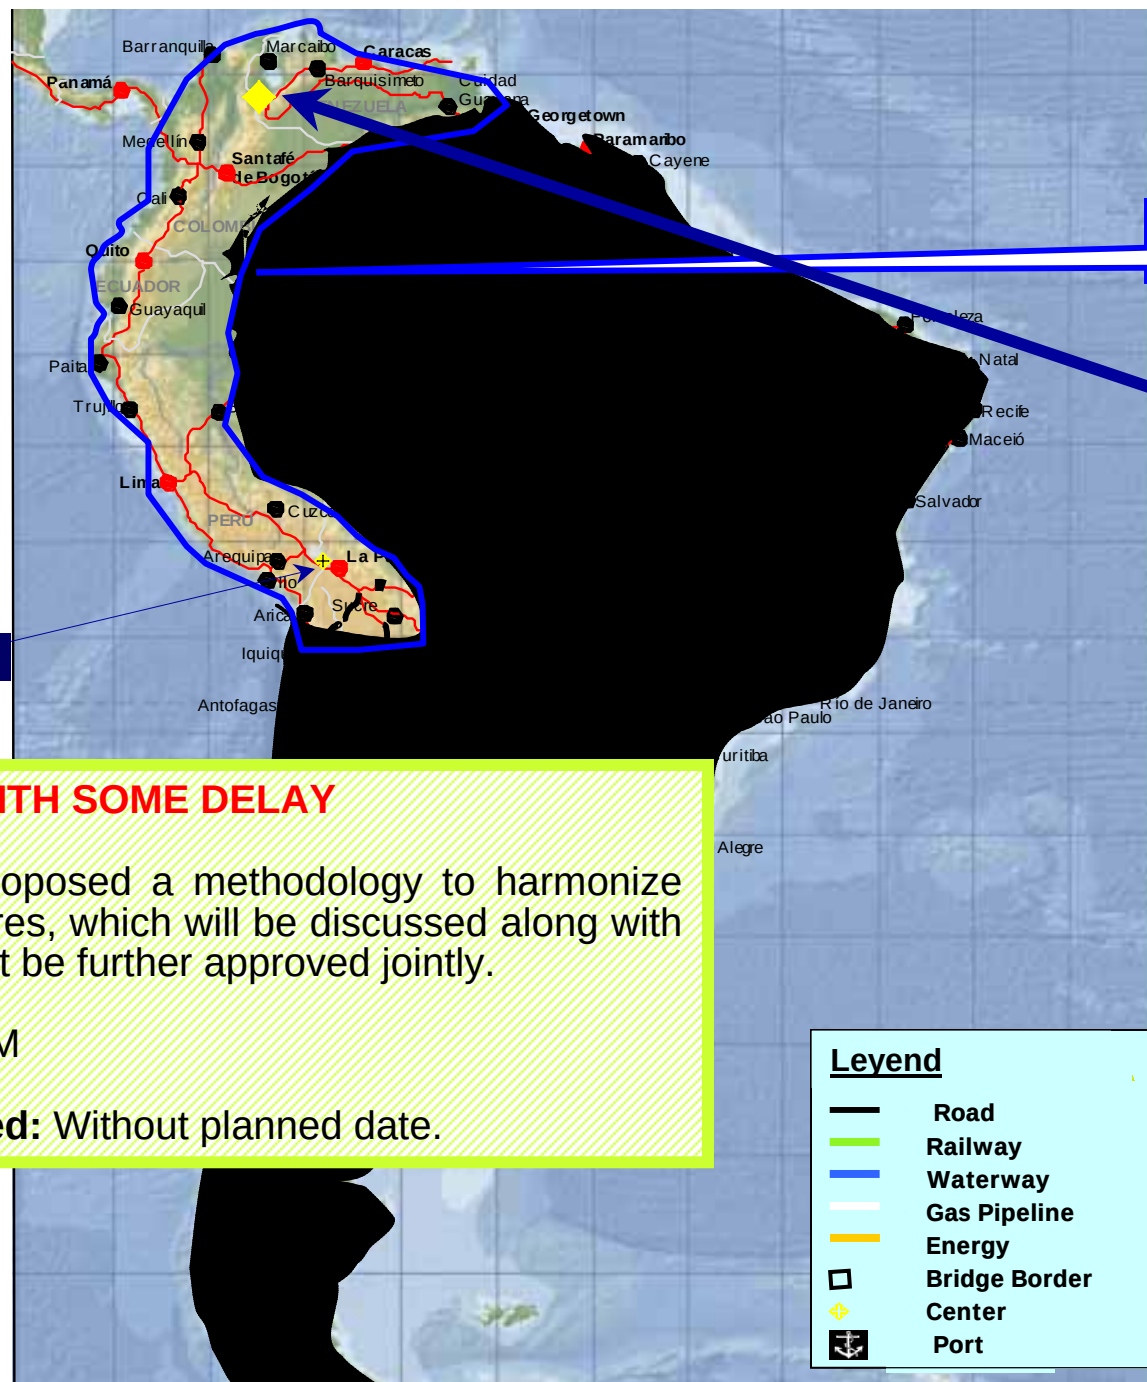

ANDEAN HUB

**AIC 18 -
Border
Center:
Cúcuta-San
Antonio**

Border Center: Desaguadero

AIC – PROJECT WITH SOME DELAY

State: Colombia proposed a methodology to harmonize the control procedures, which will be discussed along with Venezuela and must be further approved jointly.

Amount: US\$ 2.0 M

Completion planned: Without planned date.

AIC 19 - Navigability Meta River

Border Center: Cúcuta-
San Antonio

ANDEAN HUB

Border Center: Desaguadero

AIC – PROJECT UNDER MODERATE PROGRESS (COLOMBIA) AND WITH SOME RESTRICTIONS (VENEZUELA)

State: Under development (Colombia) and being analyzed by the Venezuelan government

Amount: US\$ 108 M

Completion planned: November 2009 (Colombia) – without definition (Venezuela).

Legend

- Road
- Railway
- Waterway
- Gas Pipeline
- Energy
- Bridge Border
- ◆ Center
- ⚓ Port

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

**Connection: Cúcuta
- Maracaibo**

**Border Center: Cúcuta-
San Antonio**

ANDEAN HUB

Border Center: Desaguadero

Other Projects in the Portfolio


State: Development.

Amount : US\$ 20 M (CAF US\$ 11 M)

Legend

- Road
- Railway
- Waterway
- Gas Pipeline
- Energy
- Bridge Border
- ◆ Center
- ⚓ Port

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

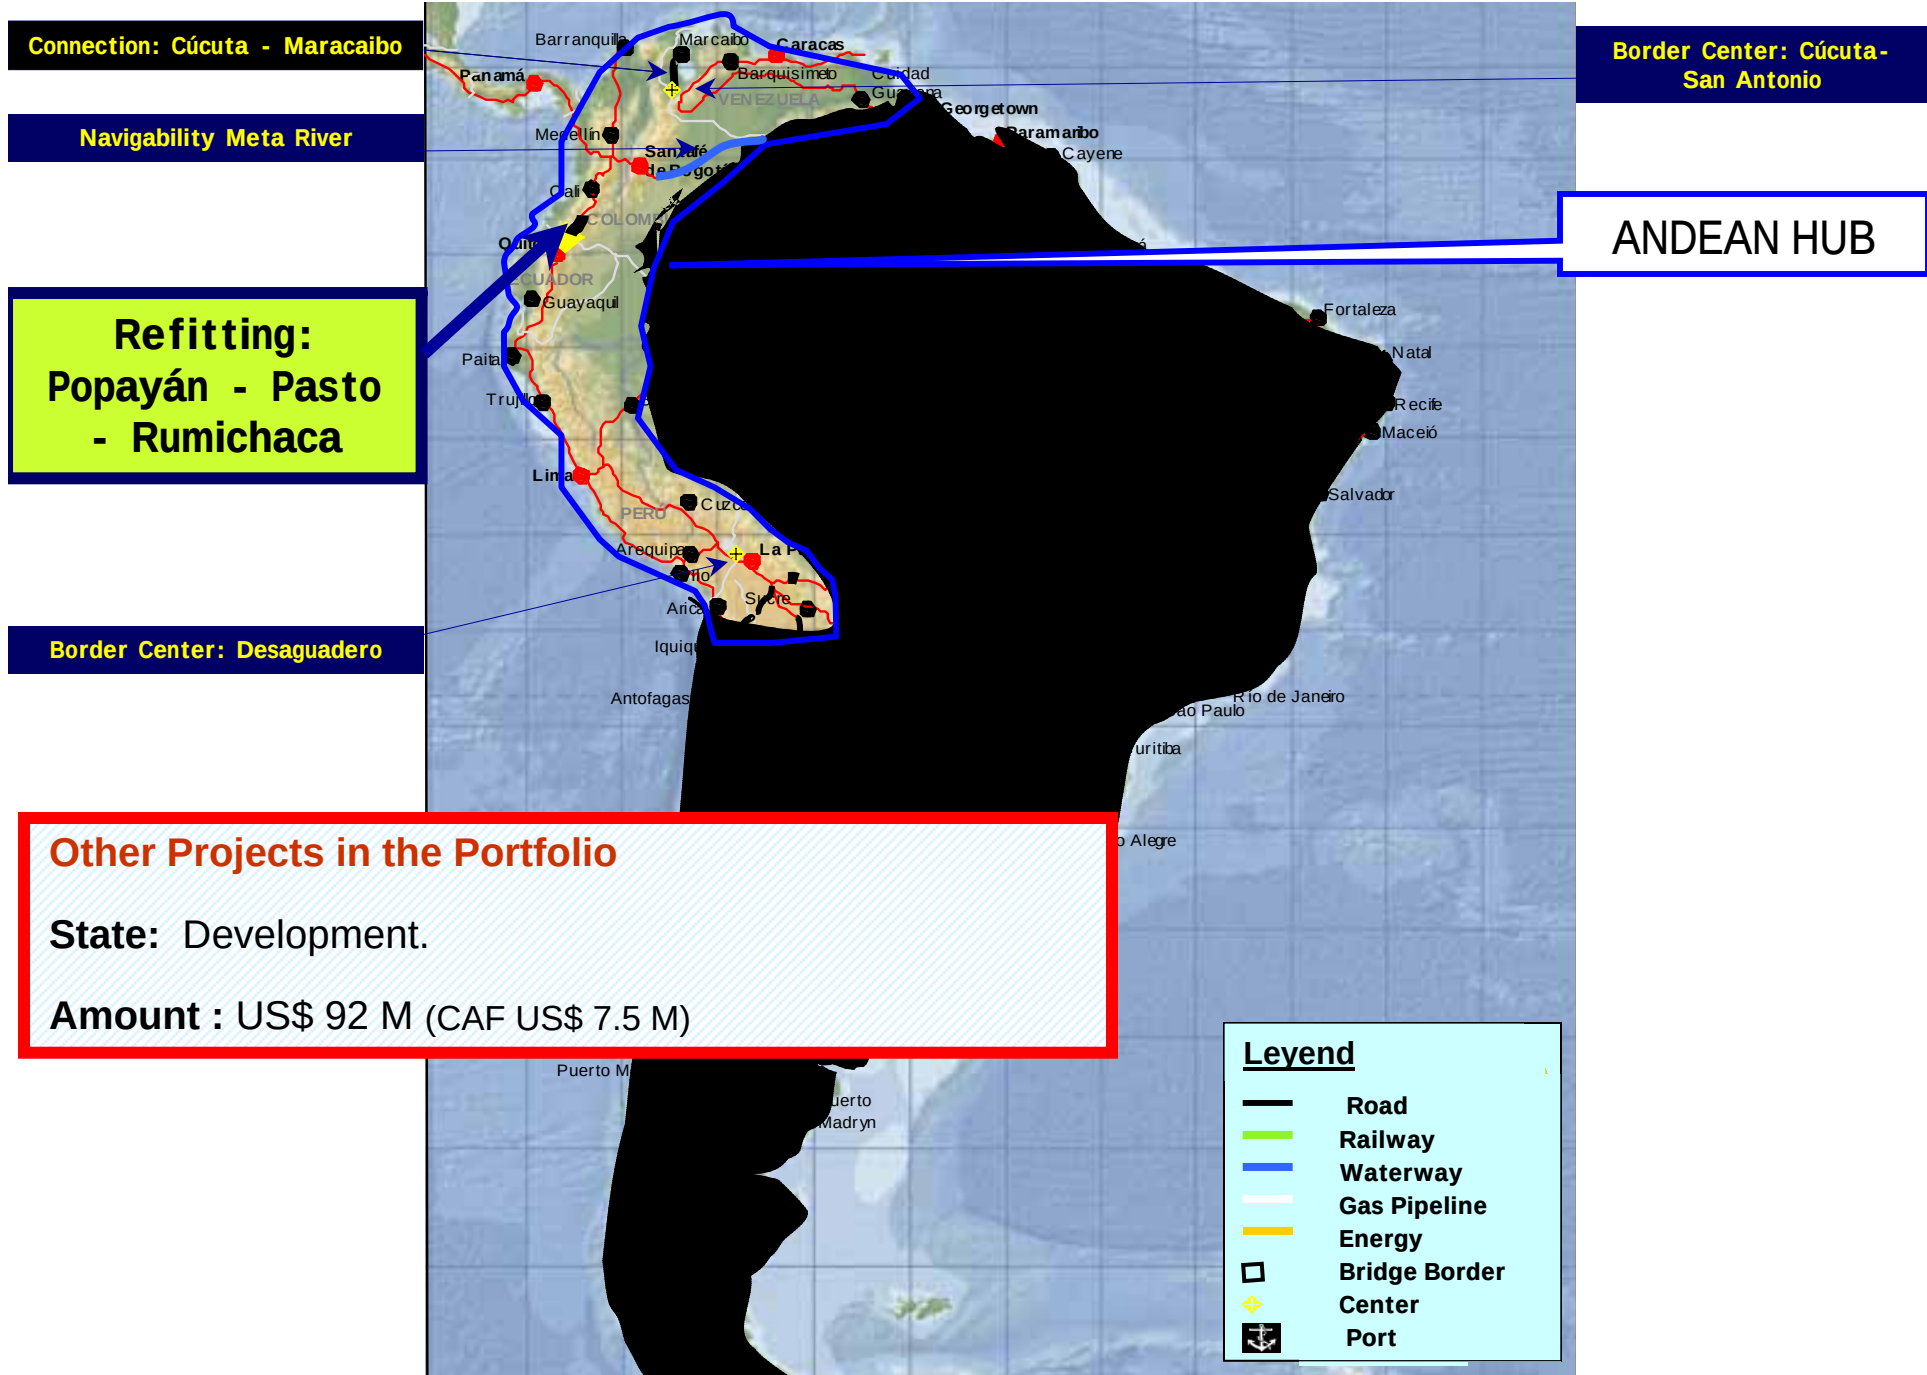

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Connection: Cúcuta - Maracaibo

Navigability Meta River

Bogotá -
Buenaventura /
Section: Buga-
Buenaventura

Border Center: Desaguadero


Border Center: Cúcuta-
San Antonio

ANDEAN HUB

Other Projects in the Portfolio

State: Execution.

Amount : US\$ 278 M (CAF US\$ 32 M)

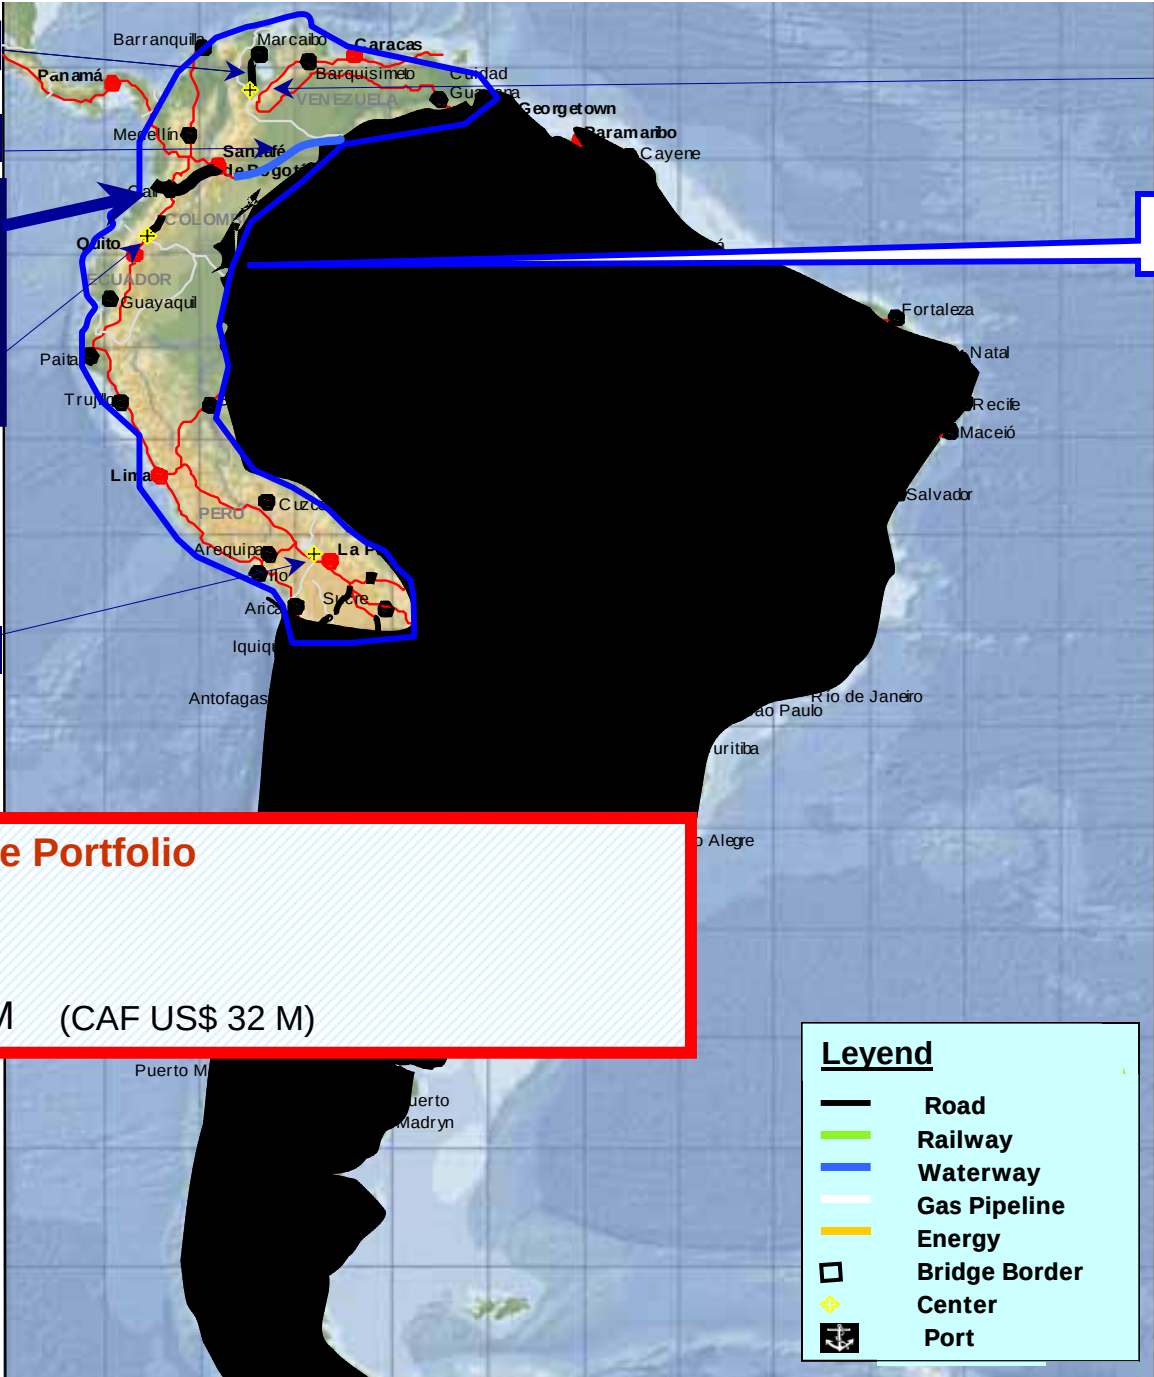

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Connection: Cúcuta - Maracaibo

Navigability Meta River


Bogotá - Buenaventura /
Section: Buga - Buenaventura

Refitting: Popayán - Pasto -
Rumichaca and Construction of
crossing through Pasto

Border Center: Desaguadero

Border Center: Cúcuta -
San Antonio


ANDEAN HUB

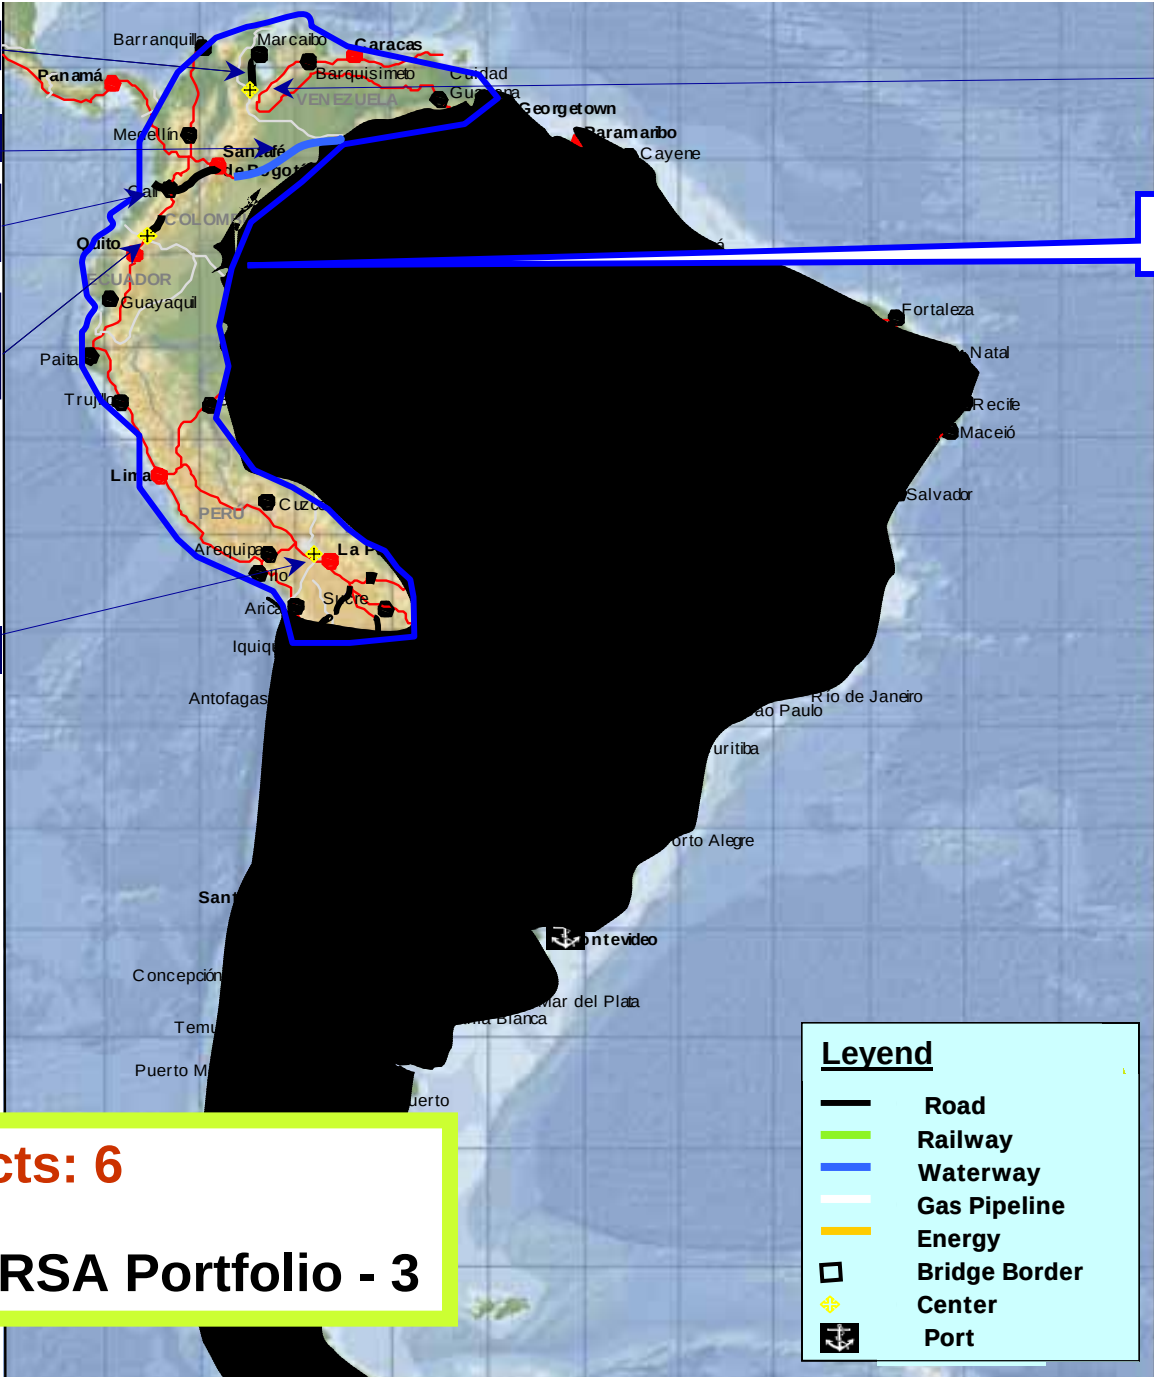

Total of Projects: 6

- AIC - 3
- Rest of the IIRSA Portfolio - 3

**AIC 20 - Road:
Pasto - Mocoa**

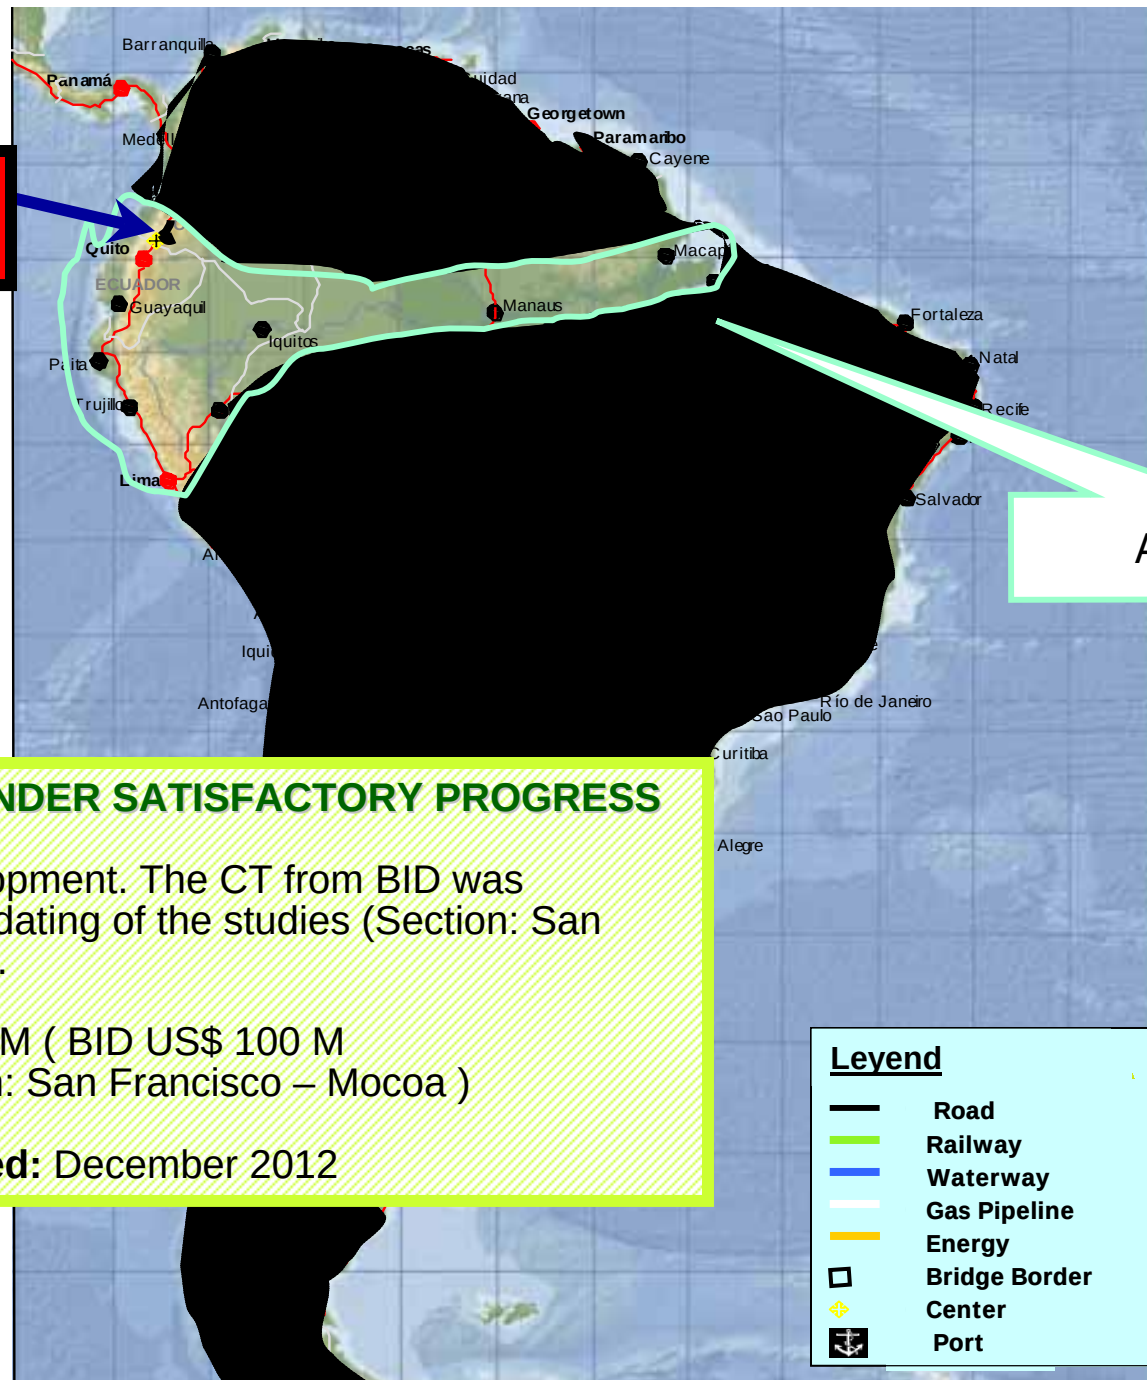


AIC – PROJECT UNDER SATISFACTORY PROGRESS

State: Under development. The CT from BID was approved for the updating of the studies (Section: San Francisco – Mocoa).

Amount : US\$ 183 M (BID US\$ 100 M
Section: San Francisco – Mocoa)

Completion planned: December 2012

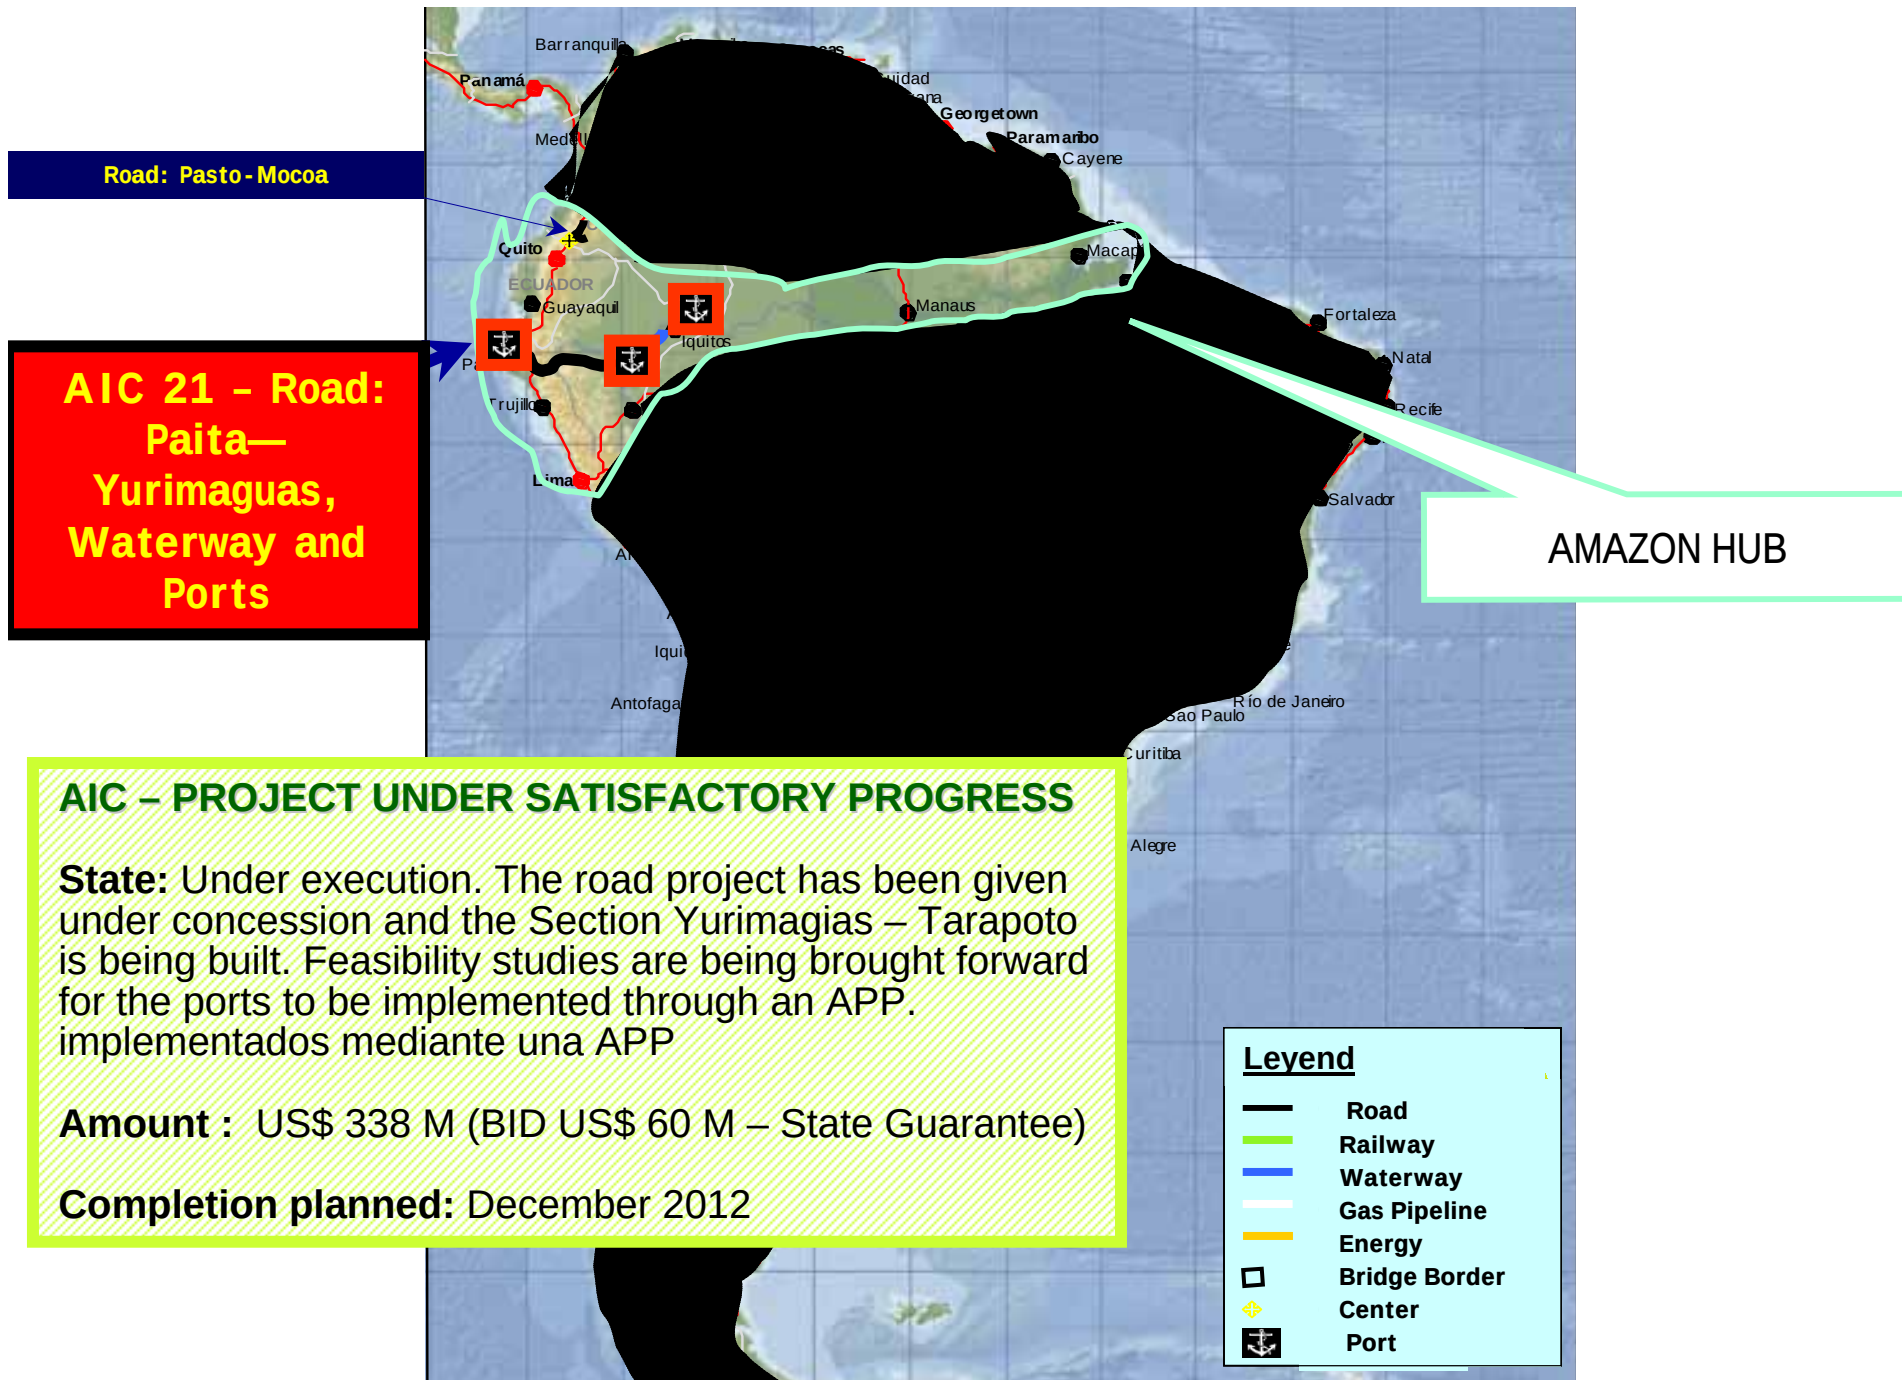



AIC – PROJECT UNDER SATISFACTORY PROGRESS


State: Under execution. The road project has been given under concession and the Section Yurimagias – Tarapoto is being built. Feasibility studies are being brought forward for the ports to be implemented through an APP.
implementados mediante una APP

Amount : US\$ 338 M (BID US\$ 60 M – State Guarantee)

Completion planned: December 2012

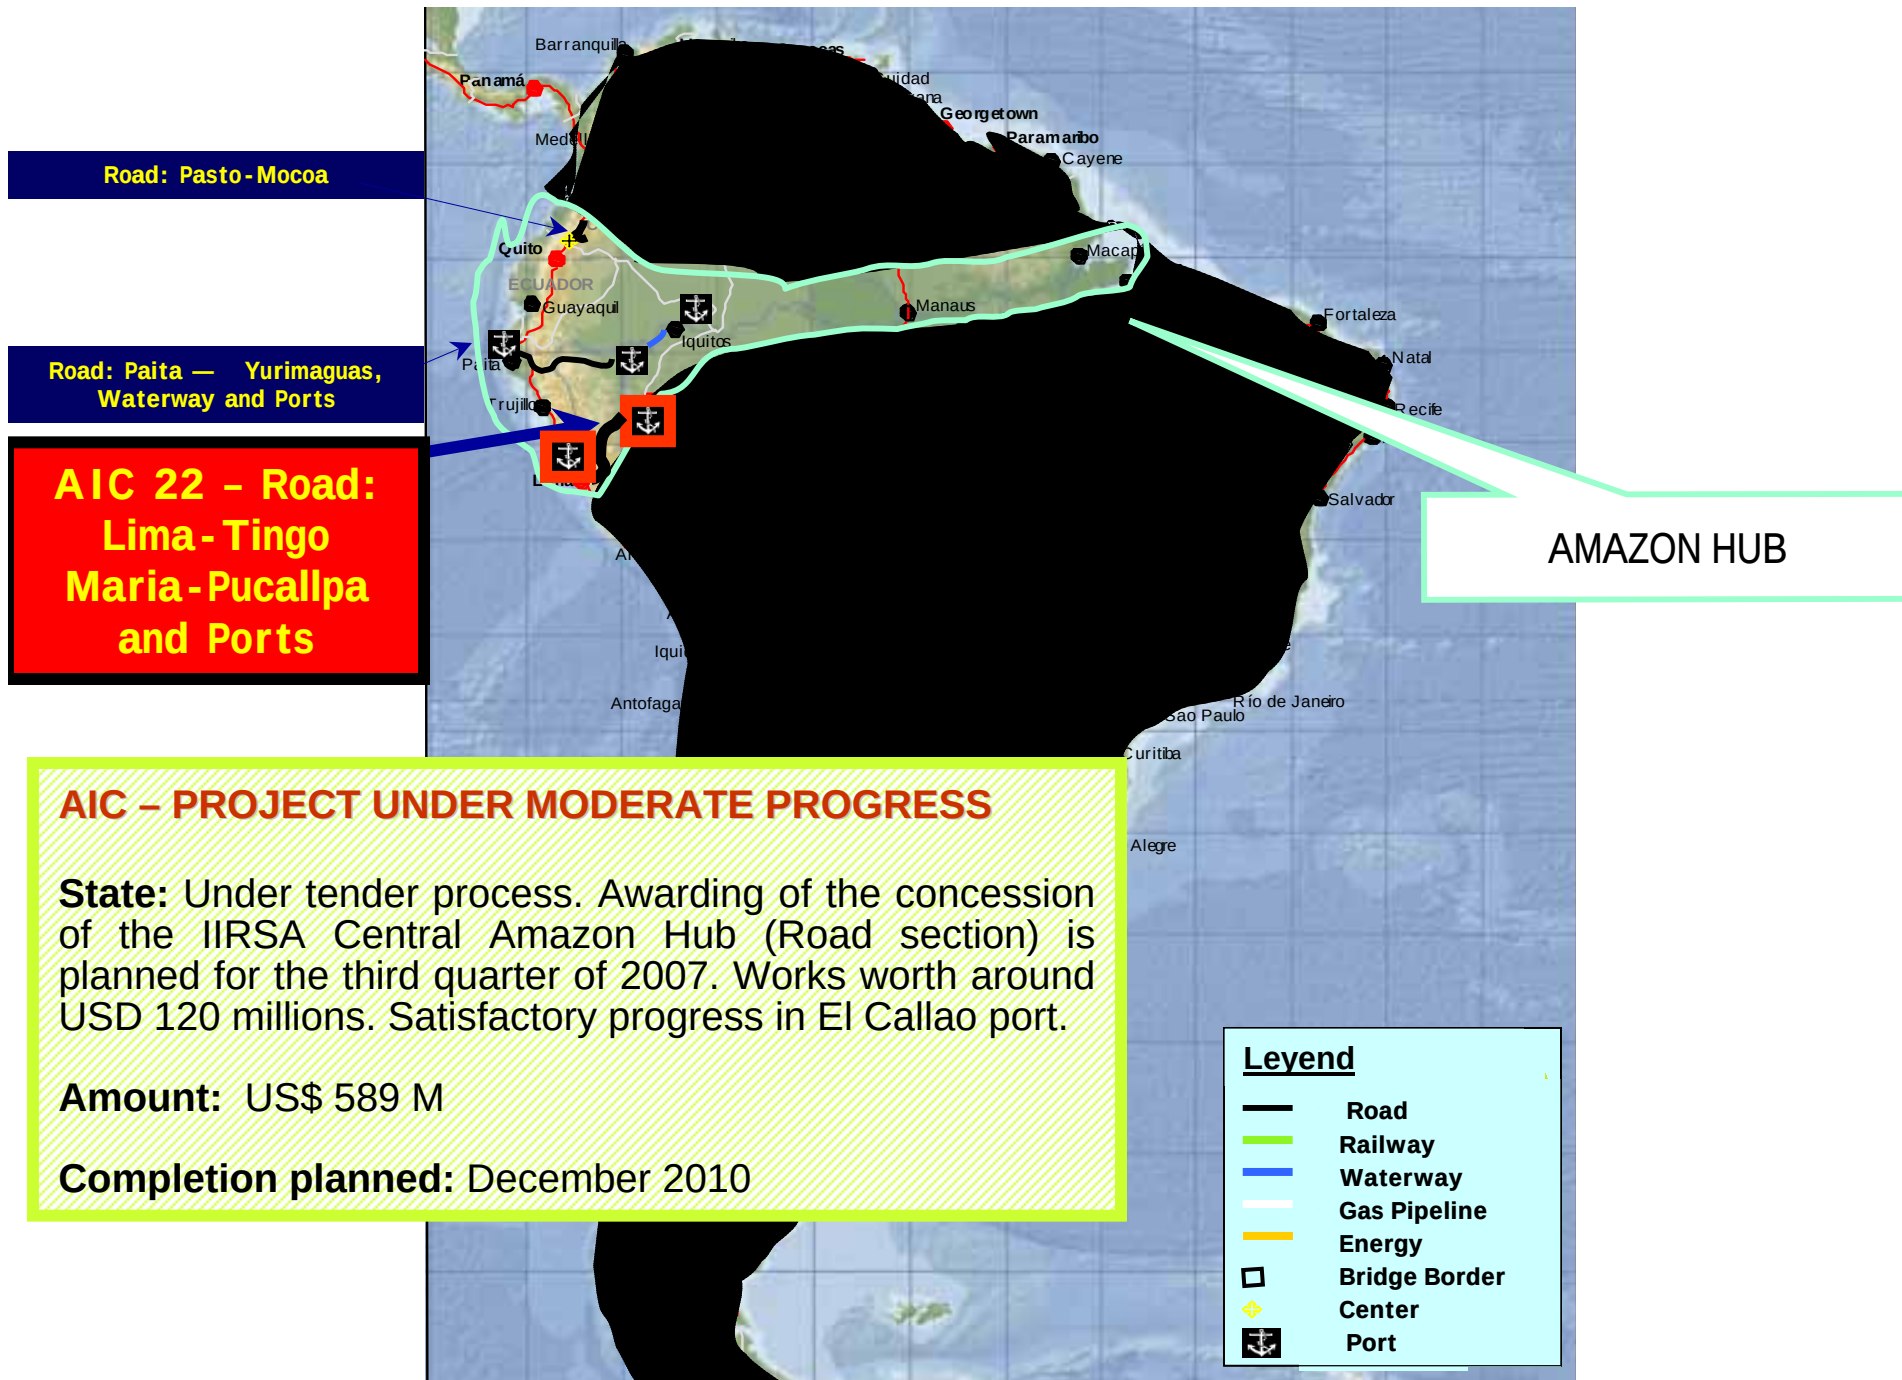

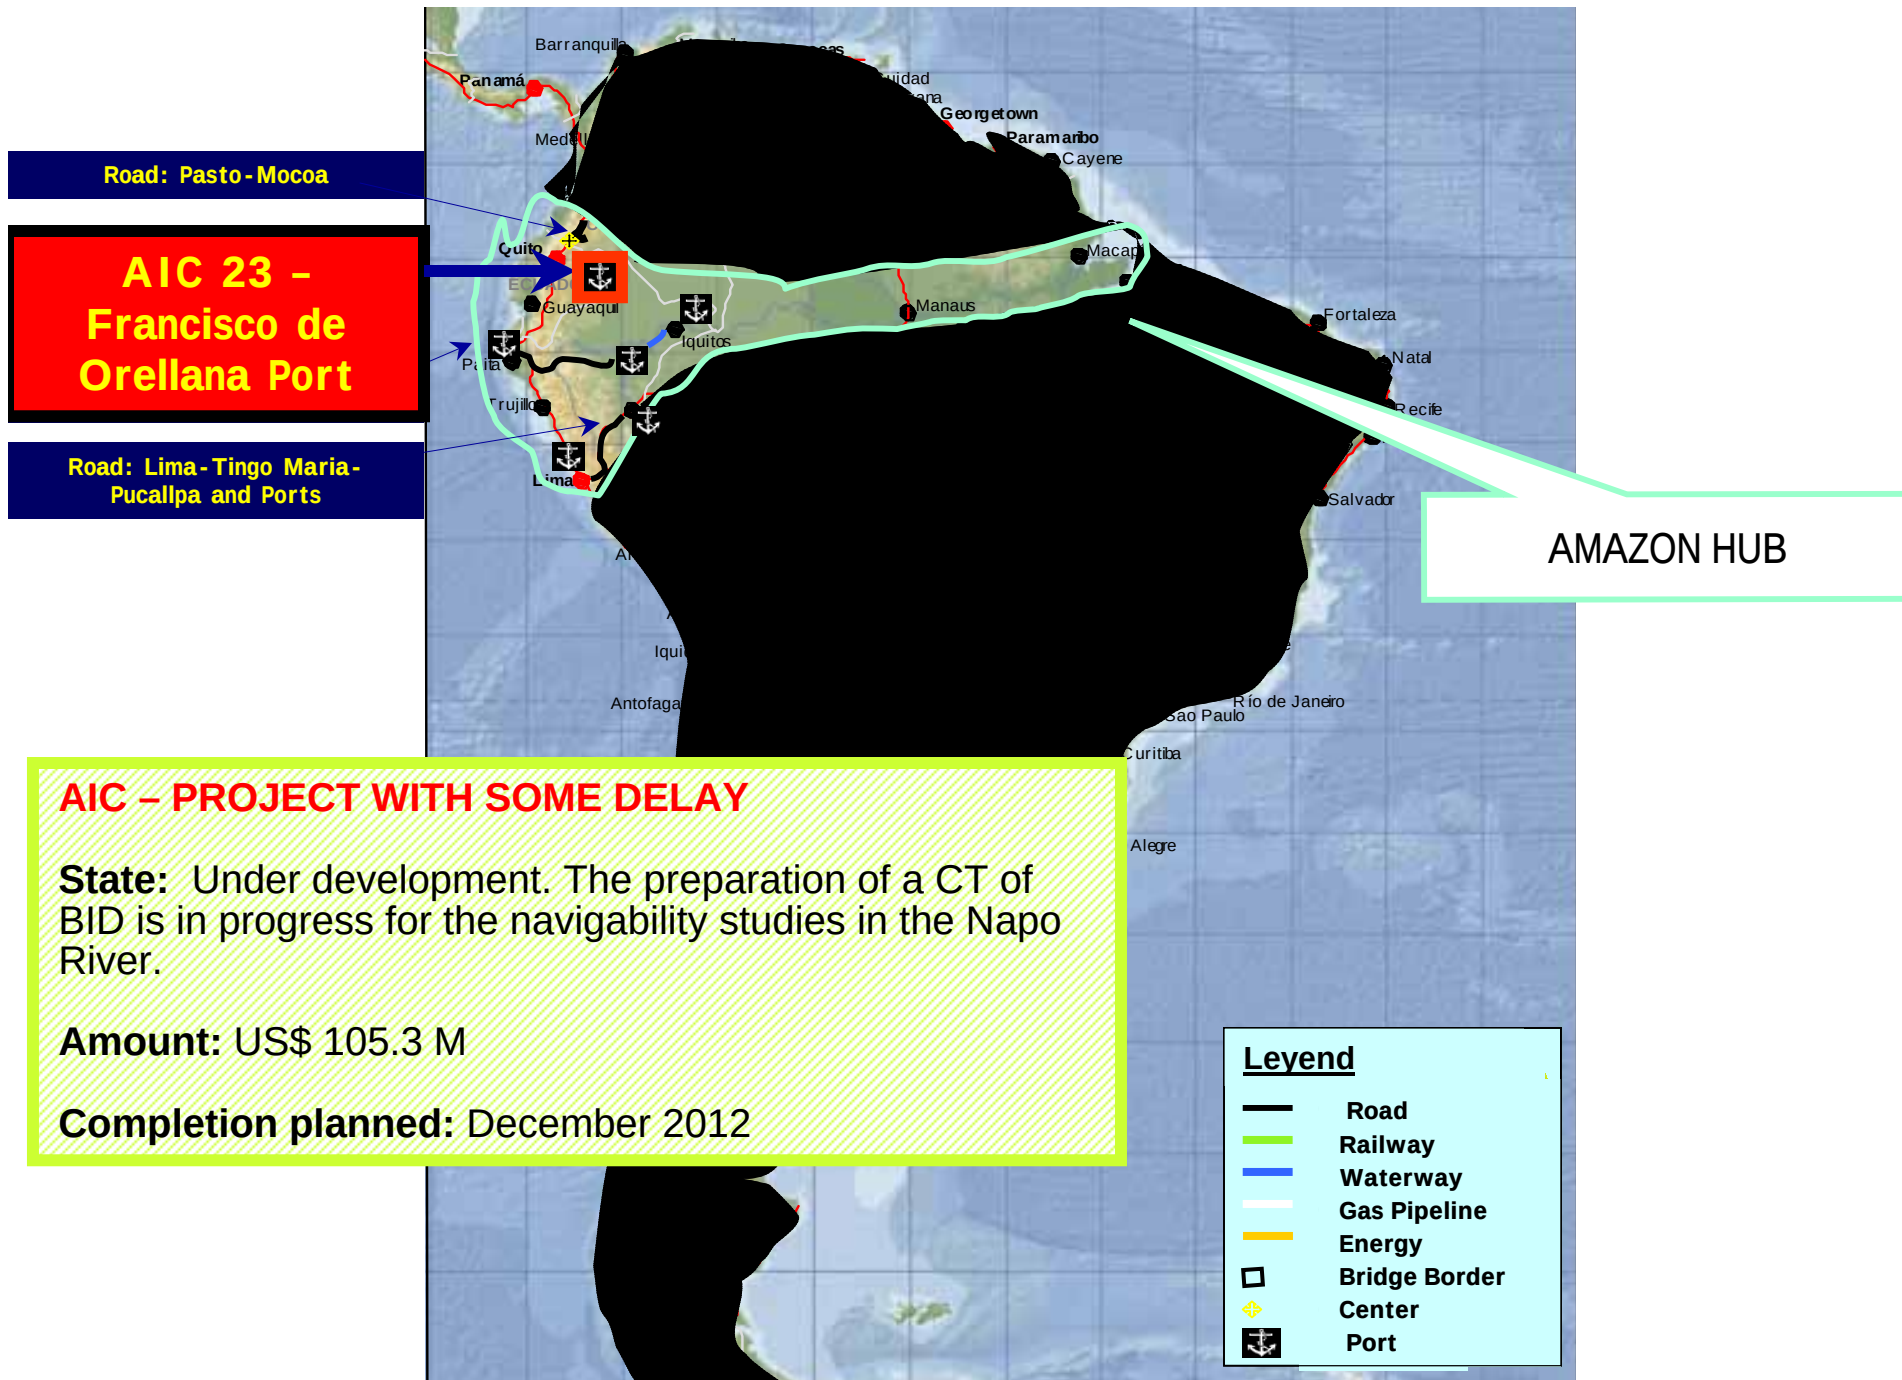

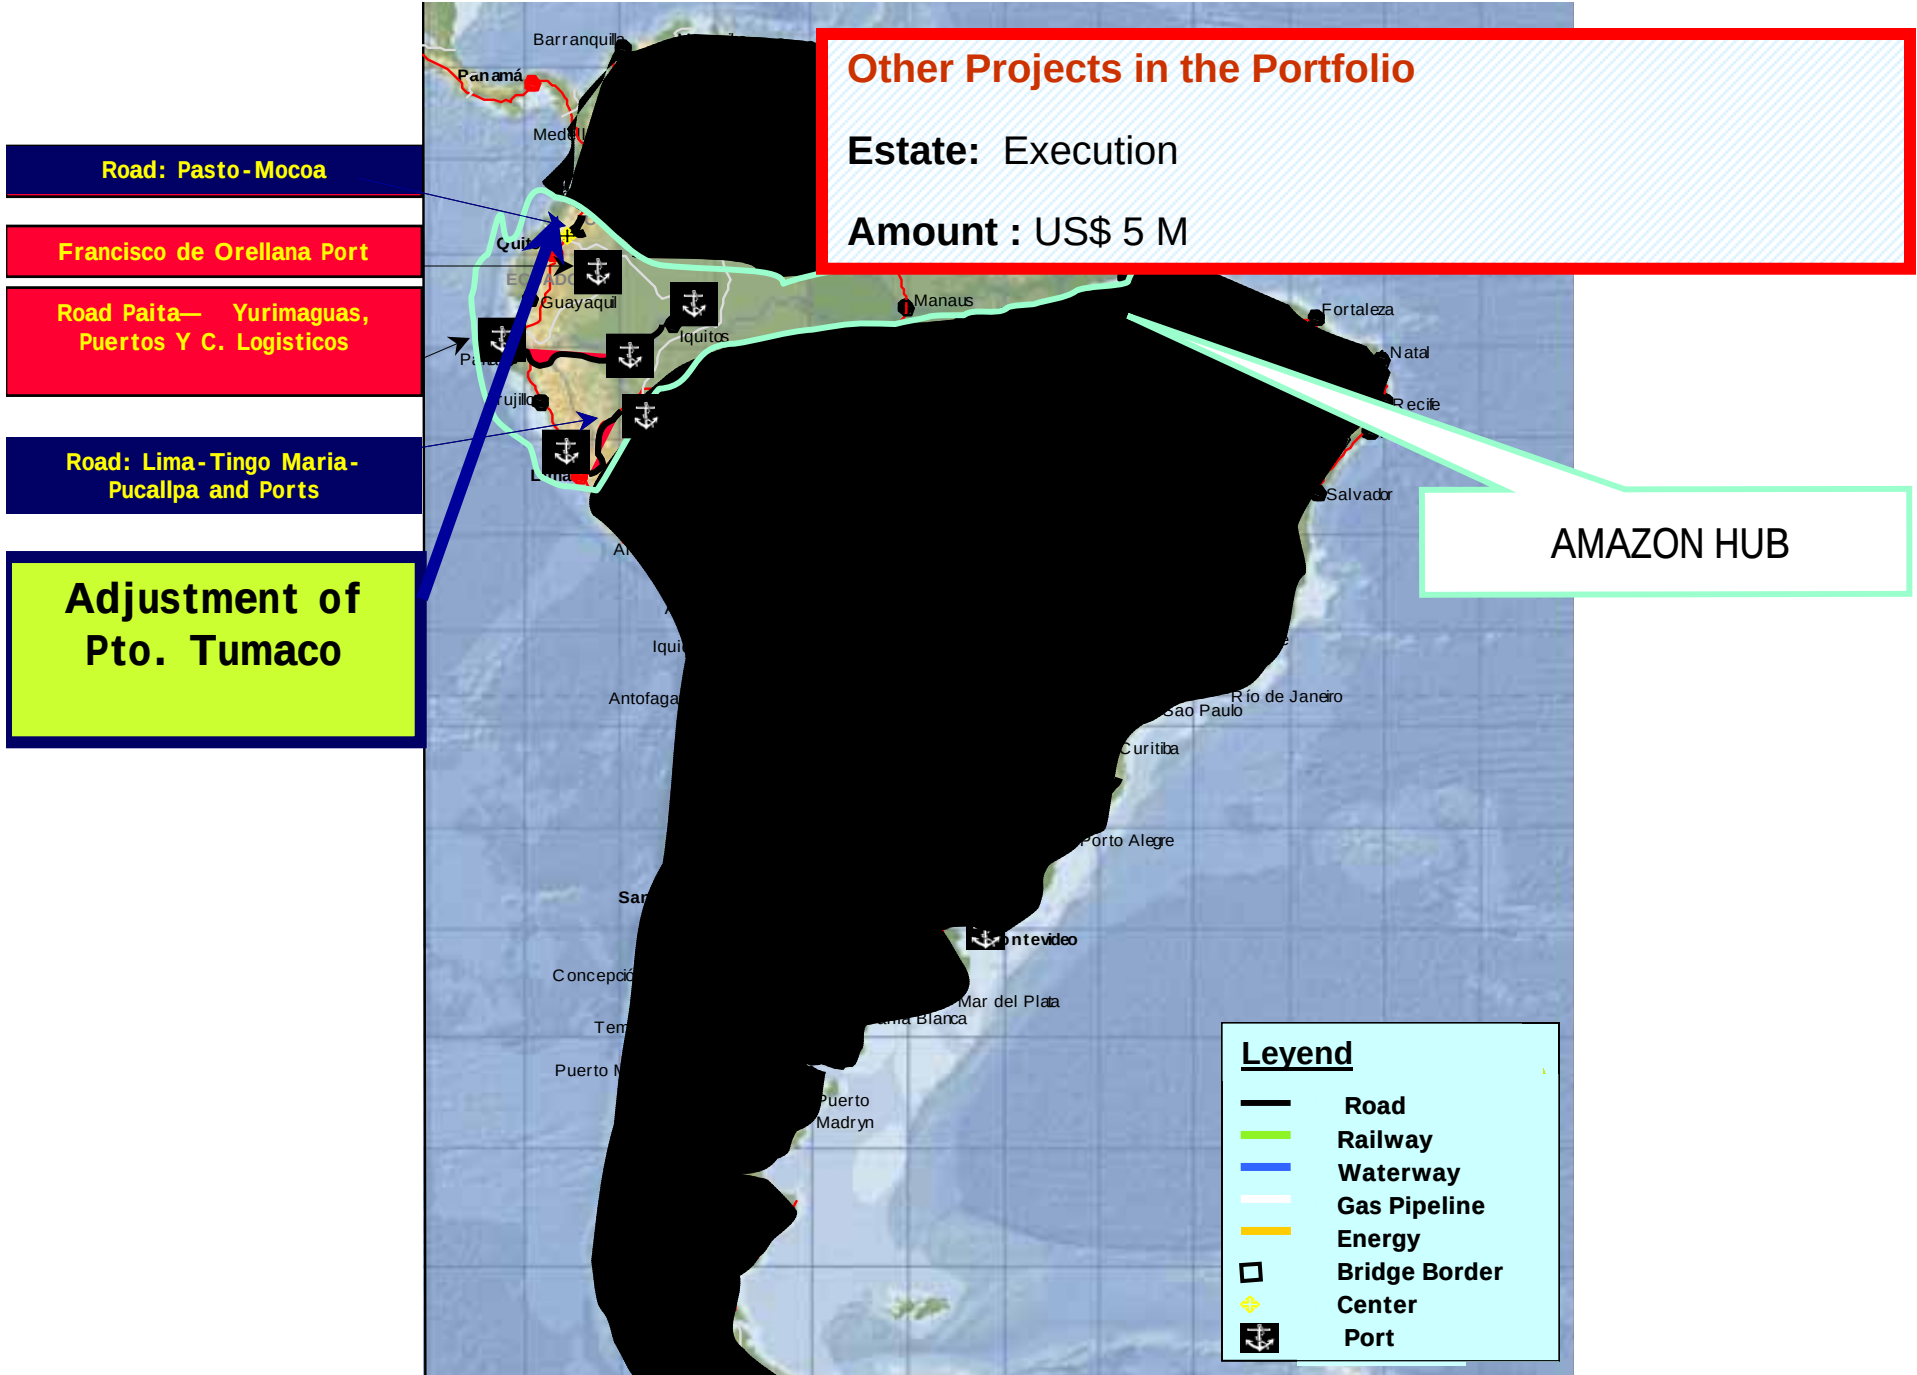

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Other Projects in the Portfolio

Estate: Execution

Amount : US\$ 6.3 M por concesión

Road: Pasto-Mocoa

Francisco de Orellana Port.

Road Paita— Yurimaguas,
Ports and Logistic C.

Road: Lima-Tingo Maria-
Pucallpa and Ports

Tumaco Port.

Improvement of
the Pucallpa
airport

AMAZON HUB

Legend

- Road
- Railway
- Waterway
- Gas Pipeline
- Energy
- Bridge Border
- ◆ Center
- ⚓ Port

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Other Projects in the Portfolio

Estate: Execution

Amount : US\$ 617. M PPP

Road: Pasto-Mocoa

Puerto Francisco de Orellana

Carretera Paita— Yurimaguas,
Puertos Y C. Logísticos

Road: Lima-Tingo Maria-
Pucallpa and Ports
Logísticos

Adecuación de Pto. Tumaco

Mejoramiento del
Aeropuerto de Pucallpa


Modernization of
the Port of
Callao

AMAZON HUB

Legend

- Road
- Railway
- Waterway
- Gas Pipeline
- Energy
- Bridge Border
- ◆ Center
- ⚓ Port

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

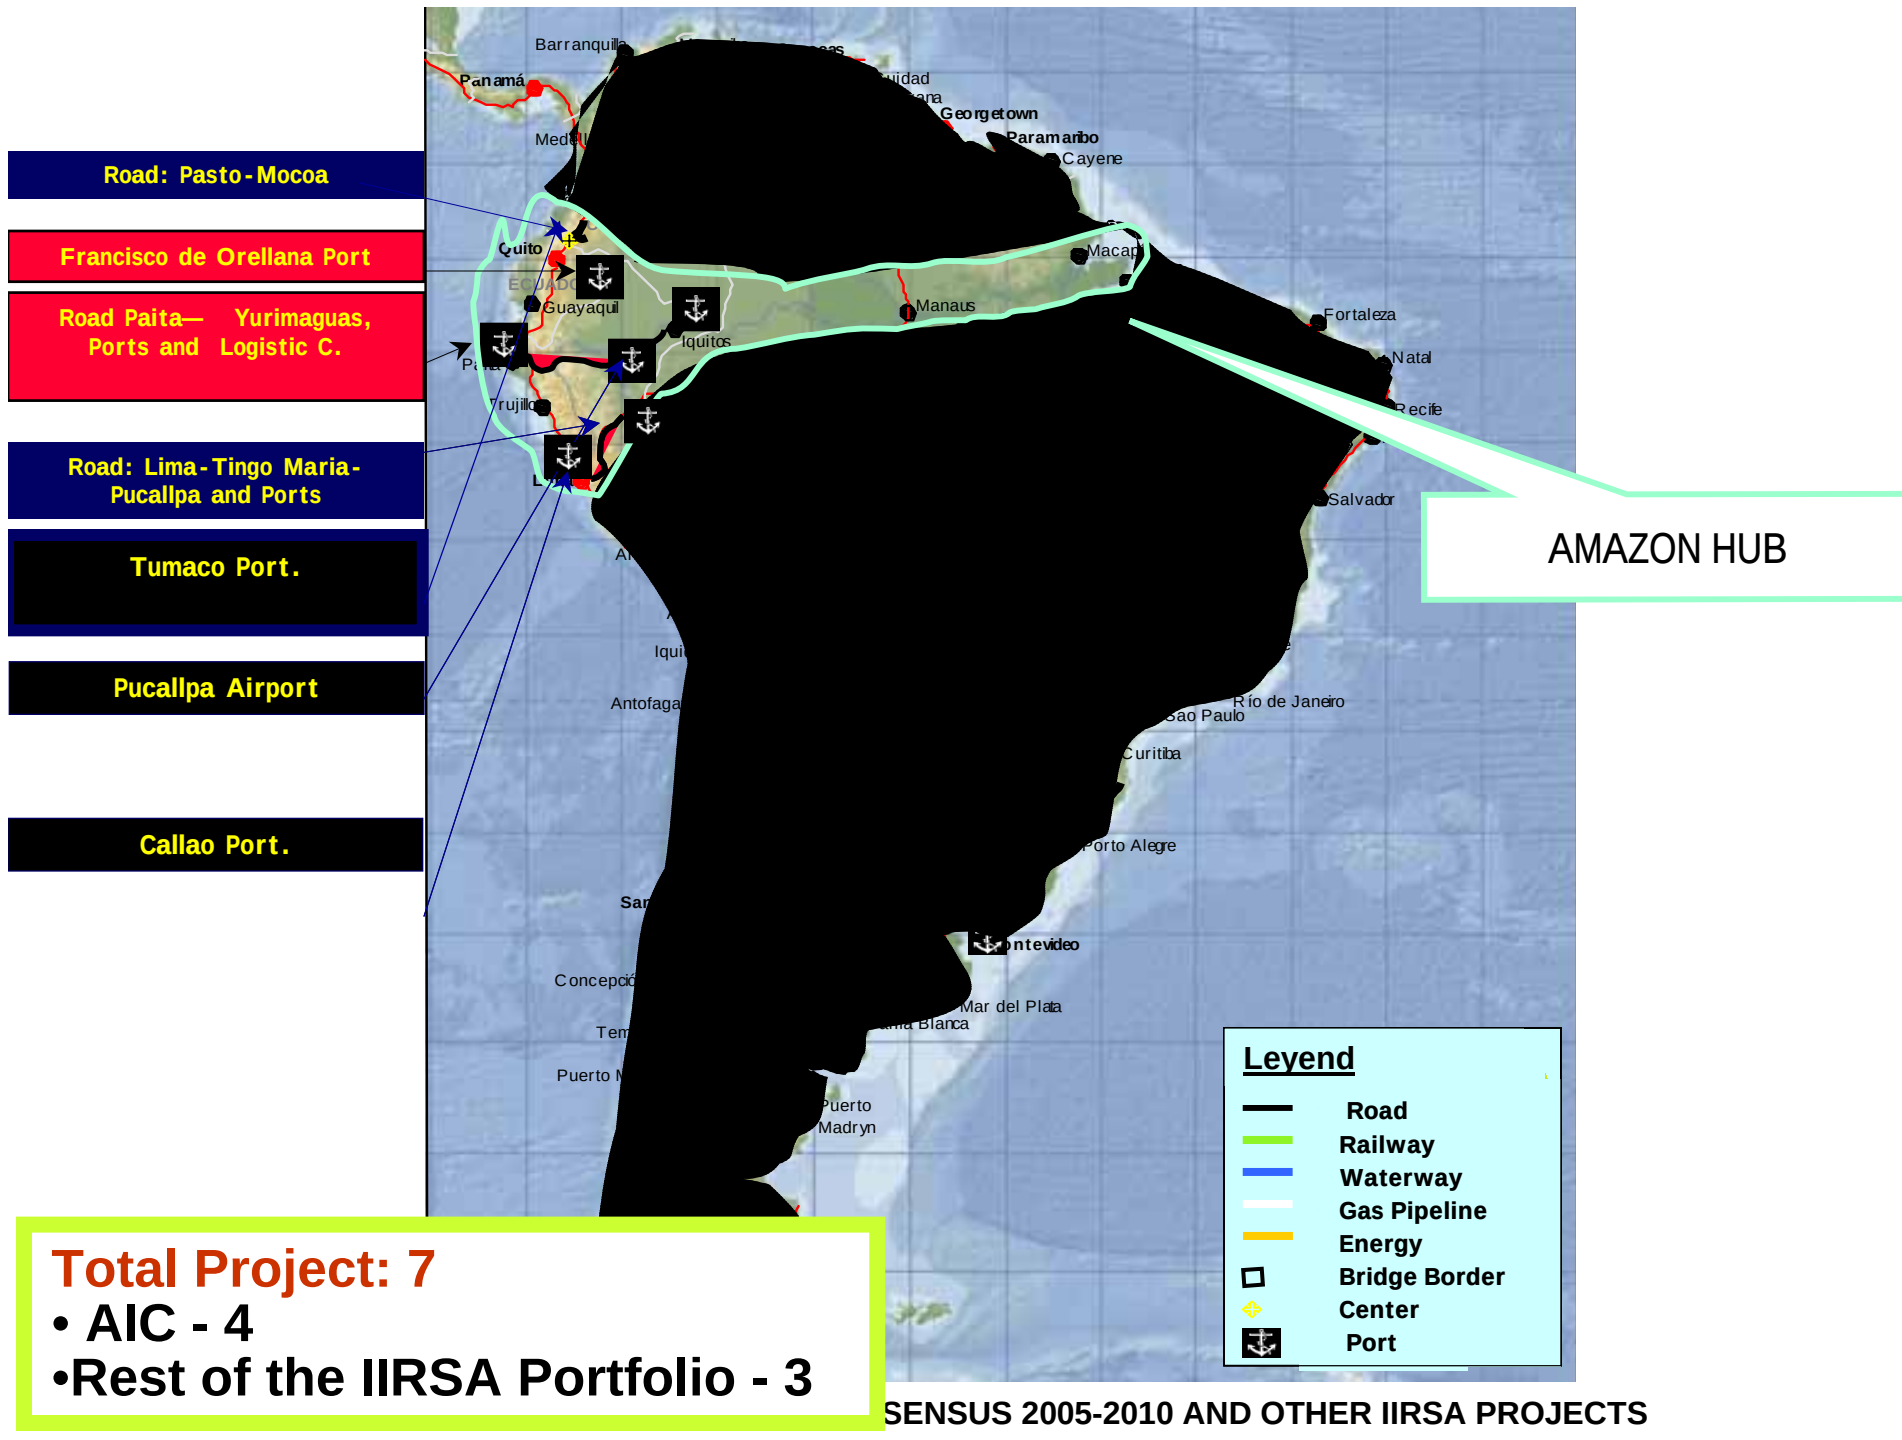

AIC – PROJECT UNDER SATISFACTORY PROGRESS


State: Execution. The road project has been given under concession.

Amount: US\$ 1,073.5 M (CAF US\$ 504.5 M)

Completion planned: December 2010

**AIC 24 – Road:
Iñapari-Cusco
and Juliaca**

PERU-BRAZIL-BOLIVIA
HUB

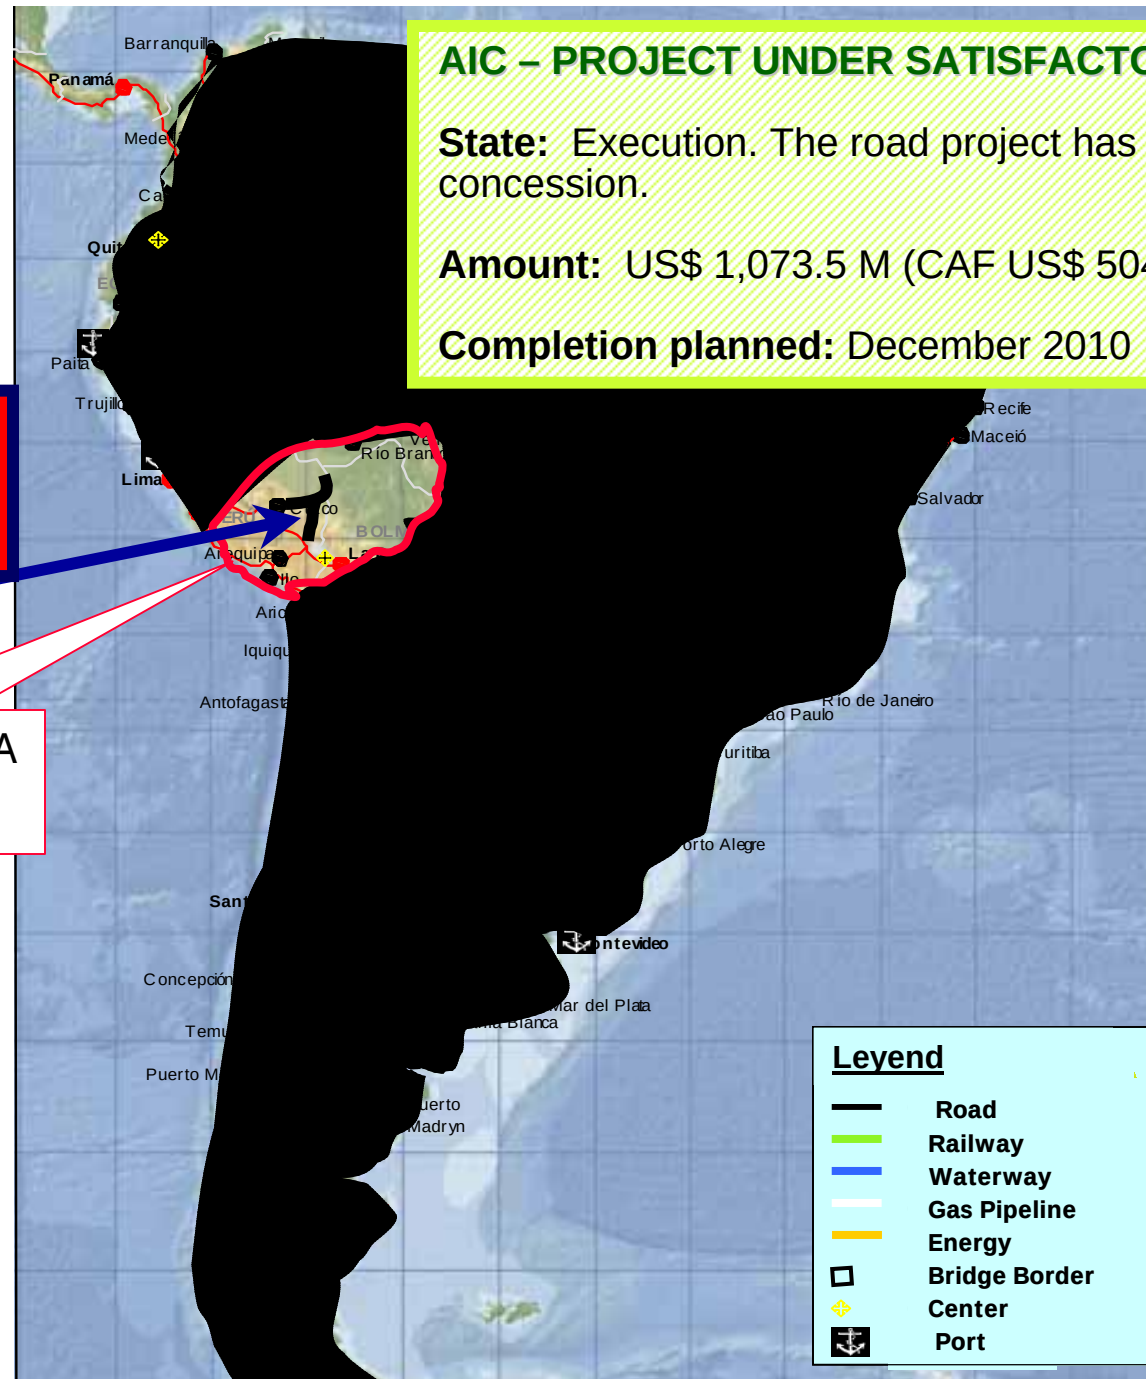

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

AIC – PROJECT: COMPLETED


State: Completed in January 2006

Amount : US\$ 12 M

Completion planned: January 2006

**AIC 25 – Bridge
over the Acre
River**

PERU-BRAZIL-BOLIVIA
HUB

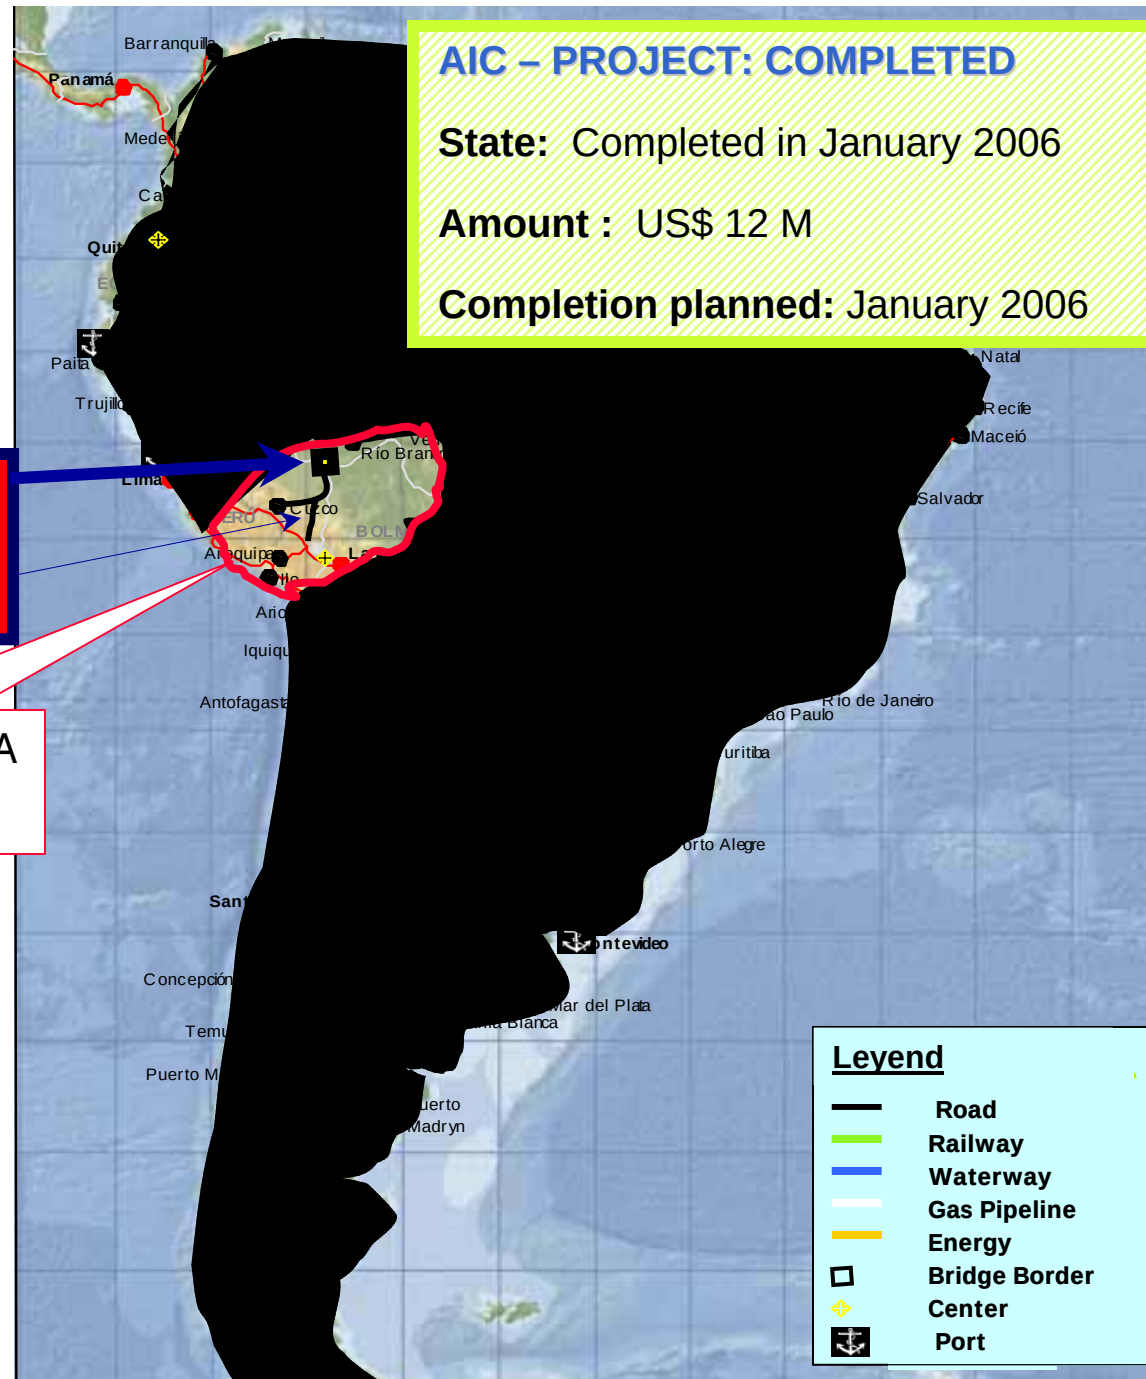

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Other Projects in the Portfolio

State: Execution.


Amount : US\$ 387 M (BID US\$ 250 M - CAF US\$ 42 M)

AIC 25 - Bridge: Acre River

Road: Iñapari-Cusco and
Juliaca

PERU-BRAZIL-BOLIVIA
HUB

Road:
Guayaramerín
- Riberalta -
Yucumo - La
Paz

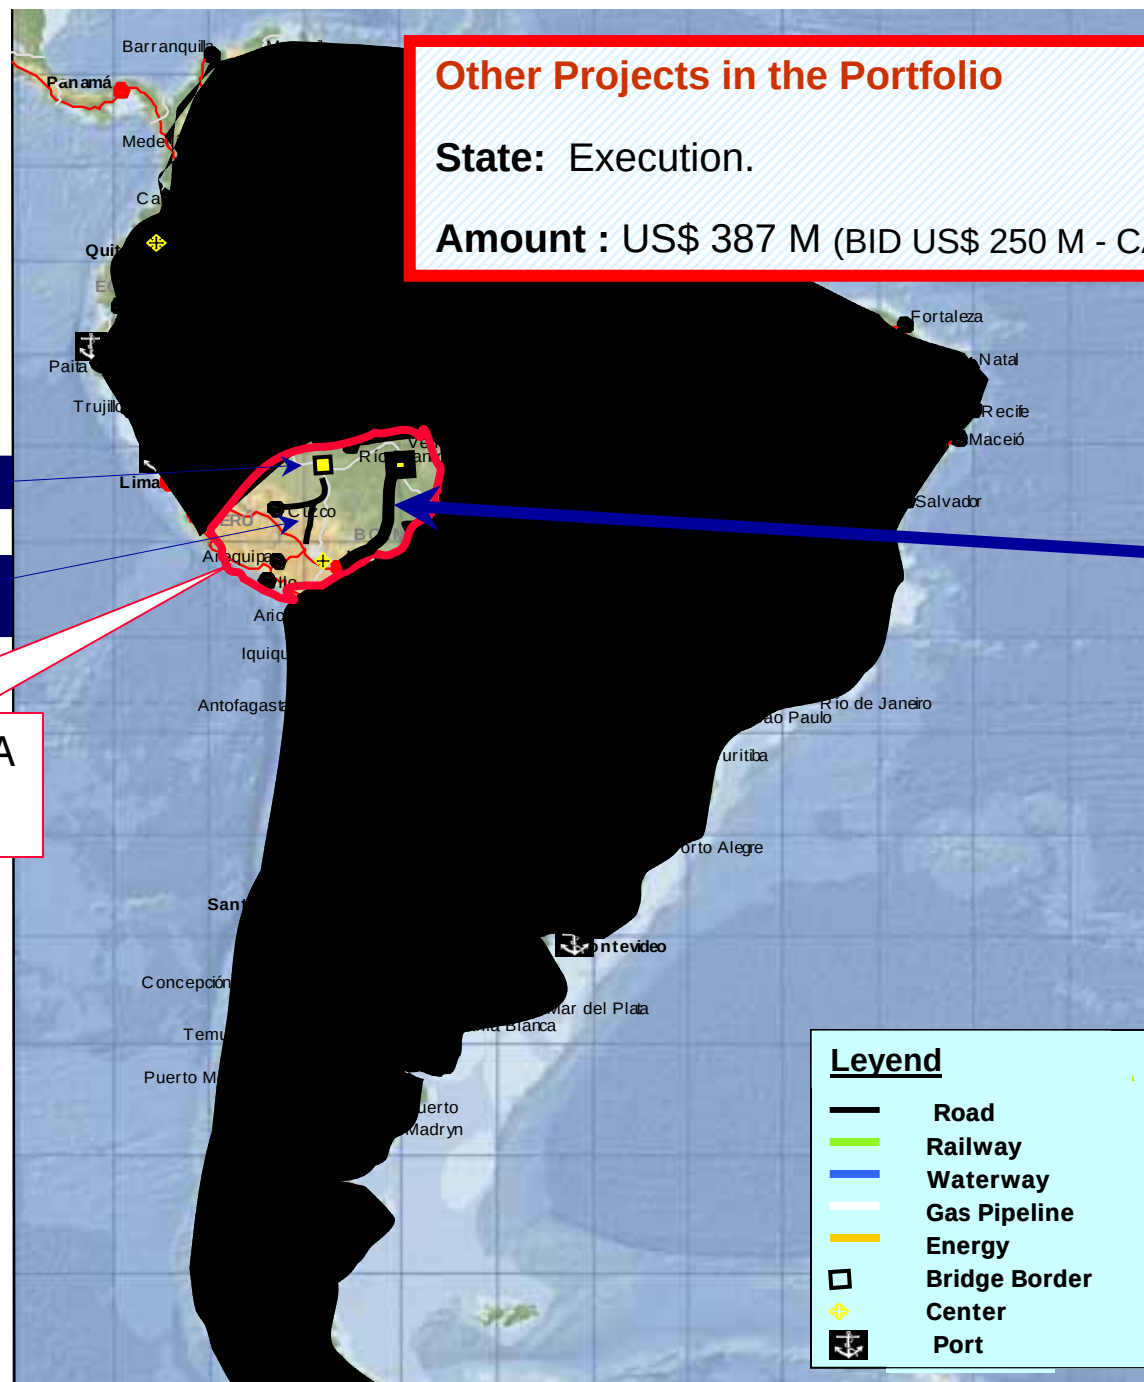

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Other Projects in the Portfolio

State: Tender Process.

Amount : N/A Private Sector.

AIC 25 - Bridge: Acre River

Road: Iñapari-Cusco and
Juliaca

PERU-BRAZIL-BOLIVIA
HUB

Road: Guayaramerín -
Riberalta - Yucumo -
La Paz

Transmission
Line: San
Gabán -
Maldonado
Port

Legend

- Road
- Railway
- Waterway
- Gas Pipeline
- Energy
- Bridge Border
- ◆ Center
- ⚓ Port

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Total of Projects: 4

- AIC - 2
- Rest of the IIRSA Portfolio - 2


AIC 25 - Bridge: Acre River

Road: Iñapari-Cusco and
Juliaca

PERU-BRAZIL-BOLIVIA
HUB

Road: Guayaramerín -
Riberalta - Yucumo - La
Paz

Transmission Line: San
Gabán - Maldonado
Port

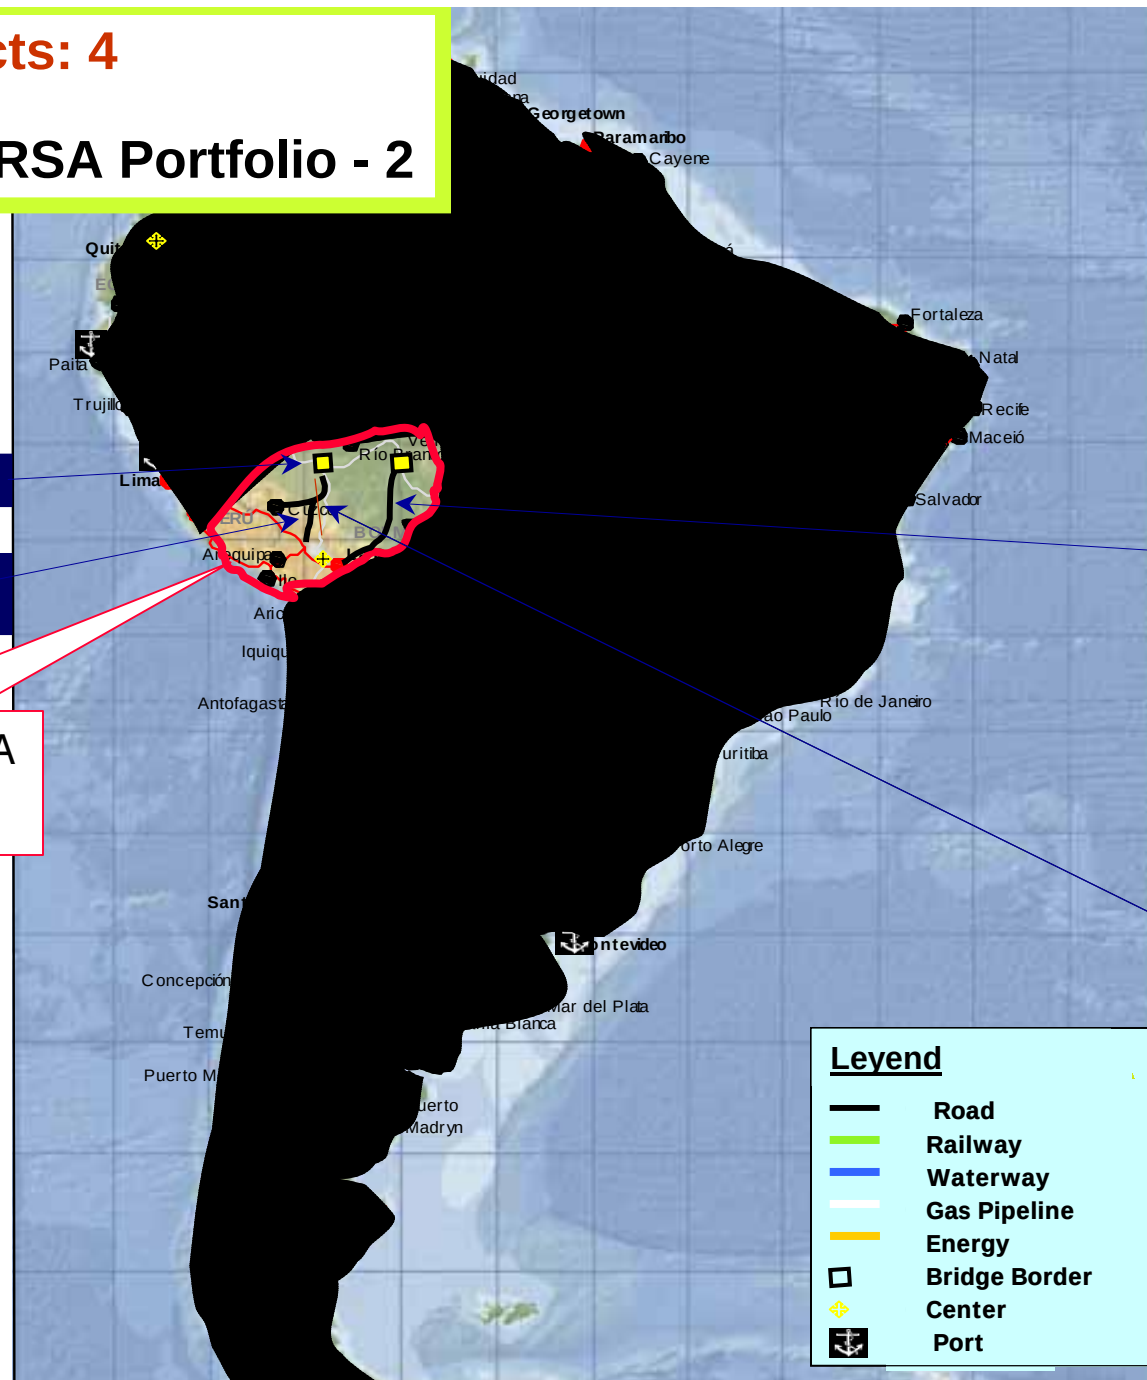

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

AIC – PROJECT UNDER SATISFACTORY PROGRESS

State: Under development. The BID has approved a CT (0.9 millions) for the updating of the Feasibility and Socio-Environmental Studies, which are about to be started.

Amount: US\$ 3.3 M (BID US\$ 0.9 M)

Completion planned: 2° semester 2008

**AIC 26 –
Road:
Boavista-
Georgetown (I
Stage)**

GUIANA SHIELD HUB

Legend

- Road
- Railway
- Waterway
- Gas Pipeline
- Energy
- Bridge Border
- ◆ Center
- ⚓ Port

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

AIC – PROJECT UNDER SATISFACTORY PROGRESS

State: Execution. The works that are in charge of the Brazilian Government have been re-started in March 2007.

Amount : US\$ 10 M

Completion planned: 1° Quarter 2008

Road: Boavista -
Georgetown (I Stage)


**AIC 27 -
Bridge over
Takutu River**

GUIANA SHIELD HUB

Legend

- Road
- Railway
- Waterway
- Gas Pipeline
- Energy
- Bridge Border
- ◆ Center
- ⚓ Port

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

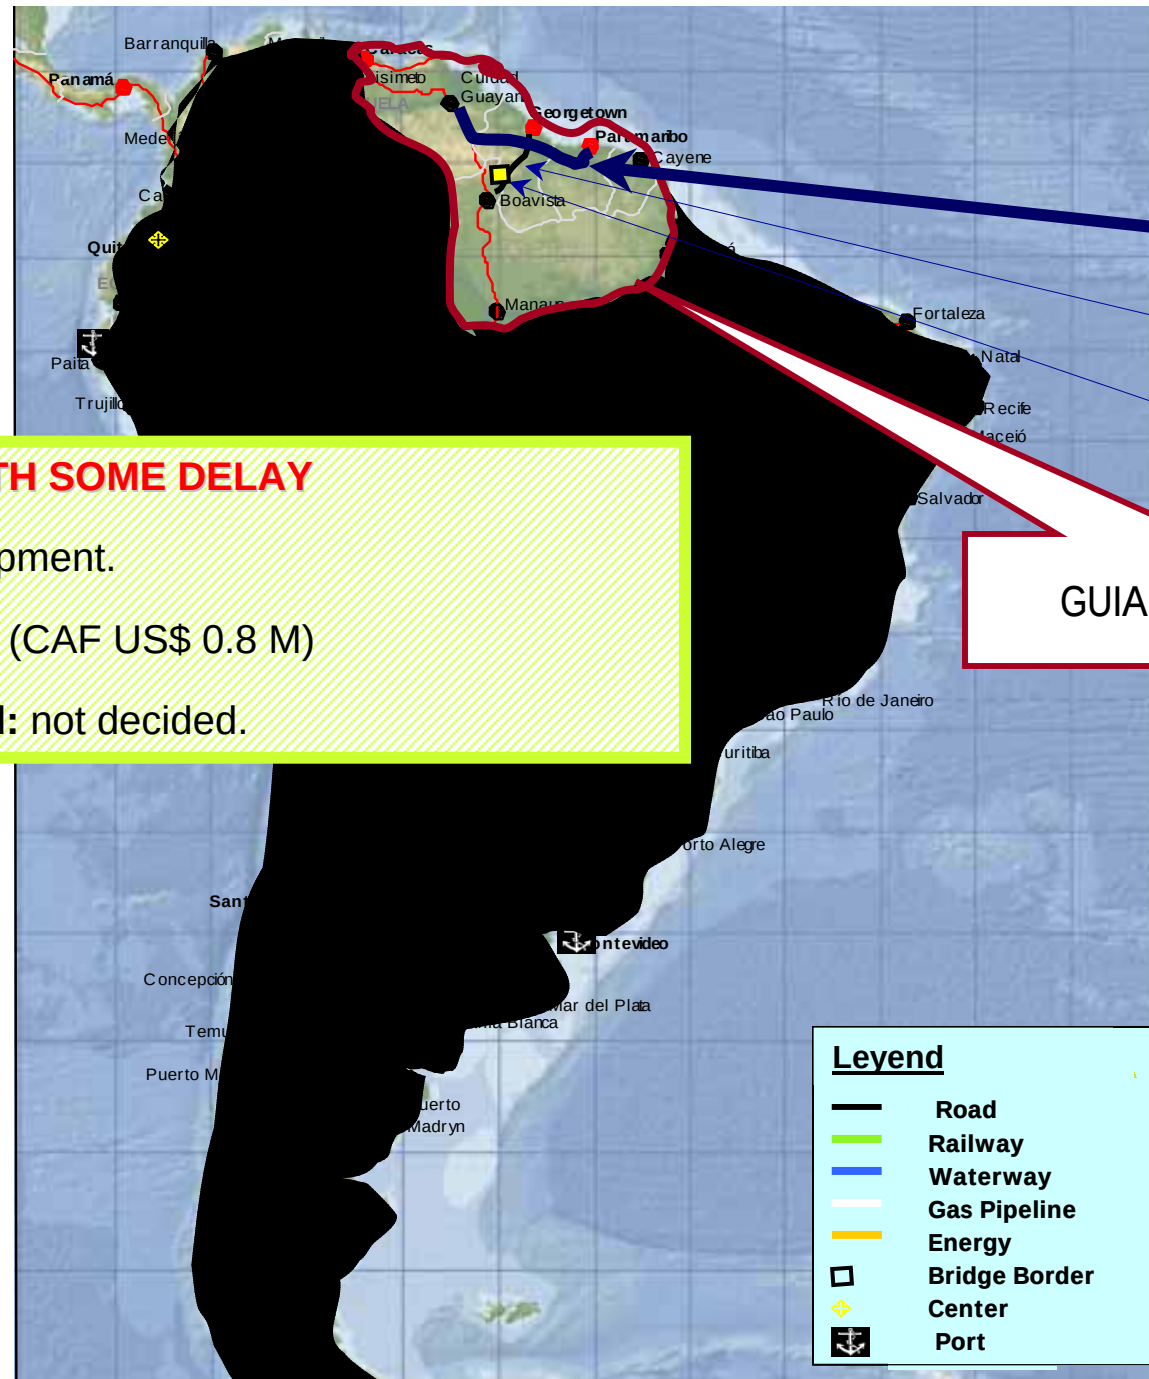

AIC – PROJECT WITH SOME DELAY

State: Under development.

Amount : US\$ 0.8 M (CAF US\$ 0.8 M)

Completion planned: not decided.


**AIC 28 -
Road:
Venezuela -
Guyana -
Suriname (1
Stage)**

GUIANA SHIELD HUB

Leyend

- | | |
|---|---------------|
|  | Road |
|  | Railway |
|  | Waterway |
|  | Gas Pipeline |
|  | Energy |
|  | Bridge Border |
|  | Center |
|  | Port |

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

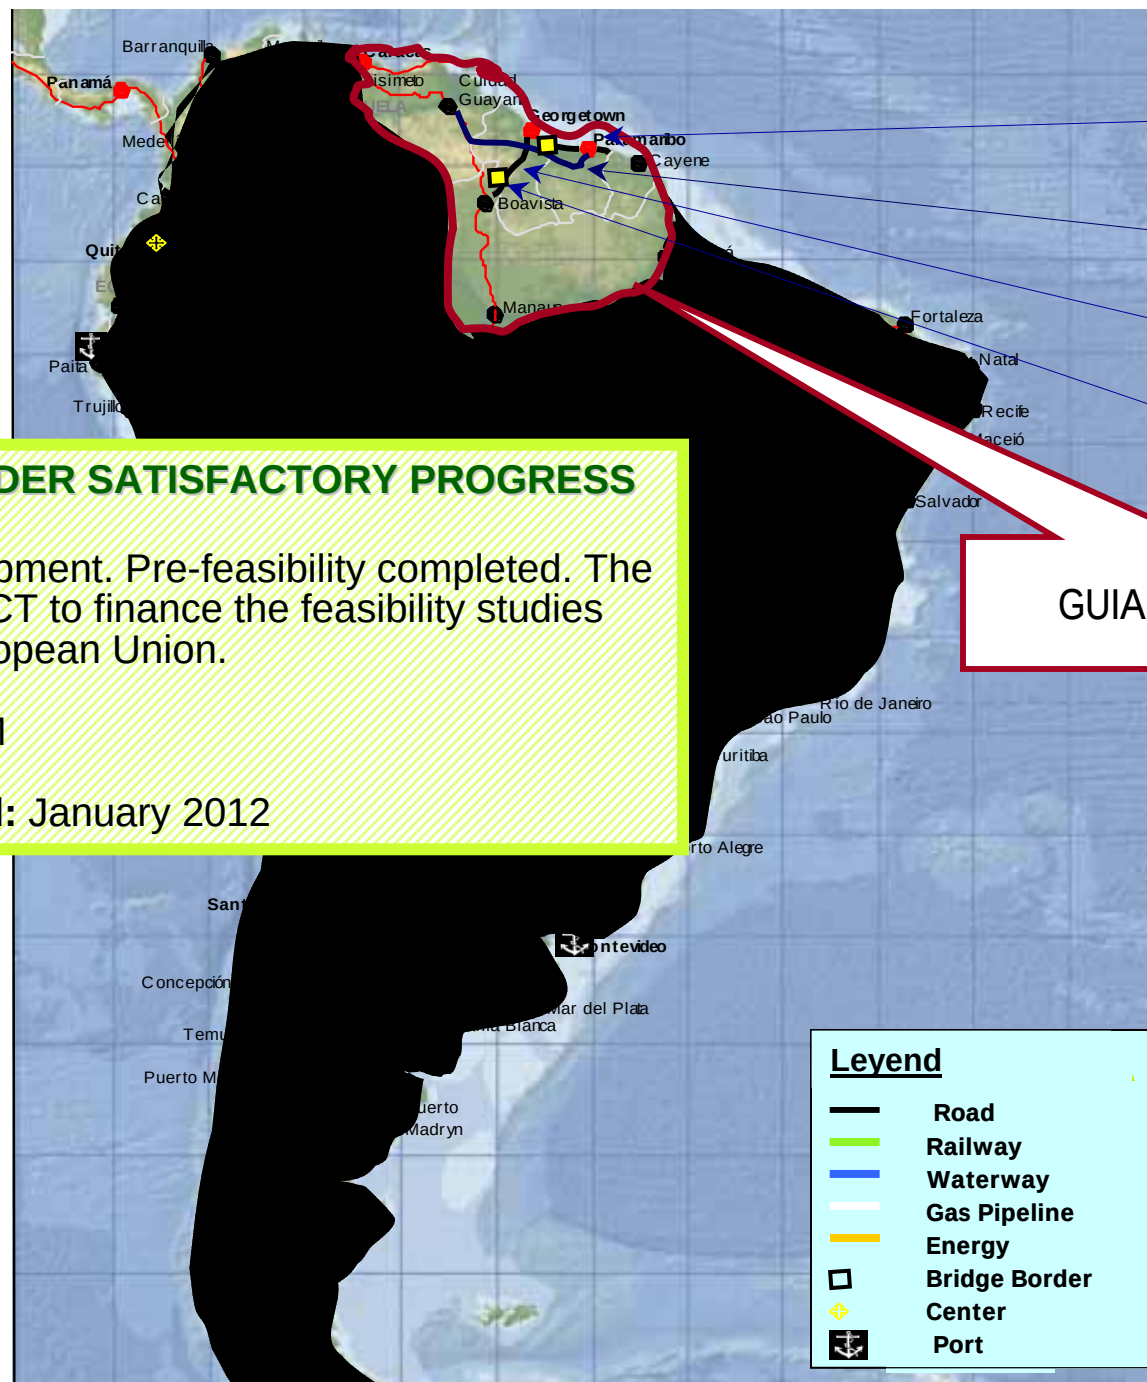

**AIC 29 -
Road: Nieu
Nickerie-
Paramaribo-
Albina and
Bridge**

Bridge over Itakutu River

GUIANA SHIELD HUB

AIC – PROJECT UNDER SATISFACTORY PROGRESS

State: Under development. Pre-feasibility completed. The BID has approved a CT to finance the feasibility studies together with the European Union.

Amount : US\$ 105 M

Completion planned: January 2012

**Road: Caracas-
Manaos**

**Road: Nieuw Nickerie-
Paramaribo-Albina and
Bridge**

**Road: Venezuela-Guyana-
Suriname (I Stage)**

**Road: Boavista-
Georgetown (I Stage)**

Bridge over Itakutu River

GUIANA SHIELD HUB

Other Projects in the Portfolio

State: Completed.

Amount : US\$ 168 M (CAF US\$ 86 M)

Legend

-  Road
-  Railway
-  Waterway
-  Gas Pipeline
-  Energy
-  Bridge Border
-  Center
-  Port

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

**System for the
Support of
Navigation across
the Orinoco River**

**Road: Nieuw Nickerie-
Paramaribo-Albina and
Bridge**

**Road: Venezuela-Guyana-
Suriname (I Stage)**

**Road: Boavista-
Georgetown (I Stage)**

Bridge over Itakutu River

GUIANA SHIELD HUB

Other Projects of the Portfolio

State: Execution.

Amount : US\$ 14.3 M (CAF US\$ 10 M)

Legend

-  Road
-  Railway
-  Waterway
-  Gas Pipeline
-  Energy
-  Bridge Border
-  Center
-  Port

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

**System for the Support of
Navigation across the Orinoco
River**

Road: Caracas - Manaus

**Road: Nieuw Nickerie-
Paramaribo-Albina and
Bridge**

**Road: Venezuela-Guyana-
Suriname (I Stage)**

**Road: Boavista-
Georgetown (I Stage)**

Bridge over Itakutu River

GUIANA SHIELD HUB

Total of Projects: 6

- AIC - 4
- Rest of the IIRSA Portfolio - 2

Legend

- Road
- Railway
- Waterway
- Gas Pipeline
- Energy
- Bridge Border
- ◆ Center
- ⚓ Port

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

INFORMATION AND COMMUNICATION TECHNOLOGIES


**AIC 30 -
Exports
through postal
delivery for
PyMES**

AIC - PROJECT UNDER SATISFACTORY PROGRESS

State: Under development. The organization that will coordinate the regional project (UPAEP) is established. CT under development for its pilot implementation in 4 countries.

Amount : US\$ 2.5 M (BID US\$ 1.5 M)

Completion planned: December 2009

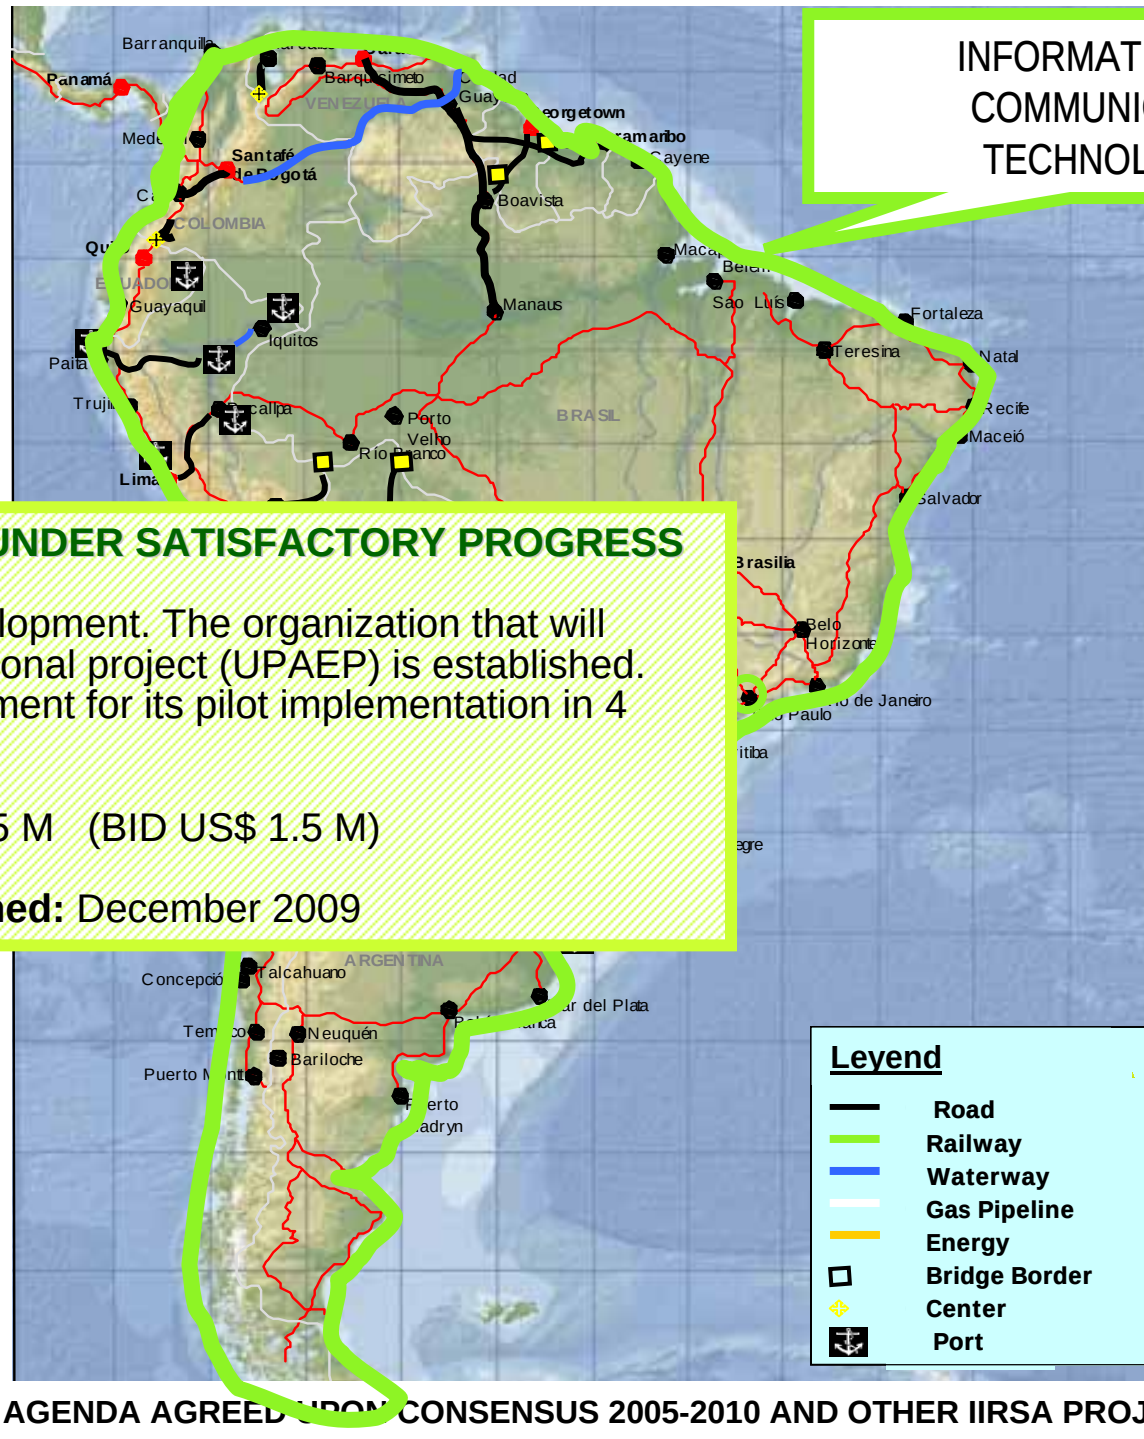

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

Exports through postal
delivery for PyMES

AIC 31 - South American Roaming

AIC - PROJECT WITH SOME DELAY

State: In order to encourage the project again, the team is developing a technical cooperation, which will be financed by the BID (US\$ 0.4 M), for the development of a regional study through which it will be possible to solve the main technical, administrative, legal and tax problems that currently hinder regional roaming. The study will allow to establish a new work plan for the project.

As a complement, a regional forum on South American roaming is being organized, which will be held by the end of 2007.

Completion planned: December 2010

INFORMATION AND COMMUNICATION TECHNOLOGIES

Legend


- Road
- Railway
- Waterway
- Gas Pipeline
- Energy
- Bridge Border
- ◆ Center
- ⚓ Port

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS

INFORMATION AND COMMUNICATION TECHNOLOGIES

Exports through postal
delivery for PyMES

AIC 31 - South American
Roaming

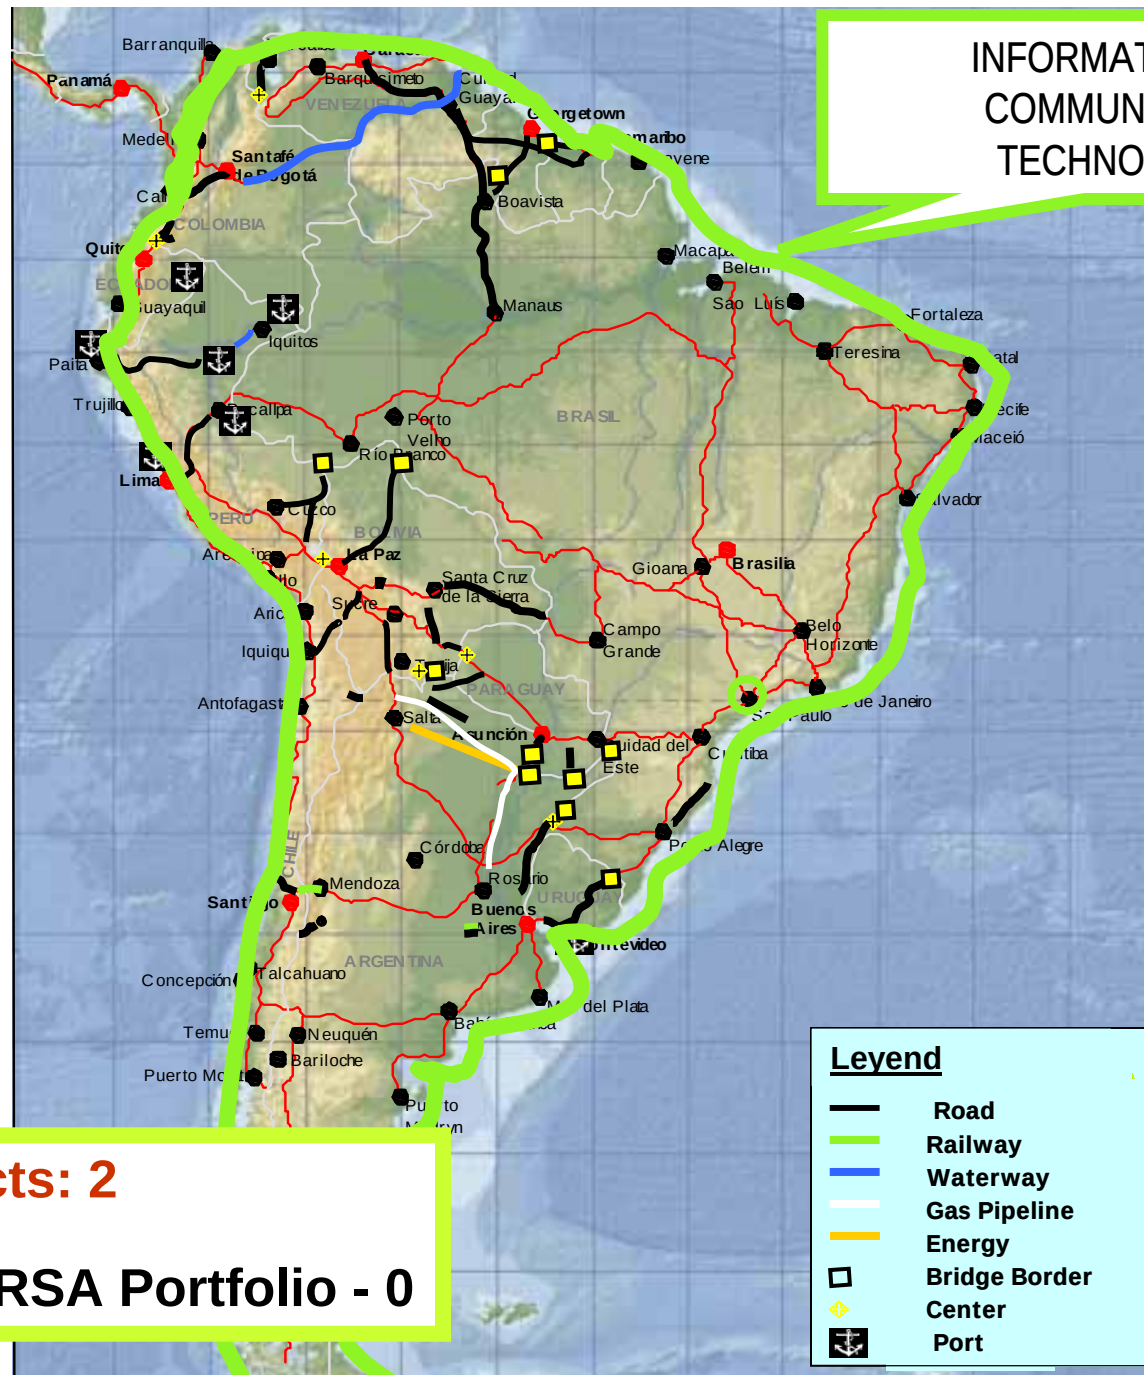

Total of Projects: 2

- AIC - 2
- Rest of the IIRSA Portfolio - 0

AGENDA AGREED UPON CONSENSUS 2005-2010 AND OTHER IIRSA PROJECTS




**State of the Projects that belong to the Agenda Agreed Upon
Consensus (Agenda de Implementación Consensuada – AIC - in
Spanish)
and the IIRSA Project Portfolio Estado de Avance
July, 2007**

Total Projects: 71 (US\$ 11,174 M)

- **AIC: 31 (US\$ 6, 939.6 M)**
- **Rest of the IIRSA Portfolio: 40 (US\$ 4,703 M)**

<i>Financing Source</i>	<i>US\$ Mill.</i>
<i>Public</i>	3,626
<i>PPP</i>	3,776
<i>Private</i>	597
<i>Multilateral</i>	3,644
<i>Total</i>	11,643

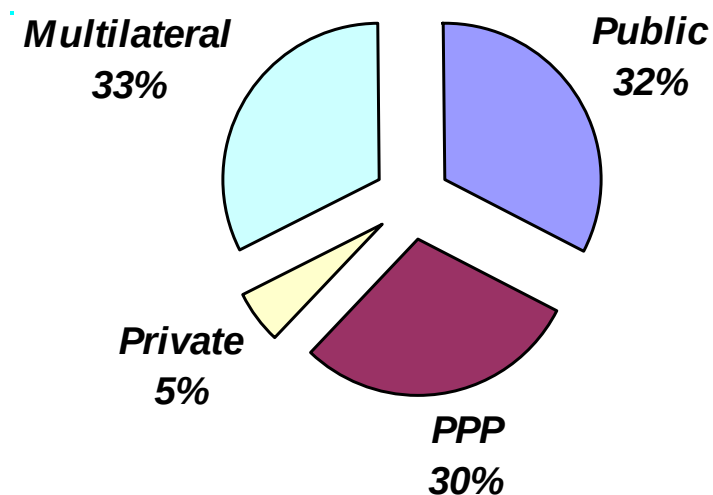



*State of the Projects that belong to the Agenda Agreed Upon Consensus (Agenda de Implementación Consensuada – AIC - in Spanish)
and the IIRSA Project Portfolio Estado de Avance*

Carlos Tamayo
Project Economist VPC/BID
carlostm@iadb.org

www.iirsa.org

Thanks



*X Reunión de Coordinadores Nacionales IIRSA
Montevideo, Julio del 2007*
